



Toll Bridge Seismic Retrofit and Regional Measure 1 Programs


Monthly Progress Report December 2006



TOLL BRIDGE PROGRAM
OVERSIGHT COMMITTEE

CALTRANS BAY AREA TOLL AUTHORITY CALIFORNIA TRANSPORTATION COMMISSION

Released: January 2007

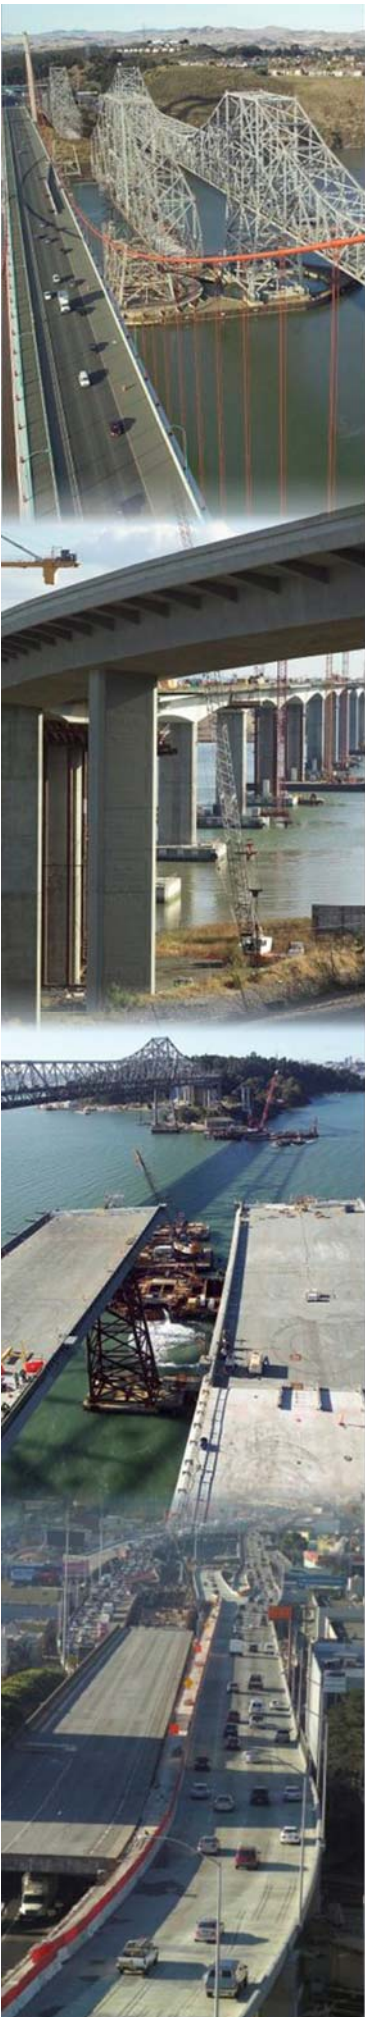

Toll Bridge Seismic Retrofit and Regional Measure 1 Programs

Monthly Progress Report
December 2006




TABLE OF CONTENTS

Introduction	1
Executive Summary	2
<i>Toll Bridge Seismic Retrofit Program—Cost</i>	<i>2</i>
<i>Toll Bridge Seismic Retrofit Program—Schedule</i>	<i>3</i>
<i>Regional Measure 1 Program—Cost</i>	<i>4</i>
<i>Regional Measure 1 Program—Schedule</i>	<i>5</i>
<i>Highlights of Project/Program Activities and TBPOC Actions</i>	<i>6</i>
Project / Contract Reports	7
<i>San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project Summary</i>	<i>8</i>
▶ Skyway Contract	10
▶ Self-Anchored Suspension (SAS) Superstructure Contract	14
▶ Self-Anchored Suspension (SAS) E2/T1 Foundations Contract	17
▶ Yerba Buena Island (YBI)	20
• YBI South/South Detour Contract	20
• YBI Transition Structure Contracts	22
▶ Oakland Touchdown	23
• Oakland Touchdown Submarine Cable Relocation Contract	23
• Oakland Touchdown #1 Contract	24
• Oakland Touchdown #2 Contract	25
▶ Other Major Contracts	26
▶ Other Completed Contracts and Related Work	28
<i>San Francisco-Oakland Bay Bridge (SFOBB) West Approach Replacement Project</i>	<i>29</i>
<i>Richmond-San Rafael Bridge (RSRB) Seismic Retrofit Project</i>	<i>32</i>
<i>Other Completed Seismic Retrofit Projects</i>	<i>34</i>
<i>Other Toll Bridges</i>	<i>35</i>
Project / Contract Reports	37
<i>New Benicia-Martinez Bridge Project Summary</i>	<i>38</i>
▶ New Benicia-Martinez Bridge Contract	42
▶ Other Contracts and Related Project Activities	44
<i>New Carquinez Bridge Project</i>	<i>46</i>
<i>Richmond-San Rafael Bridge (RSRB) Deck Overlay Project</i>	<i>49</i>
<i>Interstate 880/State Route 92 Interchange Reconstruction Project</i>	<i>51</i>
<i>Other Completed Regional Measure 1 (RM1) Projects</i>	<i>52</i>
Appendices	53
<i>Appendix A: San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project Cost Detail</i>	<i>54</i>
<i>Appendix B: Toll Bridge Seismic Retrofit Program Cost Detail</i>	<i>56</i>
<i>Appendix C: Toll Bridge Seismic Retrofit Program Summary Schedule</i>	<i>57</i>
<i>Appendix D: Regional Measure 1 Program Cost Detail</i>	<i>58</i>
<i>Appendix E: Regional Measure 1 Program Summary Schedule</i>	<i>61</i>
<i>Appendix F: Glossary of Terms</i>	<i>62</i>

Toll Bridges of the San Francisco Bay Area



* Under the Jurisdiction of the Golden Gate Bridge, Highway and Transportation District

INTRODUCTION

In July 2005, Assembly Bill 144, Hancock (AB 144) created the Toll Bridge Project Oversight Committee (TBPOC) to implement a project oversight and project control process for the Benicia-Martinez Bridge project and the state toll bridge seismic retrofit program projects. Comprised of the Caltrans Director, the Bay Area Toll Authority (BATA) Executive Director and the Executive Director of the California Transportation Commission (CTC), the TBPOC's project oversight and control processes include but are not limited to reviewing bid specifications and documents, providing field staff to review ongoing costs, reviewing and approving significant change orders and claims in excess of \$1 million (as defined by the committee) and preparing project reports.

AB 144 identified the Toll Bridge Seismic Retrofit Program and the new Benicia-Martinez Bridge Project as under the direct oversight of the TBPOC. The Toll Bridge Seismic Retrofit Program includes:

Toll Bridge Seismic Retrofit Projects	Seismic Safety Status
San Francisco-Oakland Bay Bridge East Span Replacement	Construction
San Francisco-Oakland Bay Bridge West Approach Replacement	Construction
San Francisco-Oakland Bay Bridge West Span Seismic Retrofit	Complete
San Mateo-Hayward Bridge Seismic Retrofit	Complete
Richmond-San Rafael Bridge Seismic Retrofit	Complete
Eastbound Carquinez Bridge Seismic Retrofit	Complete
Benicia-Martinez Bridge Seismic Retrofit	Complete
San Diego-Coronado Bridge Seismic Retrofit	Complete
Vincent Thomas Bridge Seismic Retrofit	Complete

The new Benicia-Martinez Bridge is part of a larger program of toll-funded projects, called the Regional Measure 1 (RM1) Toll Bridge Program, under the responsibility of the BATA. While the rest of the projects in the RM1 program are not directly under the responsibility of the TBPOC, BATA and Caltrans (CT) will continue to report on their progress as an informational item. The RM1 program includes:

RM1 Projects	Open to Traffic Status
New Benicia-Martinez Bridge	Construction
1927 Carquinez Bridge Demolition	Construction
Interstate 880/State Route 92 Interchange Reconstruction	Design
Richmond-San Rafael Bridge Deck Overlay Rehabilitation	Open
Richmond-San Rafael Bridge Trestle, Fender & Deck Joint Rehabilitation	Open
Westbound Carquinez Bridge Replacement	Open
San Mateo-Hayward Bridge Widening	Open
State Route 84 Bayfront Expressway Widening	Open
Richmond Parkway	Open

This report focuses on identifying critical project issues and monitoring project cost and schedule performance for the projects as measured against approved budgets and schedule milestones. This report is intended to fulfill Caltrans' requirement to provide monthly project progress reporting to the TBPOC under Section 30952.05 of the Streets and Highway Code.

EXECUTIVE SUMMARY

Toll Bridge Seismic Retrofit Program—Cost (\$Millions)

Project	Work Status	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast*	At- Completion Variance	Cost Status
a	b	c	d	e = c + d	f	g	h = g - e	i
SFOBB East Span Replacement Project								
Capital Outlay Support		959.4	-	959.4	461.9	977.1	17.7	●
Capital Outlay Construction								
Skyway	Construction	1,293.0	-	1,293.0	1,107.5	1,293.0	-	●
SAS E2/T1 Foundations	Construction	313.5	-	313.5	187.2	313.5	-	●
SAS Superstructure	Construction	1,753.7	-	1,753.7	211.2	1,767.4	13.7	●
YBI South/South Detour	Design/Const	131.9	-	131.9	36.6	152.2	20.3	●
YBI Transition Structures	Design	299.3	-	299.3	-	318.5	19.2	●
Oakland Touchdown (OTD)		283.8	-	283.8	-	302.5	18.7	
* OTD Submarine Cable	Advertise				-	9.6	-	●
* OTD No. 1 (Westbound)	Design				-	226.5	-	●
* OTD No. 2 (Eastbound)	Design				-	62.0	-	●
* OTD Electrical Systems	Design				-	4.4	-	●
Existing Bridge Demolition	Design	239.2	-	239.2	-	222.0	(17.2)	●
Stormwater Treatment Measures	Construction	15.0	-	15.0	4.4	15.0	-	●
East Span Completed Projects		90.3	-	90.3	88.6	90.3	-	
Right-of-Way and Environmental Mitigation		72.4	-	72.4	38.8	72.4	-	●
Other Budgeted Capital		35.1	-	35.1	0.6	11.0	(24.1)	
Total SFOBB East Span Replacement Project		5,486.6	-	5,486.6	2,136.8	5,534.9	48.3	
SFOBB West Approach Replacement	Construction							●
Capital Outlay Support		120.0	-	120.0	86.0	120.0	-	
Capital Outlay Construction		309.0	-	309.0	218.8	309.0	-	
Total SFOBB West Approach Replacement		429.0	-	429.0	304.8	429.0	-	
Richmond-San Rafael Bridge Retrofit	Construction							●
Capital Outlay Support		134.0	(7.0)	127.0	125.6	127.0	-	
Capital Outlay Construction & Right-of-Way		780.0	(82.0)	698.0	665.6	698.0	-	
Total Richmond-San Rafael Bridge Retrofit		914.0	(89.0)	825.0	791.2	825.0	-	
Program Completed Projects	Complete							
Capital Outlay Support		219.8	-	219.8	219.4	219.8	-	
Capital Outlay Construction		705.6	-	705.6	698.0	705.6	-	
Total Program Completed Projects		925.4	-	925.4	917.4	925.4	-	
Miscellaneous Program Costs		30.0	-	30.0	24.5	30.0	-	
Program Contingency		900.0	89.0	989.0	-	940.7	(48.3)	
Total Toll Bridge Seismic Retrofit Program		8,685.0	-	8,685.0	4,174.7	8,685.0	-	

● Within Approved Current Schedule and Budget

● Potential Cost and Schedule Impacts: Possible future need for Program Contingency Allocation

● Known Cost and Schedule Impacts: Request for Program Contingency Allocation forthcoming

Note: Details may not sum to totals due to rounding effects.

* Cost forecasts are as of August 31, 2006. Forecasts for the Monthly Reports are generally updated on a quarterly basis in conjunction with Risk Analysis assessments for the TBSRP Projects and the TBSRP Quarterly Reports.

Toll Bridge Seismic Retrofit Program—Schedule

Project	AB 144 / SB 66 Project Complete Baseline (07/2005)	Approved Changes (Months)	Project Complete Current Approved Schedule (11/2006)	Project Complete Schedule Forecast (11/2006)	Schedule Variance (Months)	Schedule Status	Remarks
a	b	c	d = b + c	e	f = e - d	g	h
SFOBB East Span Replacement Project Skyway	Apr 07	8	Dec 07	Dec 07	-	●	A schedule extension due to hinge pipe beam fabrication, service platforms electrical appurtenances, polyester concrete, etc., has been approved by the TBPOC. See page 10.
SAS E2/T1 Foundations	Jun 08	(3)	Mar 08	Mar 08	-	●	
SAS Superstructure	Mar 12	12	Mar 13	Mar 13	-	●	Contract executed on May 3, 2006. See Note.
YBI South/South Detour	Jul 07	-	Jul 07	TBD	TBD	●	Schedule is being assessed. Forecast completion date is TBD. See page 20.
YBI Transition Structures	Nov 13	12	Nov 14	Nov 14	-	●	In March 2006, the TBPOC approved the split of the YBI contract into three contracts. Schedules and estimates for the split contracts are being developed
Oakland Touchdown (OTD)	Nov 13	12	Nov 14	Nov 14	-	●	
• OTD Submarine Cable	n/a		Jul 07	Oct 07	3	●	Award of contract is expected on January 9, 2007. See pages 9 and 23.
• OTD Westbound	n/a		Jul 09	Oct 09	3	●	Advertise date postponed to provide additional time for utility coordination and contract formation.
• OTD Eastbound	n/a		Nov 14	Nov 14	-	●	See Note.
Existing Bridge Demolition	Sep 14	12	Sep 15	Sep 15	-	●	See Note.
Stormwater Treatment Measures	Mar 08	-	Mar 08	Jun 07	(9)	●	Forecast based on actual award date and duration in contractor's A+B bid.
Open to Traffic Date: Westbound	Sep 11	12	Sep 12	Sep 12	-	●	See Note.
Open to Traffic Date: Eastbound	Sep 12	12	Sep 13	Sep 13	-	●	See Note.
SFOBB West Approach Replacement	Aug 09	-	Aug 09	Aug 09	-	●	
Richmond-San Rafael Bridge							
• Seismic Retrofit	Aug 05	-	Aug 05	Oct 05	2	●	Seismic retrofit completed July 29, 2005. Formal acceptance of contract October 28, 2005. \$89 million has been transferred to Program Contingency. See page 32.
• Public Access Project	n/a	-	May 07	May 07	-	●	Bids opened December 1, 2006.

Note: Schedules for selected projects and the Open to Traffic dates were extended by 12 months from the AB144/SB66 baseline schedule due to Addenda #5 and #7 on the SAS Superstructure contract.

Regional Measure 1 Program—Cost (\$Millions)

Project	Work Status	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast*	At- Completion Variance	Cost Status
a	b	c	d	e = c + d	f	g	h = g - e	i
New Benicia-Martinez Bridge Project	Construction							●
Capital Outlay Support		157.1	24.8	181.8	160.7	181.8	-	
Capital Outlay Construction		861.6	143.1	1,004.7	887.4	1,004.7	-	
Capital Outlay Right-of-Way		20.4	(0.1)	20.3	12.3	20.3	-	
Project Reserve		20.8	35.3	56.2	-	56.2	-	
Total New Benicia-Martinez Bridge Project		1,059.9	203.1	1,263.0	1,060.4	1,263.0	-	
Carquinez Bridge Replacement Project	Construction							●
Capital Outlay Support		124.4	(1.1)	123.3	117.6	123.2	(0.1)	
Capital Outlay Construction		381.2	3.3	384.5	365.8	384.3	(0.2)	
Capital Outlay Right-of-Way		10.5	-	10.5	9.9	10.5	-	
Project Reserve		12.1	(2.2)	9.9	-	10.2	0.3	
Total Carquinez Bridge Replacement Project		528.2	-	528.2	493.3	528.2	-	
Richmond-San Rafael Bridge Deck Overlay Rehabilitation	Complete							●
Capital Outlay Support		8.0	(3.5)	4.5	2.9	4.5	-	
Capital Outlay Construction		16.9	3.6	20.5	14.4	20.5	-	
Project Reserve		0.1	(0.1)	-	-	-	-	
Total Richmond-San Rafael Bridge Deck Overlay Rehabilitation		25.0	-	25.0	17.3	25.0	-	
I-880/SR-92 Interchange Reconstruction	Design							●
Capital Outlay Support		28.8	-	28.8	30.3	51.7	22.9	
Capital Outlay Construction		94.8	-	94.8	-	122.5	27.7	
Capital Outlay Right-of-Way		9.9	-	9.9	8.1	12.4	2.5	
Project Reserve		0.3	-	0.3	-	9.7	9.4	
Total I-880/SR-92 Interchange Reconstruction		133.8	-	133.8	38.4	196.3	62.5	
Program Completed Projects	Complete							
Capital Outlay Support		54.0	(0.5)	53.5	54.0	55.4	1.9	
Capital Outlay Construction		307.5	(1.1)	306.4	274.8	296.8	(9.6)	
Capital Outlay Right-of-Way		1.7	-	1.7	0.5	0.8	(0.9)	
Project Reserve		2.5	1.6	4.1	-	1.8	(2.3)	
Total Program Completed Projects		365.7	-	365.7	329.3	354.8	(10.9)	
Total Regional Measure 1 Program		2,112.6	203.1	2,315.7	1,938.7	2,367.3	51.6	

● Within Approved Current Schedule and Budget

● Potential Cost and Schedule Impacts: Possible future need for Program Contingency Allocation

● Known Cost and Schedule Impacts: Request for Program Contingency Allocation forthcoming

Note: Details may not sum to totals due to rounding effects.

* Cost forecasts are as of August 31, 2006. Forecasts for the Monthly Reports are generally updated on a quarterly basis in conjunction with Risk Analysis assessments for the TBSRP Projects and the TBSRP Quarterly Reports.

Regional Measure 1 Program—Schedule

Project	BATA Project Complete Baseline (07/2005)	Approved Changes (Months)	Project Complete Current Approved Schedule (11/2006)	Project Complete Schedule Forecast (11/2006)	Schedule Variance (Months)	Schedule Status	Remarks
a	b	c	d= b + c	e	f= e - d	g	h
New Benicia-Martinez Bridge Project							
• New Benicia-Martinez Bridge	Dec 07	-	Dec 07	Dec 07	-	●	
• I-680/I-780 Interchange Replacement	Dec 07	-	Dec 07	Feb 08	2	●	Final electrical work to be completed after Bridge Open to Traffic. Structure was substantially completed as of December 1, 2006. See page 45.
• Open to Traffic Date	Dec 07	-	Dec 07	Dec 07	-	●	
1927 Carquinez Bridge Demolition Project	Dec 07	-	Dec 07	Dec 07	-	●	
Richmond-San Rafael Bridge Deck Overlay Rehabilitation	Jan 07	-	Jan 07	Jan 07	-	●	
I-880/SR-92 Interchange Reconstruction	Nov 10	-	Nov 10	Jun 11	7	●	Delay in the procurement of right-of-way is impacting the cost/schedule for this project. See page 51.

Highlights of Project/Program Activities and TBPOC Actions for December 2006

Toll Bridge Seismic Retrofit Program

SFOBB East Span Seismic Replacement Project

- ◆ For the Skyway Contract, the last remaining precast segments on the westbound structure were shipped from the Stockton fabrication facility of December 5th and installed on December 7, 2006. (See Page 10).
- ◆ In November 2006, Caltrans rebid the San Francisco-Oakland Bay Bridge East Span Replacement Project Submarine Cable Relocation Contract. The rebid included two separate bids: one for a one-cable project and one for a two-cable project. On Monday, December 18, 2006, Caltrans opened five proposals each for the 1-cable and 2-cable relocation contracts. Caltrans rejected two of the submittals because they were incomplete. Manson Construction submitted the apparent low bid for the two-cable project (\$9.7 million) and for the one-cable project (\$7.0 million). Based on the recommendations of the TBPOC, on December 20th 2006, BATA supported Caltrans awarding a two-cable project, subject to the City of San Francisco providing required additional non-toll funding and upon Caltrans' review of the bids for responsiveness and allocated an additional \$600,000 in SRP funds to allow, if necessary, for the award to either the 2nd or 3rd lowest bidders on either the 2-cable or 1-cable contracts in the event that the contract could not be awarded to the lowest bidder to ensure that there are no further delays, related to the award of the cable project. Caltrans is expected to award the contract by January 9, 2007. (See pages 9 and 23).
- ◆ Drilling for rock sockets has started on the T1 foundation for the SAS E2/T1 Foundations contract. The steel footing frame for the Pier E2 has been placed and stabbing of the cofferdam sheet piling is complete.

Richmond-San Rafael Bridge Seismic Retrofit Project

- ◆ The Richmond-San Rafael Public Access Project to construct a public access lot to comply with a Bay Conservation and Development Commission (BCDC) permit condition conducted a bid opening on December 1, 2006. Seven bids were submitted with Ghilloti Bros. Inc., submitting the apparent lowest A+B bid of \$1,005,863.40 as compared to the Engineer's Estimate of \$1,072,157.25. (See page 32).


Regional Measure 1 Program

New Benicia-Martinez Bridge Projects

- ◆ As of the end of November 2006, all 344 segments of Frames 2 and 3 of the new Benicia-Martinez bridge has been completed. Six (6) of the nine (9) concrete closure pours, which links the individual piers together into a frame have been completed. (See page 42).

Richmond-San Rafael Bridge Deck Overlay Project

- ◆ As of December 1, 2006, all construction work for the RSRB Deck Rehabilitation contract has been accepted. (See page 48).

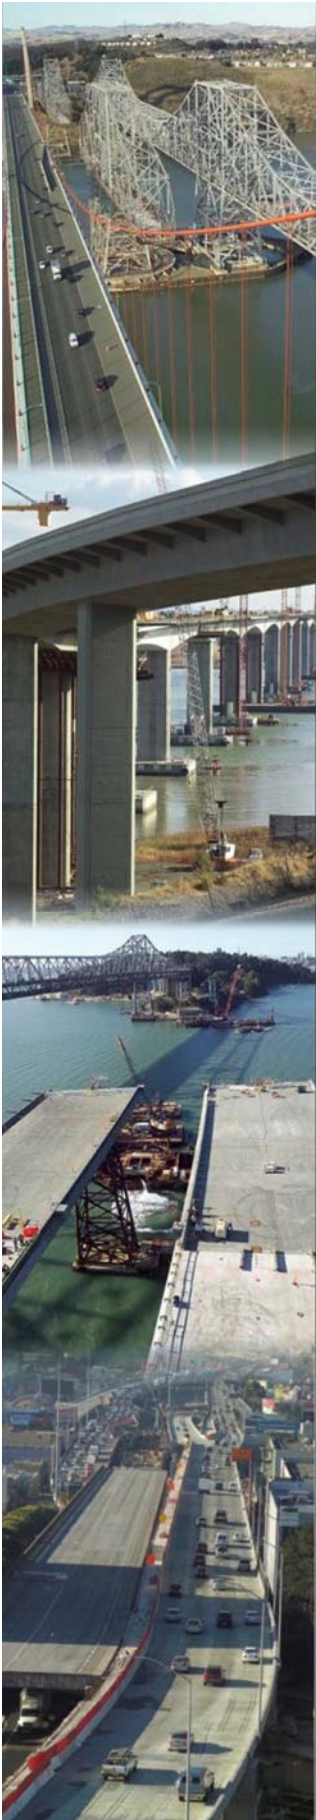

PROJECT / CONTRACT REPORTS

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project Summary

- Skyway Contract
- Self-Anchored Suspension (SAS) Superstructure Contract
- Self-Anchored Suspension (SAS) E2/T1 Foundations Contract
- Yerba Buena Island (YBI)
 - * Yerba Buena Island (YBI) South/South Detour Contract
 - * Yerba Buena Island (YBI) Transition Structure Contracts
- Oakland Touchdown (OTD)
 - * Oakland Touchdown (OTD) Submarine Cable Relocation Contract
 - * Oakland Touchdown (OTD) #1 Contract
 - * Oakland Touchdown (OTD) #2 Contract
- Other Major Contracts
- Other Contracts and Related Project Work

San Francisco-Oakland Bay Bridge (SFOBB) West Approach Replacement Project

Richmond-San Rafael Bridge Seismic Retrofit Project

Other Completed Seismic Retrofit Projects

Toll Bridge Seismic Retrofit Program


San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project Summary

Project Description: The East Span will be seismically retrofitted through the complete replacement of the existing span. The remaining effort for this project consists of the following contracts: Skyway—construction of two parallel concrete structures, each approximately 1.3 miles in length; Self-Anchored Suspension (SAS) Foundation—construction of SAS marine foundations; SAS Superstructure—construction of a self-anchored 385-meter main span superstructure incorporating a 160-meter fabricated structural steel tower with a main cable and inclined suspenders that will support steel orthotropic decks; Yerba Buena Island (YBI) South/South Detour—design and construction of a temporary double-deck bypass structure that will detour traffic to the existing SFOBB while completing the westerly permanent tie-in structure of the new East Span at Yerba Buena Island; YBI Structures—construction of a new structure connecting the western end of the self-anchored suspension to the Yerba Buena Island viaduct, which will be retrofitted; Oakland Touchdown—at the Oakland end of the East Span, construction of two parallel, cast-in-place post-tensioned concrete viaducts, which join the skyway to the at-grade Oakland approach fill; and Existing Bridge Demolition—demolition of the existing 1936 SFOBB East Span structure after the construction and placement of traffic onto the new East Span.

SFOBB East Span Replacement Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
Capital Outlay Support	959.4	-	959.4	461.9	977.1	17.7
Capital Outlay				-	-	-
Skyway	1,293.0	-	1,293.0	1,107.5	1,293.0	-
SAS Superstructure	1,753.7	-	1,753.7	187.2	1,767.4	13.7
SAS E2/T1 Foundations	313.5	-	313.5	211.2	313.5	-
YBI Structures	299.3	-	299.3	36.6	318.5	19.2
Oakland Touchdown (OTD)	283.8	-	283.8	-	302.5	18.7
* OTD Submarine Cable				-	9.6	
* OTD No. 1 (Westbound)				-	226.5	
* OTD No. 2 (Eastbound)				-	62.0	
* OTD Electrical Systems				-	4.4	
YBI South/South Detour	131.9	-	131.9	-	152.2	20.3
Existing Bridge Demolition	239.2	-	239.2	-	222.0	(17.2)
Stormwater Treatment Measures	15.0	-	15.0	4.4	15.0	-
East Span Completed Projects	90.3	-	90.3	88.6	90.3	-
Right-of-Way and Environmental Mitigation	72.4	-	72.4	38.8	72.4	-
Other Budgeted Capital	35.1	-	35.1	0.6	11.0	(24.1)
TOTAL	5,486.6	-	5,486.6	2,136.8	5,534.9	48.3

Note: Details may not sum to totals due to rounding effects.



SFOBB East Span Replacement Project

SFOBB East Span Replacement Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
Skyway	April 2007	8	December 2007	December 2007	-
YBI South / South Detour*	July 2007	-	July 2007	TBD	TBD
Stormwater Treatment Measures	March 2008	-	March 2008	June 2007	(9)
SAS E2/T1 Foundations	June 2008	(3)	March 2008	March 2008	-
Open to Traffic: Westbound	September 2011	12	September 2012	September 2012	-
SAS Superstructure	March 2012	12	March 2013	March 2013	-
Open to Traffic: Eastbound	September 2012	12	September 2013	September 2013	-
Oakland Touchdown (OTD)	December 2013	12	December 2014	December 2014	-
* OTD Submarine Cable	n/a		July 2007	October 2007	3
* OTD No. 1 (Westbound)	n/a		July 2009	October 2009	3
* OTD No. 2 (Eastbound)	n/a		December 2014	December 2014	-
YBI Transition Structure*	December 2013	12	December 2014	December 2014	-
Existing Bridge Demolition*	September 2014	12	September 2015	September 2015	-

* Contract schedules being further assessed due to changes in SAS schedule.

Project Status: Construction is currently ongoing on the Skyway, YBI South/South Detour, SAS E2/T1 Foundations and Stormwater Treatment Measures contracts. Contracts in design include the OTD #1 (westbound), OTD #2 (eastbound), the YBI Transition Structure (YBITS) Contract #1, YBITS Contract #2, and Existing Bridge Demolition contract. Design of each contract is proceeding per its schedule requirements. On December 18, 2006, Caltrans opened bids for the Submarine Cable Relocation contract. Caltrans is expected to award the contract by January 9, 2007.

Project Issues: All projects except Demolition have a Risk Response Team and a Risk Register incorporating quantitative risk analyses. A preliminary risk register has also been developed for Capital Outlay Support (COS) costs, as well as program-level risk register that captures risks common to all projects; the development of a quantitative COS risk analysis is in progress. The Risk Response Teams have focused attention on developing and executing risk response actions for their most significant risks. Many of the actions have been effective, as evidenced by a reduction of risk impacts on the Skyway and E2/T1 contracts from the previous quarter. The effort to develop and execute risk response actions to mitigate the cost and schedule impacts posed by risk issues will continue to be a high priority.

Recent TBPOC Actions: See the following contract detail pages for specific TBPOC actions on East Span contracts.

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► SKYWAY CONTRACT

Contract Description: The Skyway contract constructs two parallel pre-cast concrete approach spans from Oakland to the self-anchored suspension span near Yerba Buena Island.

Skyway Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
East Span - Skyway						
Capital Outlay Support	197.0	-	197.0	152.1	197.0	-
Capital Outlay Construction	1,293.0	-	1,293.0	1,107.5	1,293.0	-
TOTAL	1,490.0	-	1,490.0	1,259.6	1,490.0	-

Note: Details may not sum to totals due to rounding effects.

Skyway Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
East Span - Skyway	April 2007	8	December 2007	December 2007	-

Contract Status: The Skyway contract is currently in construction and is 94% complete as of November 20, 2006. The foundation work is complete including the installation of the fenders around six of the pier footings. The eastbound and westbound structures are 100% complete with the erection of all segments. The last remaining segments on the westbound structure were erected on December 7, 2006. Bike path cantilever beam installation is complete and the installation of the panel segments is currently 84% complete.

Contract Issues:

Issue	Mitigating Action
KFM issued 15 NOPC's on behalf of USI for welding issues related to the fabrication of the Steel Orthotropic Box Girders (SOBG).	USI completed the fabrication of the SOBG. All NOPC's filed were recommended to be heard by the Dispute Review Board.

Recent TBPOC Actions: none.

Contract Photographs


Closure Pour




Hinge Pipe Beam BW Lifted from the Barge



HPG lift panoramic view

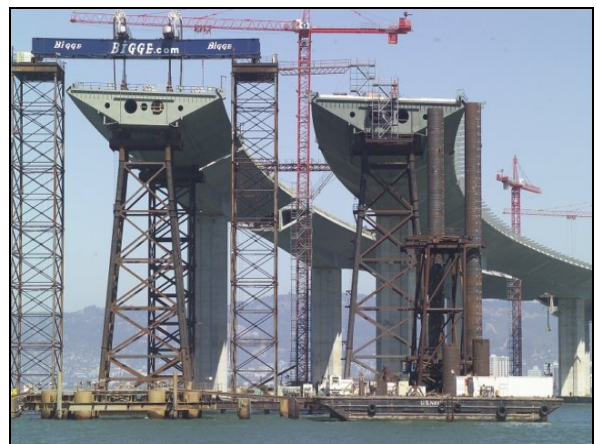Contract Photographs Cont'd.*Inserting HPB BW into the Bridge**Installation of Bike Path Panel Segments**Installing HPB BW**Lifting HPB BW**Placing HPB BW into the Bridge**West end of the Skyway*

San Francisco-Oakland Bay Bridge East Span Replacement Project - Skyway Contract December 2006

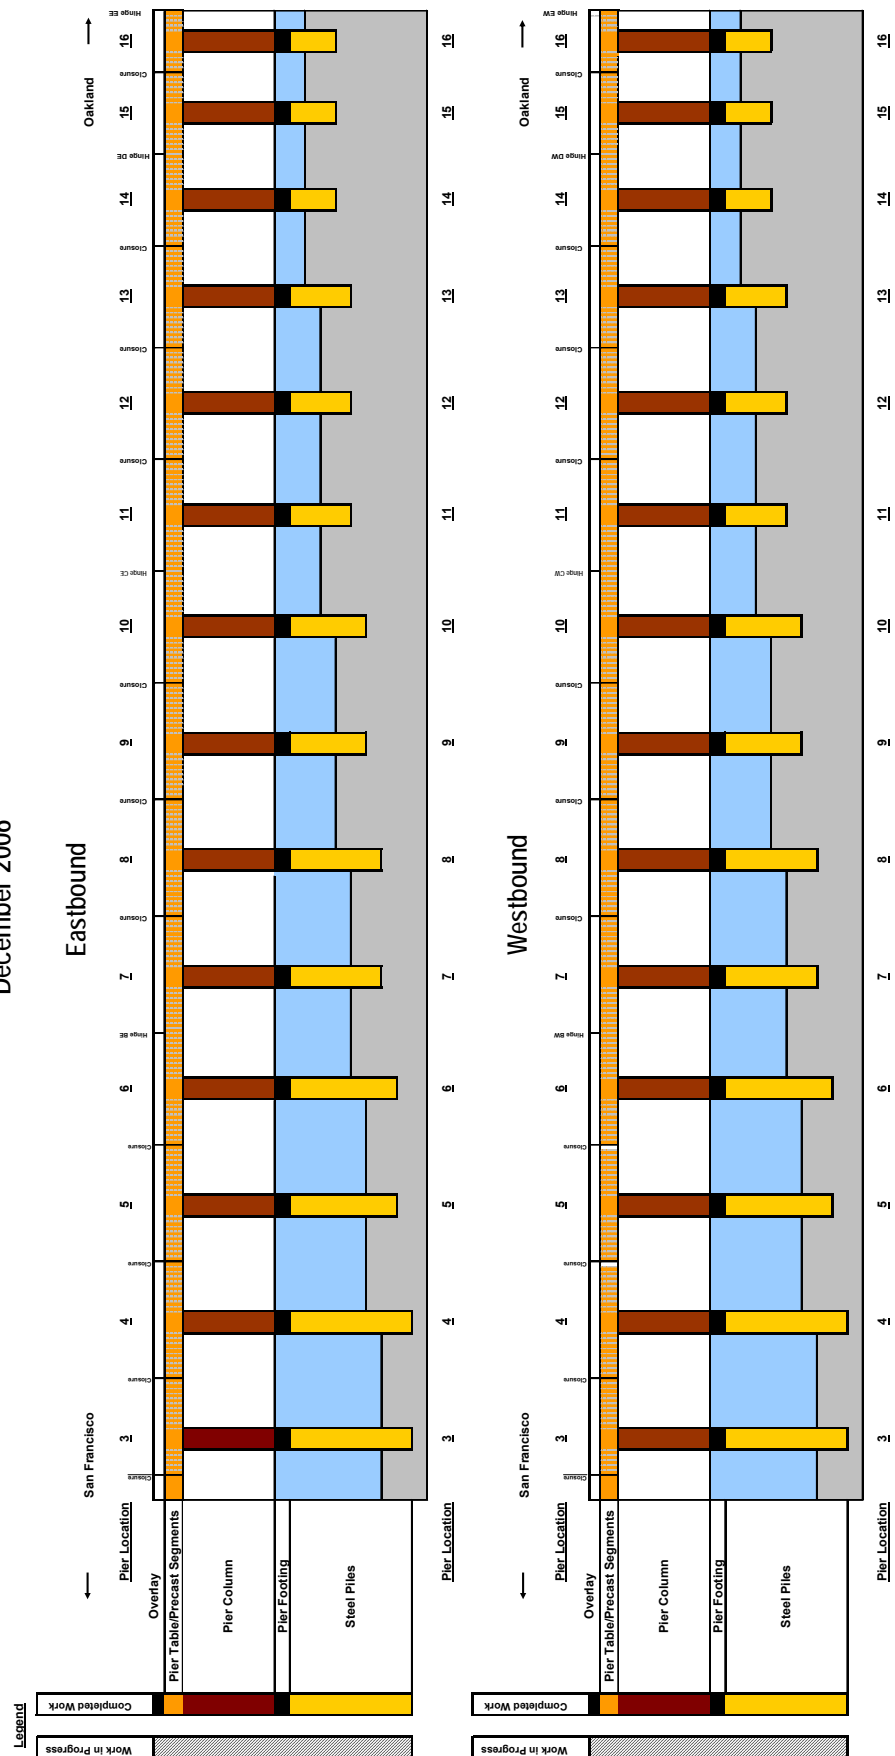

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► SELF-ANCHORED SUSPENSION (SAS) SUPERSTRUCTURE CONTRACT

Contract Description: The Self-Anchored Suspension (SAS) Superstructure contract constructs a signature tower span between the skyway and the Yerba Buena Island transition structure. Work on the SAS bridge has been split between three contracts—the SAS Superstructure (under construction), the SAS E2/T1 Foundation (under construction), and the SAS W2 Foundation (completed).

SAS Superstructure Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
East Span - SAS Superstructure						
Capital Outlay Support	214.6	-	214.6	26.8	214.6	-
Capital Outlay Construction	1,753.7	-	1,753.7	211.2	1,767.4	13.7
TOTAL	1,968.3	-	1,968.3	238.0	1,982.0	13.7

Note: Details may not sum to totals due to rounding effects.

SAS Superstructure Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
East Span - SAS Superstructure	March 2012	12	March 2013	March 2013	-

Contract Status: The contract is 10% complete as of November 20, 2006. The Contractor, American Bridge Fluor Enterprises, Inc., a Joint Venture (ABF), continues to mobilize staff to the field office on Pier 7, prepare various administrative submittals, and finalize agreements with manufacturers, fabricators, suppliers and subcontractors. Pre-fabrication welding procedures and approval processes are being developed at Zhenhua Port Machinery Company (ZPMC) of Shanghai, China for fabrication of the SAS superstructure tower and decks.

The forecast \$13.7 million increase in construction costs on the SAS contract from the approved budget reflects actions taken to encourage additional bidders for the contract.


Contract Issues:

Issue	Mitigating Action
Caltrans has identified the need for added resources to monitor work at the ZPMC steel fabrication facilities in China.	Caltrans and BATA are working together to set up facilities and to organize resources that will ensure an effective Owner's presence in the steel fabrication shops.
Potential for cost increases during construction due to steel plate conflicts. Applies to structural steel including the towers and box girders.	Establish Working Drawing Campus with Contractor to facilitate discussion about conflicts and meet regularly. Caltrans has constructed models and has identified conflicts, for which CCOs are to be prepared. Number of required mockups in the contract was reduced by addendum due to concerns about time for construction. Could continue to look at potential for mockups. Facilitated Cost Reduction Incentive Proposal (CRIP) sessions to discuss more changes and improvements at the beginning of the contract.

Recent TBPOC Actions: None.



Contract Photographs

SAS Superstructure Artist Rendition

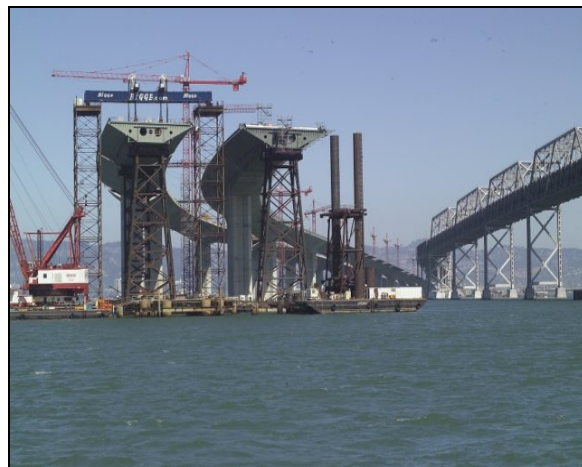

View of the Western End of the Skyway Contract that will connect with the Future SAS Contract.

SAS Superstructure Construction Progress

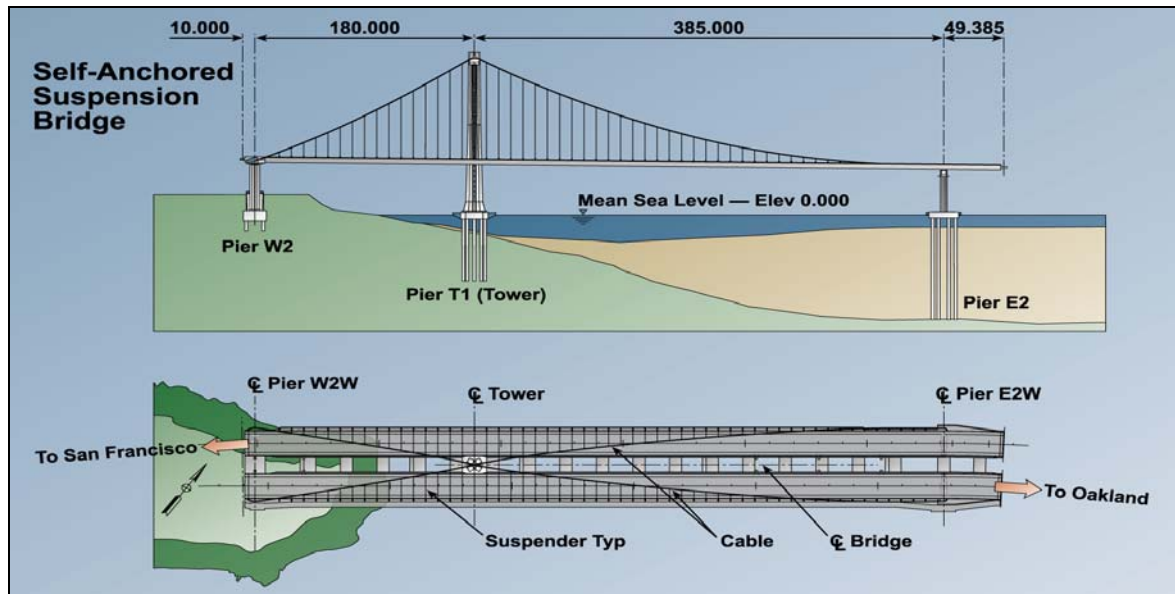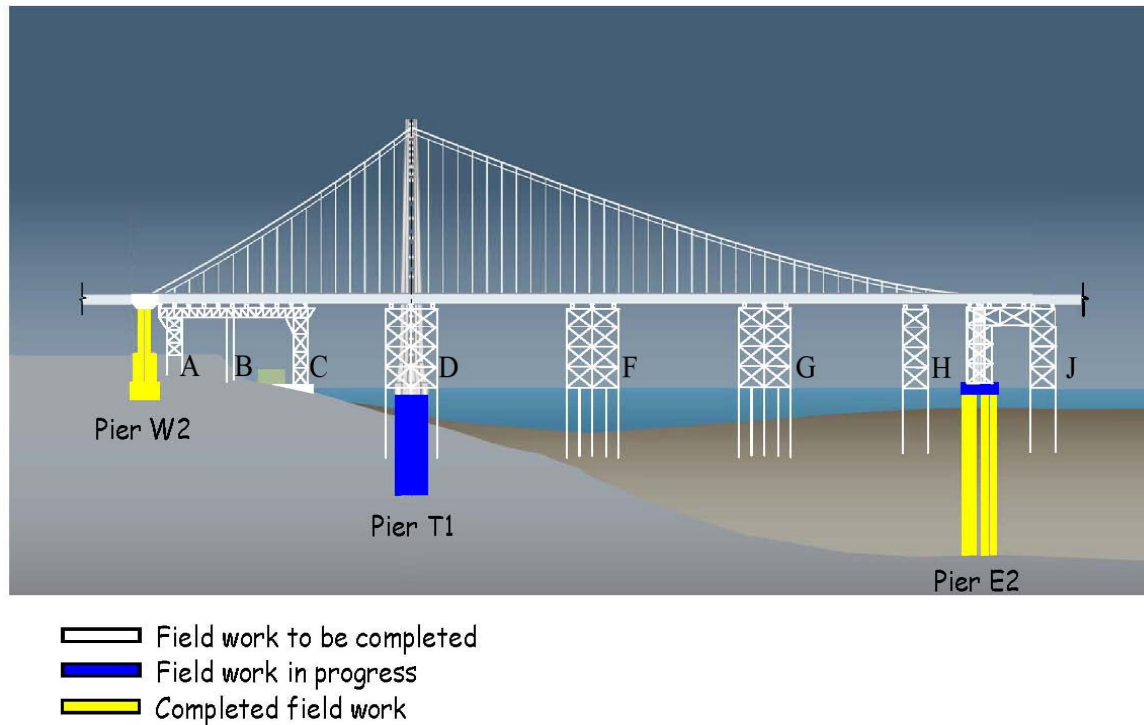

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► SELF-ANCHORED SUSPENSION (SAS) E2/T1 FOUNDATIONS CONTRACT

Contract Description: The Self-Anchored Suspension (SAS) E2/T1 Foundations contract constructs the main tower foundation at T1 and the adjacent east foundation at E2.

SAS E2/T1 Foundations Cost Summary (\$ Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
East Span - SAS E2 / T1 Foundations						
Capital Outlay Support	52.5	-	52.5	16.3	52.5	-
Capital Outlay Construction	313.5	-	313.5	187.2	313.5	-
TOTAL	366.0	-	366.0	203.5	366.0	-

Note: Details may not sum to totals due to rounding effects.

SAS E2/T1 Foundations Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
East Span - SAS E2 / T1 Foundations	June 2008	(3)	March 2008	March 2008	-


Contract Status: E2 pile driving has been completed. Installation of the steel footing frame for Pier E2 is underway. As of December 22, 2006, 6 of 13 of the rock sockets for the T1 foundation off of YBI have been completed (See contract issues below).

Contract Issues:

Issue	Mitigating Action
Rock sockets have historically been problematic during construction. A differing site condition for the T1 rock sockets could increase costs.	Contractor has similar experience with rock sockets from the new Benicia-Martinez Bridge Project and has contingent equipment on site if problems arise. As of December 2006, 6 of 13 rock sockets have been completed. Furthermore, having E2/T1 footings as a separate contract is a risk mitigation measure for the SAS contract.

Recent TBPOC Actions: None.


Project Photographs

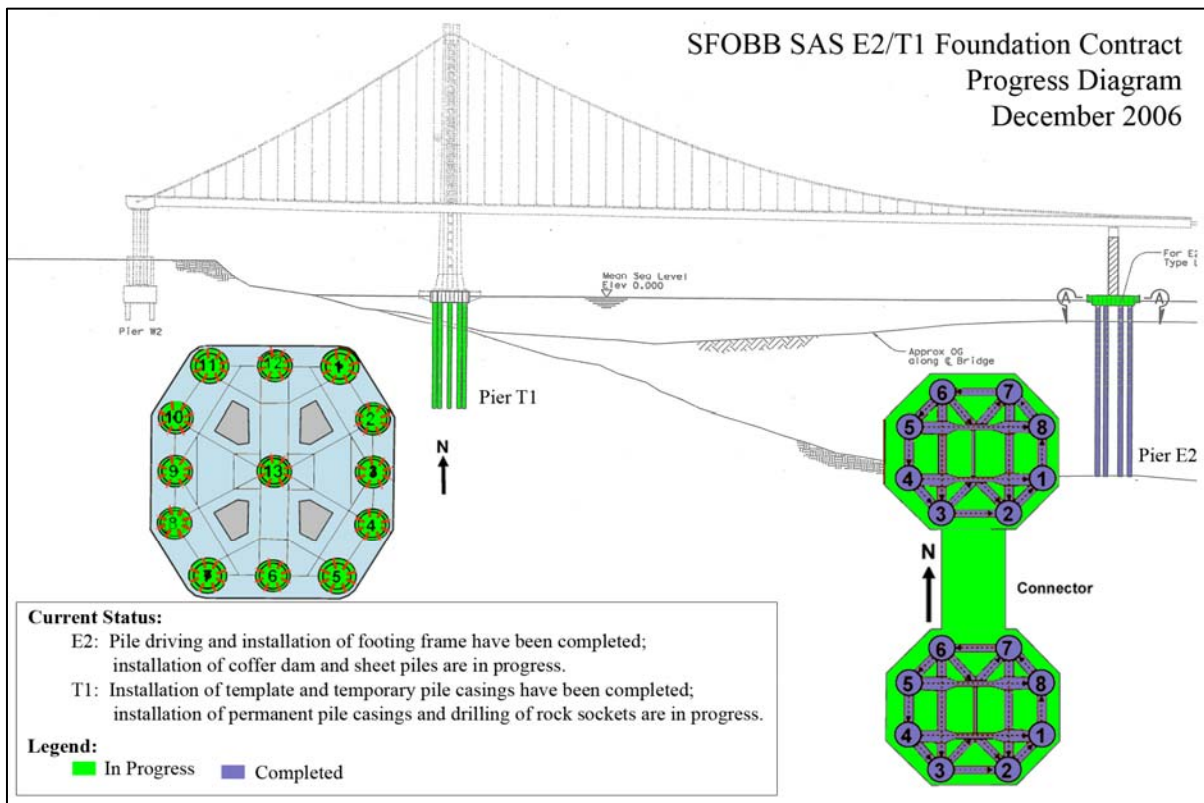

KFM Crew is Getting Ready for Concrete Placement of Pile #4 at T1



Placing Concrete in Pile # 4 at T1

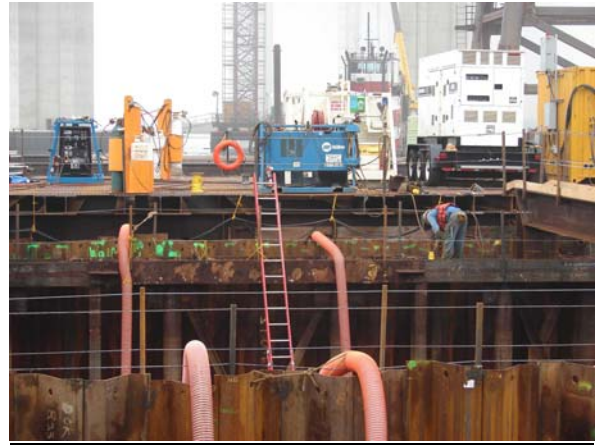Project Photographs cont'd.*Pumping System at E2**Pumping Water out of Cofferdam at E2**Rock Socket Drilling in Pile # 12 at T1**Rock Socket Drilling in Pile # 4 at T1**Sheet piling Cofferdam at E2**Spud Piles for Cofferdam Access Platforms at E2*

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► YERBA BUENA ISLAND (YBI)

• SOUTH/SOUTH DETOUR CONTRACT

Contract Description: The Yerba Buena Island (YBI) South/South Detour (SSD) Contract constructs a temporary detour from the YBI tunnel to the existing east span of the Bay Bridge. This detour maintains traffic on the existing bridge while the YBI Transition Structure Contract completes the tie-in from the SAS to the existing tunnel.

YBI South/South Detour Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
YBI South/South Detour						
Capital Outlay Support	29.5	-	29.5	17.5	29.5	-
Capital Outlay Construction	131.9	-	131.9	36.6	152.2	20.3
TOTAL	161.4	-	161.4	54.1	181.7	20.3

Note: Details may not sum to totals due to rounding effects.

YBI South/South Detour Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
YBI South / South Detour *	July 2007	-	July 2007	TBD	TBD

* Contract schedule under assessment. See Contract Issues below.

Contract Status: Construction of the SSD is underway and is currently about 40% complete. Caltrans is currently designing the East and West Tie-ins that will connect the SSD structure to the existing bridge and to the YBI tunnel. The current corridor schedule for completion of the SAS has necessitated additional design enhancements to the SSD viaduct segment to allow it to stand in place alone for a longer duration than originally intended. As a result, the schedule for the SSD work is being re-evaluated (See contract issues below).

A cost variance from the Current Approved Budget of \$20.3 million is forecast for the SSD contract due to the extension of the SSD contract schedule to integrate it with the current SAS contract schedule and the cost impact of the redesign of east and west tie-in structures and viaduct. Caltrans is also exploring the accelerating construction work on the island by adding portions of the YBI transition structure work into the SSD contract to mitigate project schedule risk. The additional work will require a future transfer of project budget from the transition structure contract to the SSD contract and other funds.

Contract Issues:

Issue	Mitigating Action
Delay to the SAS contract due to re-advertising and Addenda #5 and #7 to the SAS contract has impacts on the South/South Detour Contract.	<p>The TBPOC approved a plan to continue with the currently programmed SSD structure (see Recent TBPOC Actions below). Various options concerning contract scope and schedule are being considered to efficiently complete this contract while integrating any future SAS schedule revisions.</p> <p>The amount of contract delay is subject to analysis by Caltrans and negotiation with the Contractor. The projected delay to the SSD project is not expected to delay the overall open-to-traffic date for the East Span Replacement project, but is likely to have a significant impact to the SSD contract completion date.</p>

Recent TBPOC Actions: None

Contract Photographs

Column Cage



Excavation at W3



Trestle Construction



YBITS Advanced Work - Excavation at W3

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► YERBA BUENA ISLAND (YBI)

• YBI TRANSITION STRUCTURE CONTRACTS

Contract Description: The YBI Transition Structure #1 Contract will construct the mainline YBI transition structures (YBITS) that will connect the SAS portion of the new bridge to the existing YBI tunnels. The YBI Transition Structures #2 Contract includes demolition of the South/South Detour (SSD) temporary structure, completion of the new eastbound on-ramp, completion of the bike path section at YBI and reconstruction of local and affected facilities at YBI. The YBI Landscaping Contract includes slope restoration, vegetation restoration and plant maintenance for the areas affected by YBI construction.

YBI Transition Structure Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
YBI Transition Structure #1						
Capital Outlay Support	78.7	-	78.7	11.5	78.7	-
Capital Outlay Construction	299.3	-	299.3	-	318.5	19.2
TOTAL	378.0	-	378.0	11.5	397.2	19.2

Note: Details may not sum to totals due to rounding effects.

YBI Transition Structure Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
YBI Transition Structure #1	December 2013	12	December 2014	December 2014	-

Contract Status: The TBPOC has requested Caltrans to explore options to accelerate YBITS work in the SSD contract to reduce project schedule risks. The concept of advanced YBITS work was discussed as part of Alternative 1 for the SSD that was approved by the TBPOC on May 31, 2006. A specific package of accelerated foundation work on YBI has been identified by Caltrans, who will be presenting the package to the TBPOC for approval.

Contract Issues: None

Recent TBPOC Actions: None

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► OAKLAND TOUCHDOWN

• OAKLAND TOUCHDOWN SUBMARINE CABLE RELOCATION CONTRACT

Contract Description: The OTD Submarine Cable Contract will replace the existing submarine electrical cable from Oakland to Treasure Island, and will be completed ahead of OTD Contract No. 1 to avoid possible construction conflicts.

Oakland Touchdown Submarine Cable Relocation Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
OTD Submarine Cable						
Capital Outlay Support	-	-	-	0.3	3.0	-
Capital Outlay Construction	-	-	-	-	9.6	-
TOTAL	-	-	-	0.3	12.6	-

Note: Details may not sum to totals due to rounding effects. The allocation of AB144/SB 66 budgets is proceeding. Budget amount is TBD. Overall OTD budgets and forecasts are shown on page 2.

Oakland Touchdown Submarine Cable Relocation Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
OTD Submarine Cable	TBD	-	July 2007	October 2007	3

Contract Status: This contract was originally advertised for bids on July 31, 2006. On September 19, 2006, Caltrans received a single bid of \$13.1 million for the project, which Caltrans was not able to award due to issue with the technical specifications. In November 2006, Caltrans rebid the contract as two separate bids: one for a one-cable project and one for a two-cable project. On Monday, December 18, 2006, Caltrans opened five proposals each for the 1-cable and 2-cable relocation contracts. Caltrans rejected two of the submittals because they were incomplete. Manson Construction submitted the apparent low bid for the two-cable project (\$9.7 million) and for the one-cable project (\$7.0 million). Based on the recommendations of the TBPOC, on December 20th 2006, BATA supported Caltrans awarding a two-cable project, subject to the City of San Francisco providing required additional non-toll funding and upon Caltrans' review of the bids for responsiveness and allocated an additional \$600,000 in SRP funds to allow, if necessary, for the award to either the 2nd or 3rd lowest bidders on the 2-cable contract in the event that the contract could not be awarded to the lowest bidder to ensure that there are no further delays, related to the award of the cable project. Caltrans is expected to award the contract by January 9, 2007.

Contract Issues:

Issue	Mitigating Action
If the contractor cannot procure and install the cables within the specified timeframes, the cable relocation project could potentially delay work on the OTD#1 contract.	Work around specification language has been developed for the OTD#1 contract in case the cables are delayed.

Recent TBPOC Actions: In December 2006, TBPOC recommended that Caltrans award a submarine cable contract to the lowest responsive bidder for either the 2 or 1 cable relocation contract, subject to available funding from BATA and the City of San Francisco.

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► OAKLAND TOUCHDOWN

• OAKLAND TOUCHDOWN #1 CONTRACT

Contract Description: The Oakland Touchdown #1 Contract includes construction of all marine foundations, westbound bridge section and roadway approach for the section that connects the new Skyway portion to the roadway west of the Oakland Toll Plaza. This contract also constructs the electrical substation and the eastbound detour roadway. Traffic will not be placed on the detour until later during OTD #2.

Oakland Touchdown #1 Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
Oakland Touchdown #1						
Capital Outlay Support	-	-	-	2.5	49.9	-
Capital Outlay Construction	-	-	-	-	226.5	-
TOTAL	-	-	-	2.5	276.4	-

Note: Details may not sum to totals due to rounding effects. The allocation of AB144/SB 66 budgets is proceeding. Budget amount is TBD. Overall OTD budgets and forecasts are shown on page 2.

Oakland Touchdown #1 Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
Oakland Touchdown #1	-	-	July 2009	October 2009	3

Contract Status: Design work is complete. Plans, Specifications, and Engineer's Estimate (PS&E) were submitted to the Office Engineer on September 1, 2006. Bid advertise date is scheduled in early 2007 and contract completion is scheduled in October 2009.

Contract Issues:

Issue	Mitigating Action
Delays and cost increases due to conflicts from delays to the relocation of the submarine cable.	Caltrans will be incorporating work-around specification language in the OTD 1 contract to mitigate delays due to the cable.

Recent TBPOC Actions: In September 2006, the TBPOC approved the Plans, Specifications and Estimates for the OTD #1 contract. In October 2006, the TBPOC approved a capital outlay construction forecast of \$226.5 million.

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► OAKLAND TOUCHDOWN

• OAKLAND TOUCHDOWN #2 CONTRACT

Contract Description The Oakland Touchdown #2 Contract includes construction of the remaining eastbound bridge section and roadway approach for the section that connects the new Skyway portion to the roadway west of the Oakland Toll Plaza. This work would occur once the westbound traffic is shifted onto the new SAS.

Oakland Touchdown #2 Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
Oakland Touchdown #2						
Capital Outlay Support	-	-	-	0.2	15.8	-
Capital Outlay Construction	-	-	-	-	62.0	-
TOTAL	-	-	-	0.2	77.8	-

Note: Details may not sum to totals due to rounding effects. The allocation of AB144/SB 66 budgets is proceeding. Budget amount is TBD. Overall OTD budgets and forecasts are shown on page 2.

Oakland Touchdown #1 Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
Oakland Touchdown #2	-	-	December 2014	December 2014	-

Contract Status: Design work for the structures portion of OTD Contract No. 2 is complete and will be advertised as scheduled in 2010 in time for SAS opening.

Contract Issues: None

Recent TBPOC Actions: None

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► OTHER MAJOR CONTRACTS

Contract Description: Other Major Contracts include the Stormwater Treatment Measures contract, which will implement best practices for stormwater runoff treatment at the SFOBB toll plaza; the Oakland Touchdown Electrical Systems Contract, which will incorporate most of the electrical elements from OTD as well as from other segments of the East Span; and the Existing Bridge Demolition contract, which will include the complete removal of the existing 1936 east span following the opening of the new bridge.

Other Major Contracts Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
A	b	c	d = b + c	e	f	g = f - d
Capital Outlay Support	238.8	-	238.8	40.2	256.5	17.7
Capital Outlay Construction						-
Existing Bridge Demolition	239.2	-	239.2	-	222.0	(17.2)
Stormwater Treatment Measures	15.0	-	15.0	4.4	15.0	-
Total Capital Outlay Construction	254.2	-	254.2	4.4	237.0	(17.2)
TOTAL	493.0	-	493.0	44.6	493.5	0.5

Note: Details may not sum to totals due to rounding effects.

Other Major Contracts Schedule Summary

Contract	AB 144/SB 66 Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)	% Design Comp.
Existing Bridge Demolition	September 2014	12	September 2015	September 2015	-	10
Stormwater Treatment Measures	March 2008	-	March 2008	June 2007	(9)	N/A

Contract Status:

Stormwater Treatment Measures: The project is currently under construction. Some delays in the work have been experienced due to nesting birds, buried man-made objects, unidentified utilities, and discovery of unsuitable materials. The current schedule forecast shows an early completion date due to an accelerated award of the contract by Caltrans and a reduced construction contract duration that was bid by the contractor as part of an A+B bid.

Oakland Touchdown Electrical Systems: Determination of contract scope is underway. Caltrans is also considering the option of incorporating this work into the Oakland Touchdown #2 contract.

Bridge Demolition: Design work has been temporarily suspended to assign engineering resources to higher priority tasks, and will resume at a later time. The contract schedule completion date has been extended by 12 months due to a 12-month SAS contract extension. The \$17.2 million decrease in construction costs for the Existing Bridge Demolition contract is due to a re-evaluation of cost escalation rates for the contract.

Contract Issues: None

Recent TBPOC Actions: None

Contract Photographs



Headwall Pour



Interference with Existing Ductbank



Pump Station 2 Installation



Pump Station 3A Top Slab Pour

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project

► OTHER COMPLETED CONTRACTS AND RELATED WORK

Summary Description: Substantial work has already been performed on the SFOBB East Span Replacement project to facilitate construction of the mainline construction contracts.

Other Contracts and Related Work Cost Summary (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	E	f	g = f - d
Capital Outlay Support	227.0	-	227.0	209.0	227.0	-
Right-of-Way and Environmental Mitigation	72.4	-	72.4	38.8	72.4	-
Capital Outlay Construction						-
SAS W2 Foundations	26.4	-	26.4	25.2	26.4	-
YBI/SAS Archeology	1.1	-	1.1	1.1	1.1	-
YBI - USCG Road Relocation	3.0	-	3.0	2.8	3.0	-
YBI - Substation and Viaduct	11.6	-	11.6	11.3	11.6	-
Oakland Geofill	8.2	-	8.2	8.2	8.2	-
Pile Installation Demonstration Project	9.2	-	9.2	9.2	9.2	-
Existing East Span Retrofit	30.8	-	30.8	30.8	30.8	-
Total Capital Outlay Construction Completed	90.3	-	90.3	88.5	90.3	-
TOTAL	389.7	-	389.7	336.4	389.7	

Note: Details may not sum to totals due to rounding effects.

Other Contracts and Related Work Schedule Summary

Project	Actual Project Completion Date
Existing East Span Retrofit	March 1998
Interim Retrofit	July 2000
Pile Installation Demolition Project	December 2000
YBI / SAS Archaeology	January 2003
Oakland Geofill	April 2003
YBI – USCG Road Relocation	June 2004
SAS W2 Foundations	October 2004
YBI Substation and Viaduct	May 2005

Summary Status: Construction has been completed on the above listed contracts. Caltrans continues to work with various environmental agencies to conduct compliance inspections and monitor and mitigate any environmental impacts from the project.

Contract Issues: None.

Recent TBPOC Actions: None.

Toll Bridge Seismic Retrofit Program

San Francisco-Oakland Bay Bridge (SFOBB) West Approach Replacement Project

Project Description: The SFOBB West Approach Replacement Project will replace the entire west approach structure from 5th Street to the west anchorage of the existing west spans of the SFOBB while maintaining existing traffic lanes for the weekday commute.

SFOBB West Approach Replacement Cost Summary (\$Millions)

Project	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
West Approach						
Capital Outlay Support	120.0	-	120.0	86.0	120.0	-
Capital Outlay Construction	309.0	-	309.0	218.8	309.0	-
TOTAL	429.0	-	429.0	304.8	429.0	-

Note: Details may not sum to totals due to rounding effects.

SFOBB West Approach Replacement Schedule Summary

Project	AB 144/SB 66 Project Completion Baseline (07/2005)	Approved Changes (Months)	Project Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
West Approach	August 2009	-	August 2009	August 2009	-


Project Status: Construction is 74% complete as of November 20, 2006. Major ongoing work includes continuation of work on the next phase of piles for the permanent westbound I-80 mainline structures, the 5th Street and Harrison Street ramps, the 4th Street retrofit work, and superstructure work. Beale Street was opened to vehicular traffic on October 30, 2006.

Project Issues:

Issue	Mitigating Action
Pile investigation and testing for the identification of pile anomalies must be completed in a timely manner so as to avoid construction impact.	Work on piles has progressed. Caltrans Construction coordinates closely with Structure Design and METS daily on pile investigation and testing issues, and proactively monitors this effort. Tracking of the testing effort is done for each individual pile. Team participation in Risk Management meetings has proven to be valuable in addressing this issue.
Original plans for the ST6D alignment would result in significant operational issues for the First and Essex Street on-ramps to the bridge in San Francisco. (See page 31)	Caltrans Construction is preparing a change order to modify the ST6D alignment to allow for more conventional geometric alignments for the on-ramps and I-80 eastbound mainline traffic.

Recent TBPOC Actions: None.

Project Photographs

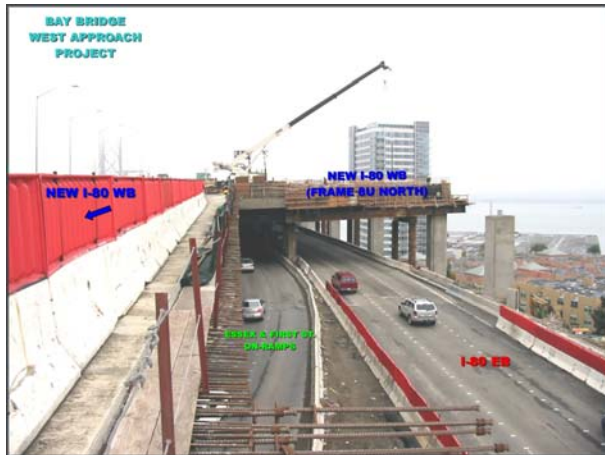

West Approach Progress Photo 1




West Approach Progress Photo 2



West Approach Progress Photo 3




West Approach Progress Photo 4

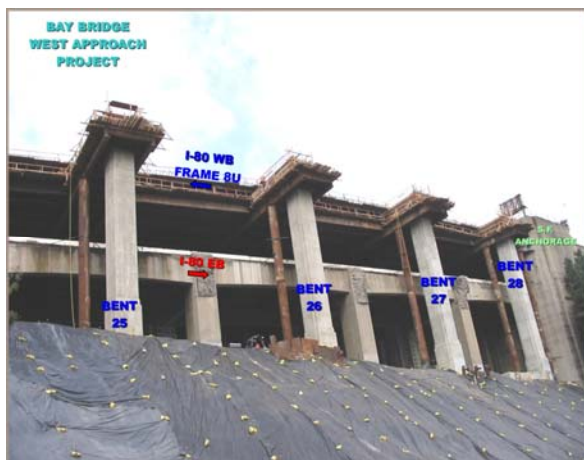

West Approach Progress Photo 5



West Approach Progress Photo 6

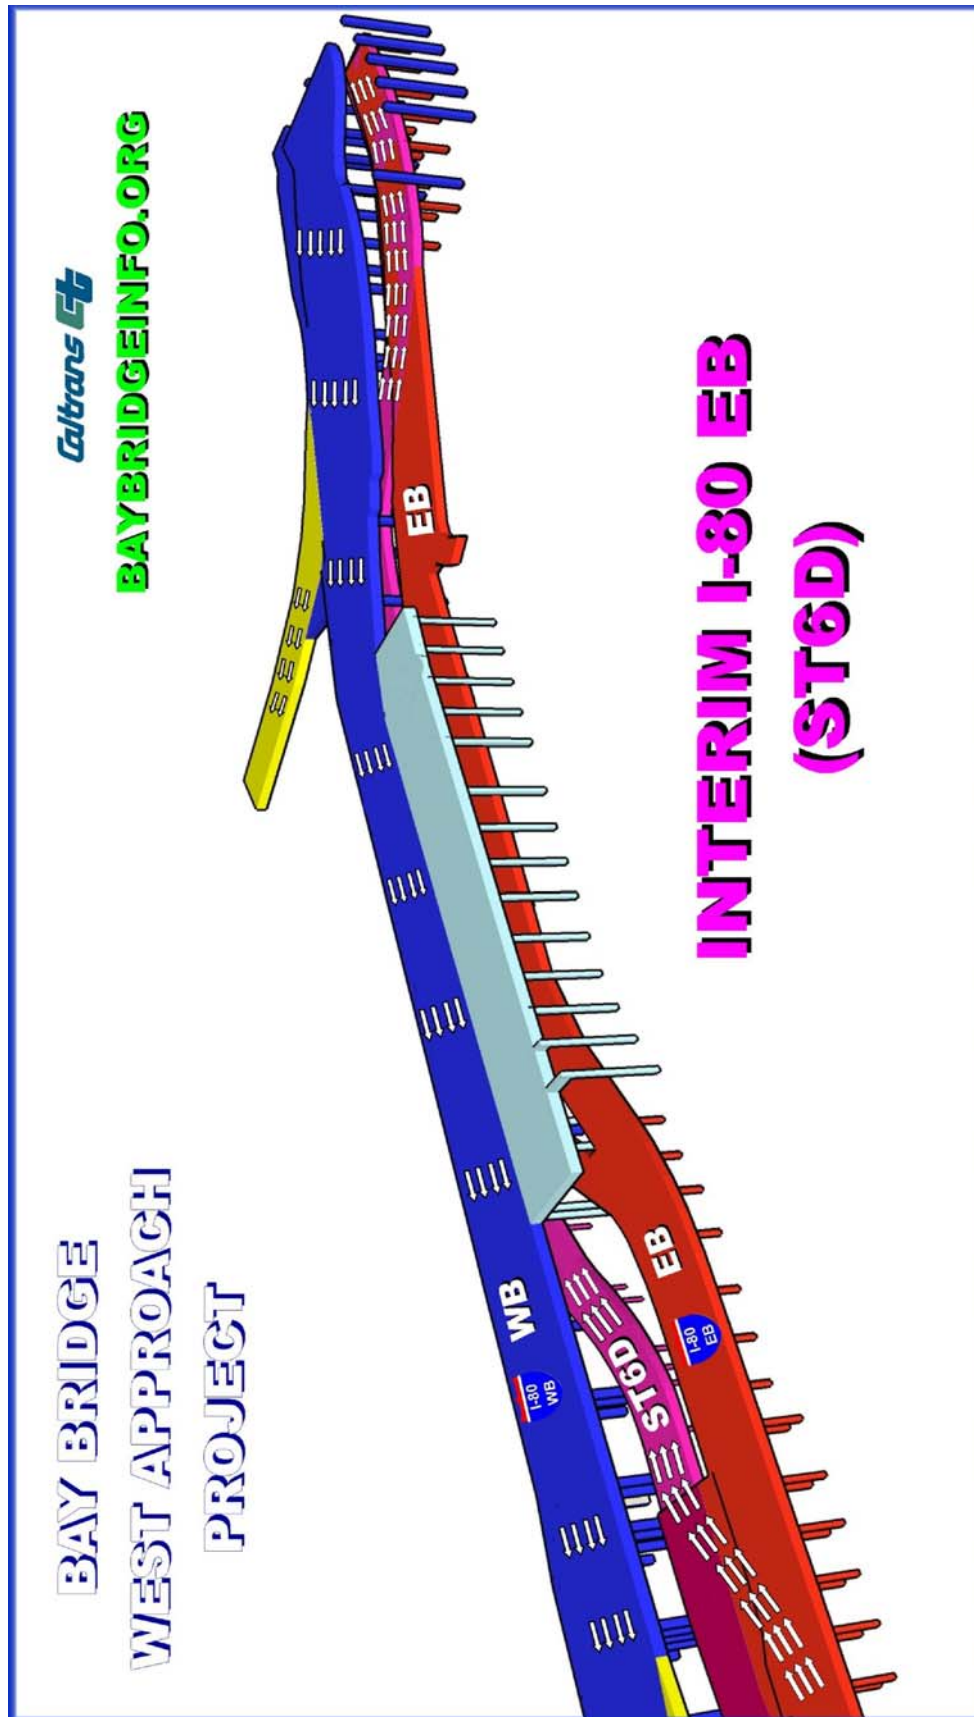

Toll Bridge Seismic Retrofit Program

Richmond-San Rafael Bridge (RSRB) Seismic Retrofit Project

Project Description: The Richmond-San Rafael (RSR) Bridge Seismic Retrofit Project strengthened the existing bridge to withstand the effects of a large seismic event. As part of the retrofit work, Caltrans performed work to strengthen the bridge foundations, replace the existing west trestle and the main channel fenders, and complete the joint rehabilitation of the bridge deck. (The RM1 work is reported in the RM1 section of the report).

RSRB Seismic Retrofit Cost Summary (\$Millions)

Project	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
RSRB Seismic Retrofit						
Capital Outlay Support	134.0	(7.0)	127.0	125.6	127.0	-
Capital Outlay Construction & Right-of-Way	780.0	(82.0)	698.0	665.6	698.0	-
TOTAL	914.0	(89.0)	825.0	791.2	825.0	-

Note: Details may not sum to totals due to rounding effects.

* The seismic retrofit contract included work to rehabilitate the bridge deck joints. Although the deck joint work was funded from RM1 toll funds, the work is also eligible for Toll Bridge Seismic Retrofit Program funding. In July 2005, BATA rescinded \$16.9 million in RM1 funds for the deck joint work to make additional RM1 funds available for the New Benicia-Martinez Bridge Project. An equivalent amount of seismic funds will be used on the deck joint work, which is included in the budget above.

RSRB Seismic Retrofit Schedule Summary

Project	AB 144/SB 66 Project Completion Baseline (07/2005)	Approved Changes (Months)	Project Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
RSRB Seismic Retrofit	August 2005	-	August 2005	October 2005	2
RSRB Public Access Project	NA	-	May 2007	May 2007	-

Project Status: The retrofit construction contract was completed and accepted on October 28, 2005.

Project savings in the amount of \$89 million has been transferred to the program contingency in October 2006.

Caltrans has submitted the project plans and specifications for a public access lot on the Marin side of the bridge to comply with a Bay Conservation and Development Commission (BCDC) permit condition (see the exhibit on page 33). It was advertised on October 2, 2006 and bids were opened on December 1, 2006. Seven bids were submitted with Ghilloti Bros. Inc., submitting the apparent lowest A+B bid of \$1,005,863.40, as compared with the Engineer's Estimate of \$1,072,157.25.

Contract Issues: None.

Recent TBPOC Actions: None.



Toll Bridge Seismic Retrofit Program

Other Completed Seismic Retrofit Projects

Summary Description: Caltrans has already completed the seismic retrofits of the West Spans of the SFOBB, the existing 1958 Carquinez Bridge, the existing Benicia-Martinez Bridge, the San Mateo-Hayward Bridge, and two former toll bridges in southern California.

Other Completed Seismic Retrofit Projects Cost Summary (\$Millions)

Project	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	F	g = f - d
San Francisco-Oakland Bay Bridge West Span Seismic Retrofit Project	307.9	-	307.9	301.0	307.9	-
Carquinez Bridge Retrofit Project	114.2	-	114.2	114.2	114.2	-
Benicia-Martinez Bridge Retrofit Project	177.8	-	177.8	177.8	177.8	-
San Mateo-Hayward Bridge Retrofit Project	163.5	-	163.5	163.4	163.5	-
Vincent Thomas Bridge Retrofit Project	58.5	-	58.5	58.4	58.5	-
San Diego-Coronado Bridge Retrofit Project	103.5	-	103.5	102.6	103.5	-
TOTAL	925.4	-	925.4	917.4	925.4	-

Note: Details may not sum to totals due to rounding effects. Capital Outlay Support and Capital Outlay have been combined.

Other Completed Seismic Retrofit Projects Schedule Summary

Project	Actual Project Completion Date
Vincent Thomas Bridge Retrofit	May 2000
San Mateo-Hayward Bridge Retrofit	June 2000
Carquinez Bridge Retrofit	January 2002
San Diego-Coronado Bridge Retrofit	June 2002
Benicia-Martinez Bridge Retrofit	August 2002
SFOBB West Span Seismic Retrofit	June 2004

Summary Status: Construction has been completed on the above-listed projects. The Estimate at Completion amounts shown above include allowances for minor project closeout costs.

Contract Issues: None.

Recent TBPOC Actions: None.

Toll Bridge Seismic Retrofit Program

Other Toll Bridges

Dumbarton and Antioch Bridges

The original design of the Dumbarton and Antioch Bridges were based on design criteria developed after the 1971 San Fernando Earthquake. In the early 1990's, Caltrans determined that these two structures had the seismic resistant features required by the post 1971 codes and were not likely to be vulnerable during a major seismic event. Since that time, Caltrans has pursued an aggressive seismic research program. Based on the results of this program, Caltrans significantly revised its seismic design practice in the late 1990's. Consistent with recommendations by the Caltrans Seismic Advisory Board, Caltrans regularly reassesses the seismic risk and performance of its bridges. Due to the tremendous changes in seismic design practice that have occurred since the design of the Dumbarton and Antioch bridges, a comprehensive assessment of the potential need and scope for seismic retrofit based on current knowledge is advised.

Vulnerability Studies

In late 2004, Caltrans initiated vulnerability studies on the Dumbarton and Antioch bridges. The purpose of these studies was to determine if the bridges would meet current seismic performance standards. The studies were essentially completed in May 2005. They were not complete global analyses, but rather investigations of selected bents modeled as independent structures. The analyses were limited in scope and based on as-built plans and currently available geotechnical information. The superstructure response was not analyzed.

The Dumbarton and Antioch Bridges have many seismic resistant features, and the results of the vulnerability studies indicate that the bridges should perform well in a moderate seismic event. However, during a major seismic event, some potential vulnerabilities (summarized below) become apparent.

- ◆ Foundation response generally governs performance. The piles may plunge axially and potentially cause permanent footing rotations.
- ◆ Potentially large foundation displacements and rotations may result in deformations that can't be easily repaired.
- ◆ The capacity of the ductile columns is greater than those of the bent cap, pile cap, pile and superstructure. As a result, the latter elements may be damaged in a major event, especially if the foundation is retrofitted.

Given the limitations of the studies, there was insufficient evidence to conclusively determine the performance of the bridges during a maximum credible earthquake (MCE). While the Dumbarton and Antioch bridges may meet performance standards, a more comprehensive technical study is necessary to understand the performance of these structures during an MCE event. A study of this level is necessary to accurately determine the structures' response and to develop any necessary retrofit strategies. A comprehensive geotechnical study using the latest analysis techniques is likely necessary in order to perform this level of analysis.

Sensitivity Analysis

As a follow-up to the Vulnerability Study, a sensitivity analysis was completed on a single representative bent used in the Vulnerability Study (Bent 23 of the Dumbarton Bridge). The goal of the analysis is to determine the structural response associated with uncertainties in the geotechnical data. An envelope of soil conditions (best-case and worst-case scenarios) was used in the analysis.

The results from the sensitivity analysis indicate that the seismic response of the bridge is largely dependant on the soil conditions and that a comprehensive geotechnical investigation is essential for understanding the bridge's performance during a major seismic event. A work plan was developed to assess the extent of geotechnical work needed for a refined seismic analysis and to assess the required performance levels for each structure. Caltrans has completed the value analysis to scope the geotechnical investigation that will be required to complete the strategy. The final report was issued on July 24, 2006.

Cost and Schedule


A preliminary cost estimate, schedule, and initial risk analysis have been developed to complete a comprehensive seismic analysis for each bridge. The preliminary estimate and schedule were developed as a baseline that assumed a complete geotechnical and geophysical investigation would be required at each bridge.

Current Progress

In June 2006, BATA approved \$17.8 million in funding to proceed with the comprehensive seismic analysis of the bridges. By September 2006, BATA entered into a contract with Earth Mechanics to conduct geotechnical and geophysical investigations, which have been on-going since December 6, 2006.

- ◆ At the Dumbarton Bridge, drilling at 17 of the 19 on-land field data locations have been completed. The marine work started on December 11, 2006 and to date, 6 of the 31 marine field data locations have been completed.
- ◆ At the Antioch Bridge, drilling at 28 of the 30 on-land field data locations have been completed. The marine work has not yet begun at Antioch.
- ◆ A bathymetric survey (the measurement of the depth from the water surface to the mudline) has been completed at both bridges. This survey will provide the topography of the bay mud in the vicinity of each bridge.

Caltrans is currently reviewing this new geotechnical data, as well as, existing geotechnical data. Caltrans is scheduled in January 2007, to begin the structural analysis in support of a range of seismic retrofit strategies for each bridge.

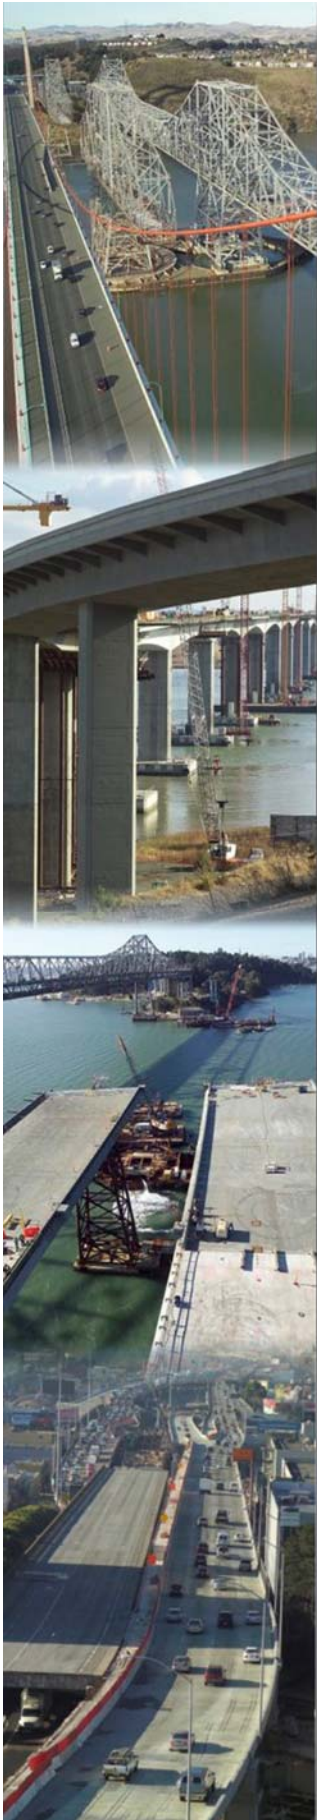

PROJECT / CONTRACT REPORTS

Regional Measure 1 Program

New Benicia-Martinez Bridge Project Summary

- New Benicia-Martinez Bridge Contract
- Other Contracts and Related Project Activities

New Carquinez Bridge Project

Richmond-San Rafael Bridge Deck Overlay Project

Interstate 880 / State Route 92 Interchange Reconstruction

Other Completed Regional Measure 1 Projects

- San Mateo–Hayward Bridge Widening Project
- Richmond Parkway Project
- Bayfront Expressway Widening Project
- Richmond-San Rafael Bridge Trestle, Fender, and Deck Joint Rehabilitation Project

Regional Measure 1 Program

New Benicia-Martinez Bridge Project Summary

Project Description: The new Benicia-Martinez Bridge project constructs a new parallel bridge just east of the existing bridge. The project will include reconstructed interchanges to the north and south of the bridges and a new toll plaza and administration building in Martinez.

New Benicia-Martinez Bridge Project Cost Summary (\$Millions)

Contract	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
Capital Outlay Support	157.1	24.8	181.8	160.7	181.8	-
Right-of-Way and Others	20.4	(0.1)	20.3	12.3	20.3	-
Capital Outlay						-
New Bridge	672.0	107.3	779.3	712.0	779.3	-
I-680/I-780 Interchange Replacement	76.3	16.1	92.4	82.9	92.4	-
I-680/Marina Vista Interchange Reconstruction	51.5	8.1	59.6	54.7	59.6	-
New Toll Plaza	24.3	2.0	26.3	22.6	26.3	-
Existing Bridge & Interchange Modifications	17.2	10.9	28.1	-	28.1	-
Other	20.3	(1.3)	19.0	15.2	19.0	-
Project Reserve	20.8	35.3	56.2	-	56.2	-
TOTAL	1,059.9	203.1	1,263.0	1,060.4	1,263.0	-

Note: Details may not sum to totals due to rounding effects.

* The budget and estimate at completion includes approximately \$33 million in non-toll bridge funds (Proposition 192 and SHOPP).

New Benicia-Martinez Bridge Project Schedule Summary

Contract	BATA Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
I-680/Marina Vista Interchange Reconstruction	March 2006	1	April 2006	April 2006	-
New Toll Plaza	June 2006	-	June 2006	January 2007	7
New Benicia-Martinez Bridge	December 2007	-	December 2007	December 2007	-
I-680/I-780 Interchange Replacement	December 2007	-	December 2007	February 2008	2
Open to Traffic	December 2007	-	December 2007	December 2007	-
Existing Bridge & Interchange Modifications	December 2009	-	December 2009	December 2009	-

*See page 45 for an explanation of change in schedule forecast.

Project Status: All major construction projects necessary to open the bridge are currently in construction. Numerous foundation and superstructure issues have significantly delayed the new bridge contract. See the following contract detail pages for more information. Note that the remaining expenditures required on the “Right-of-Way and Others” category represent environmental permitting and mitigation.

Project Issues: None

Recent TBPOC Actions: See the following contract detail pages for more information.

Project Photographs



Benicia-Martinez Toll Plaza Canopy Progress Photo 1




Benicia-Martinez Toll Plaza Canopy Progress Photo 2




Operations Building & Courtyard looking west



Toll Plaza Administration Building

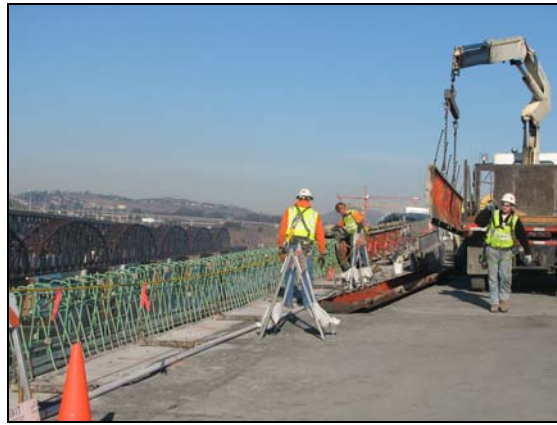Project Photographs Cont'd.*Aerial Photo of the Benicia-Martinez Bridges**Barrier Rail Construction at New Bridge Photo 1**Barrier Rail Construction at New Bridge Photo 2**Benicia-Martinez Progress Photo 1**Benicia-Martinez Progress Photo 2**Benicia-Martinez Progress Photo 3*

New Benicia-Martinez Bridge Progress Diagram December 2006

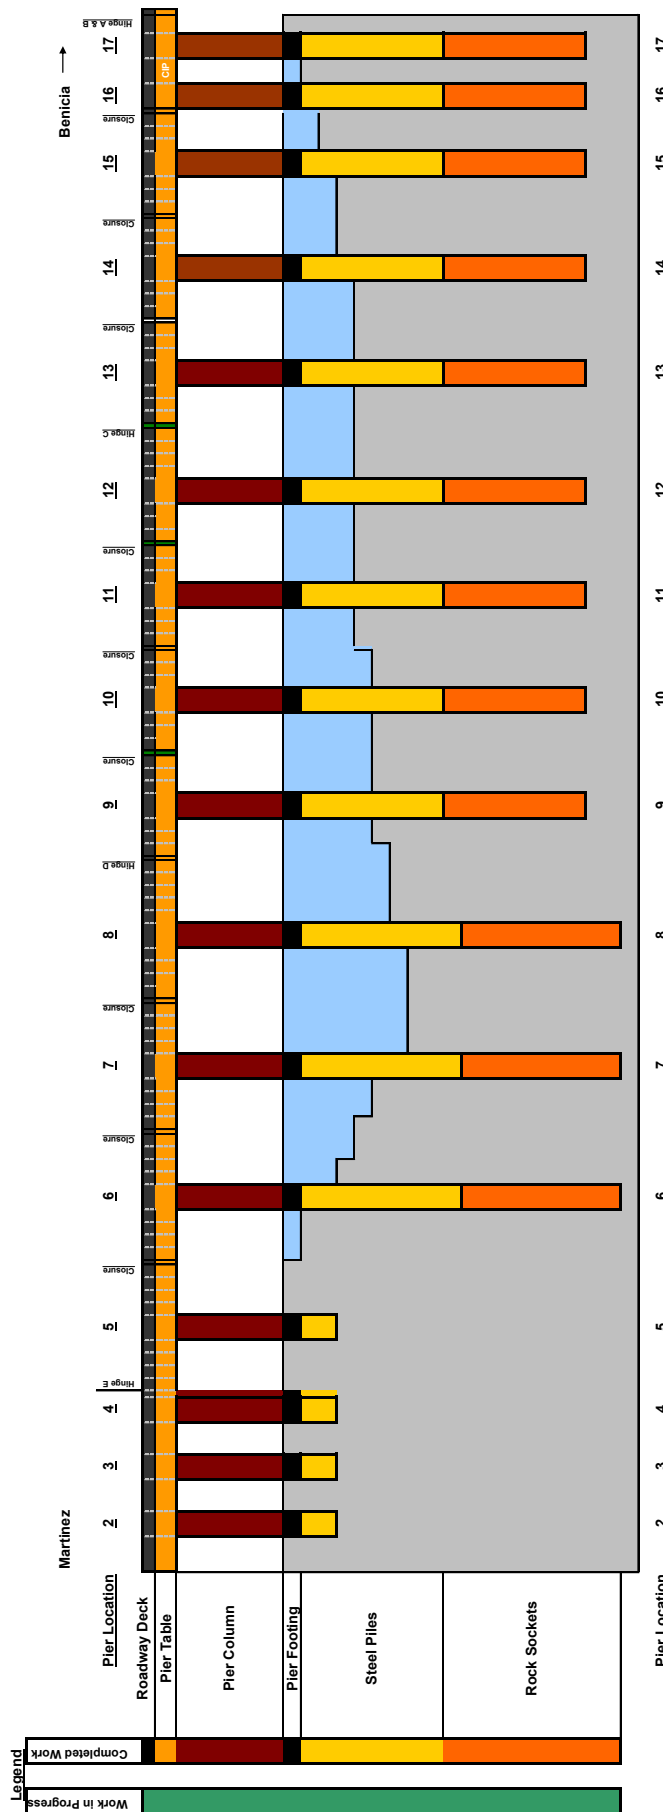

Notes:

1. Abutment 1 and Piers 2 through 5 are on land and have 66 piles. All piles, footings, columns and pier tables are complete. The superstructure is complete from Abutment 1 to Pier 4.
2. Piers 6 through 17 are located in the water and have 8 to 9 piles and rock sockets each - a total of 99. All 99 piles have been driven to their required depth and all 99 rock sockets have been installed.
3. Piers 6 through 17 have two-part footings. Piers 6, 16 and 17 have a cast-in-place (CIP) upper section and a cast-in-place (CIP) lower section, which are lowered onto the piles. All three footings are complete. Piers 7 through 15 have a precast lower section that is set on the piles and a cast-in-place (CIP) upper section. All nine precast footings have been set and all CIP footings are complete.
4. All Stage 2 footings have been poured and stressed.
5. All pier tables are complete as of the end of May 2006.
6. Piers 4 through 15 have 344 cast-in-place cantilevered superstructure segments. All of the three-hundred and forty-four (344) segments (100%) have been cast to-date. Hinges A, B, E and D are completed and Hinge C is still in progress. Six span closures (5, 6, 7, 9, 10 and 15) have been poured. Three (3) span closures remain to be done. Span 13 closure will be the last scheduled to be poured on 12/20/06.
7. The cast-in-place on falseworks superstructure south of Pier 4 is substantially complete, except for the bridge deck repair work, which are still to be done. The structure north of Pier 15 is substantially complete, including the lower and the upper hinge seats at Hinges A and B.

Regional Measure 1 Program

New Benicia-Martinez Bridge Project

► NEW BENICIA-MARTINEZ BRIDGE CONTRACT

Contract Description: The new bridge contract constructs a new cast-in-place segmentally constructed reinforced concrete bridge just east of the existing bridge. The new bridge will carry five lanes of eastbound I-680 traffic towards Benicia.

New Benicia-Martinez Bridge Cost Summary (\$Millions)

Contract	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
New Benicia-Martinez Bridge						
Capital Outlay Support	84.9	7.7	92.6	81.1	92.6	-
Capital Outlay Construction	672.0	107.3	779.3	712.0	779.3	-
TOTAL	756.9	115.0	871.9	793.1	871.9	-

Note: Details may not sum to totals due to rounding effects.

New Benicia-Martinez Bridge Schedule Summary

Contract	BATA Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
New Benicia-Martinez Bridge	December 2007	-	December 2007	December 2007	-

Contract Status: The contract is 91% complete based on the current revised schedule. All substructure and column work have been completed. Superstructure work continues throughout the project. For the cast-in-place portion of the bridge over the straits (Frames 2 and 3), all 11 of the pier tables and all 344 segments have been completed. Hinge E, connecting Frames 4 and 3 between Piers 4 and 5; Hinge D, connecting Frames 2 and 3 between Piers 8 and 9, and Hinges A & B, connecting Frame 1 with the I-680/780 connector bridges, have been completed. Hinge C is completely poured out. The remaining work consists of plate girder and bearing installation, which will continue through December 2006. Concrete closure pours on Spans 5, 6, 7, 10, 14 and 15 of the New Benicia-Martinez Bridge, which links the individual piers together into a frame, have been poured. The closure formwork has been hoisted into position at Spans 9 and 11. The closure formwork at Span 13 was hoisted into position on December 12 and poured on December 20, which will be the last closure to be done.

For the cast-on-falsework structures (Frames 1 and 4), work on Frame 4 on the south side of the straits is complete. Polyester concrete patches will be needed on the bridge deck around Pier 3, due to poor quality of surface concrete after grinding. A repair plan submittal for the polyester concrete patches has been reviewed but will not be approved until additional information and testing can be performed. On Frame 1, the structure is complete and has been stressed. Falsework removal is now complete. The Contractor continues to demobilize winches and other miscellaneous equipment. Some problems with the finishing of the Span 15 top deck occurred, so a similar repair to Frame 4 top deck will be required.

Other on-going project work includes work on the interior and exterior finishes at Piers 6, 9 and 14, installation of rails and maintenance travelers, and installation of pier table fixed platform beams at various piers, and installation of rebar, forms and pour barrier rails throughout the new bridge.

Consistent with BATA's Fastrak strategic plan, plans are progressing for the implementation of open road tolling at the toll plaza, which will involve the demolition of the toll booths. A CCO is currently being processed between Caltrans and Kiewit in the amount of \$4.83 million. Addendum # 3, which is mostly electrical changes were issued to the Contractor for pricing. This addendum # 3 and other design changes that are still being made will be treated as a Supplement to the CCO that is currently being processed

Contract Issues: None

Recent TBPOC Actions: TBPOC recently approved budget for the CCO #164 the amount of \$4.83 million plus \$500K for additional contingency.

Regional Measure 1 Program

New Benicia-Martinez Bridge Project Summary► **OTHER CONTRACTS AND RELATED PROJECT ACTIVITIES**

Contract Description: Contracts related to the new Benicia-Martinez Bridge project involve the construction of a new toll plaza south of the new bridge in Contra Costa County with 17 toll booths, including two high-occupancy vehicle (HOV) bypass lanes, and the reconstruction of the I-680/Marina Vista Road and I-680/I-780 interchanges.

Other Contracts and Related Activities Cost Summary (\$Millions)

Contract	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
Capital Outlay Support	72.2	17.0	89.2	79.6	89.2	-
Right-of-Way and Environmental Mitigation	20.4	(0.1)	20.3	12.3	20.3	-
Capital Outlay Construction						
I-680/I-780 Interchange Replacement	76.3	16.1	92.4	82.9	92.4	-
I-680/Marina Vista Interchange Reconstruction	51.5	8.1	59.6	54.7	59.6	-
New Toll Plaza	24.3	2.0	26.3	22.6	26.3	-
Existing Bridge & Interchange Modifications	17.2	10.9	28.1	-	28.1	-
Others	20.3	(1.3)	19.0	15.2	19.0	-
Total Capital Outlay Construction	189.6	35.8	225.4	175.4	225.4	-
TOTAL	282.2	52.7	334.9	267.3	334.9	-

Note: Details may not sum to totals due to rounding effects.

Other Contracts and Related Activities Schedule Summary

Contract	BATA Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
I-680/Marina Vista Interchange Reconstruction	March 2006	1	April 2006	April 2006	-
New Toll Plaza	June 2006	-	June 2006	January 2007	7
I-680/I-780 Interchange Replacement	December 2007	-	December 2007	February 2008	2
Existing Bridge & Interchange Modifications	December 2009	-	December 2009	December 2009	-

Contract Status:

Toll Plaza and Administration Building: The contract is 98% complete based on contractor payment. The Contractor is continuing work throughout the toll plaza area. Punchlist for architectural, electrical and mechanical correction work is on-going for the Operations Building, Toll Plaza and Courtyard. The contractor is continuing with the installation of column architectural paneling at the Operations Building and Courtyard. A number of notices of potential claim that have been filed by the Contractor remain to be resolved, but this will have no impact on the bridge Open-to-Traffic date. Resident Engineer's estimated date for completion is now forecast for January 15, 2007, due to rejected panel work

I-680/I-780 Interchange: The contract remains approximately 95% complete based on the current revised schedule. To-date, all of the bridge structures are substantially complete, except for barrier rails works and stripping of falsework at Span 17. Work on the Drainage System 17 was completed. The electrical sub-contractor, Bleyco, continued to install cable tray in the Benicia-Martinez Approach Structure (Br. No. 23-0215R). Final electrical work for the new Benicia-Martinez Bridge and the interchange will not be completed until after the new bridge is complete.

I-680/Marina Vista Interchange: The contract is 100% complete as of April 28, 2006, and has been accepted by Caltrans. Caltrans and the contractor are currently resolving the final payment for work on the contract. A final estimate and payment is being negotiated to settle all noted exceptions between Caltrans and the contractor.

Wetland Mitigation: The contract is 100% complete. The Contract Completion Acceptance (CCA) was submitted to Caltrans Headquarters for their approval on March 3, 2006. The Proposed Final Estimate (PFE) has been reviewed and accepted by the Contractor.

Contract Issues: None

Recent TBPOC Actions: In November 2006, the TBPOC approved the amount of \$4.83 million plus \$500K of additional contingency for the Benicia-Martinez Bridge Project CCO to cover ORT work and other work required to open the bridge to traffic.

Regional Measure 1 Program

New Carquinez Bridge Project

Project Description: The new Carquinez Bridge project involves constructing a new suspension bridge west of the existing bridges with four westbound lanes and a bicycle/pedestrian lane and demolishing the existing 1927 bridge.

New Carquinez Bridge Cost Summary (\$Millions)

Contract	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
Capital Outlay Support	124.4	(1.1)	123.3	117.6	123.2	(0.1)
Capital Outlay Construction						
Replacement Bridge	253.3	4.0	257.3	256.9	257.3	-
South Interchange Reconstruction	73.9	-	73.9	71.9	73.9	-
Existing 1927 Bridge Demolition	35.2	-	35.2	21.7	35.2	-
Other	29.3	(0.7)	28.6	25.2	28.4	(0.2)
Project Reserve	12.1	(2.2)	9.9	-	10.2	0.3
TOTAL	528.2	-	528.2	493.3	528.2	(0.0)

Note: Details may not sum to totals due to rounding effects.

New Carquinez Bridge Schedule Summary


Contract	BATA Contract Completion Baseline (07/2005)	Approved Changes (Months)	Contract Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
New Carquinez Bridge	December 2003*	-	December 2003*	December 2003*	-
1927 Carquinez Bridge Demolition	December 2007	-	December 2007	December 2007	-
Landscaping	August 2011	-	August 2011	August 2011	-

* The date shown is for the opening of the bridge to traffic.

Project Status: The new replacement bridge and all its approaches have been completed and opened to traffic. The demolition contract to remove the 1927 bridge is approximately 58% complete based on schedule. However, based on payment, this contract is 72% complete in that the greatest pay items involved the 1958 bridge approach deck replacement, which has been completed. To-date, demolition of Units 1, 2, 3 and 7 of the 1927 bridge have been completed. Demolition work has been resumed at Units 4 and 6. Stairs were installed at Unit 9 to access panel points 2, 4 and 6. Falsework for Unit 1 has been removed and will be relocated to Unit 9. Contractor is currently working on temp support at Unit 9. The demolition of the 1927 bridge approach structure has started this month, and which will go on for an approximate duration of 6 months.

Project Issues:

Issue	Mitigating Action
Contractor has not yet formally stated the schedule impact of the 3-month work suspension related to the unanticipated buckling of eye bars during the demolition of Units 3 and 7.	Caltrans will continue to communicate to the Contractor the need to submit the TIA. Caltrans will then evaluate it to establish a basis for negotiations. The resulting CCO should have no impact to the contract or overall project budget.

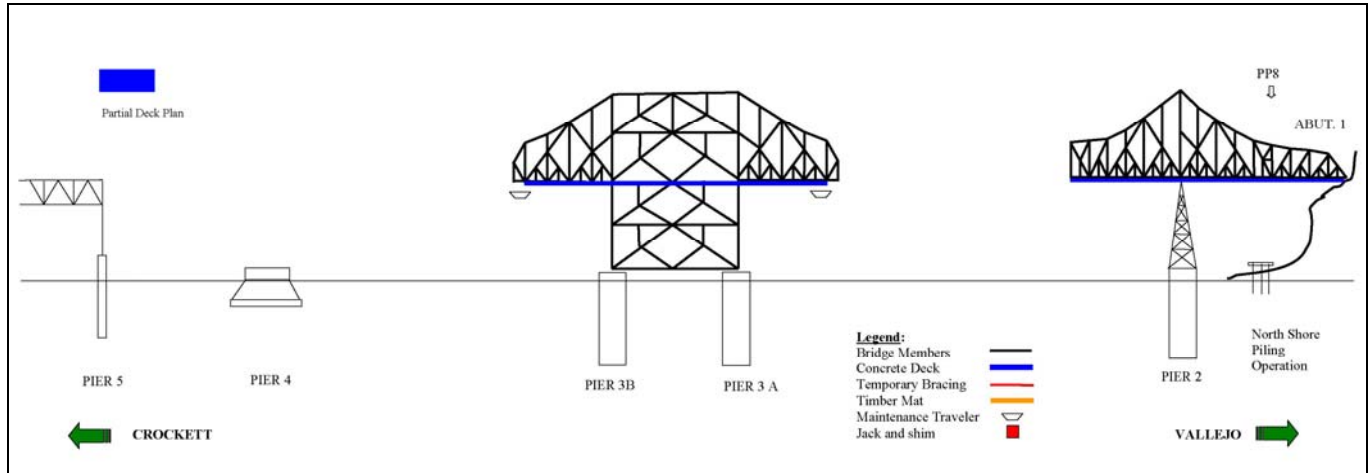Project Photographs

1927 Carquinez Bridge Demolition Progress Status as of November 30, 2006



Carquinez Bridge Progress Photo 1



Carquinez Bridge Progress Photo 2




Carquinez Bridge Progress Photo 3



Carquinez Bridge Progress Photo 4



Carquinez Bridge Progress Photo 5

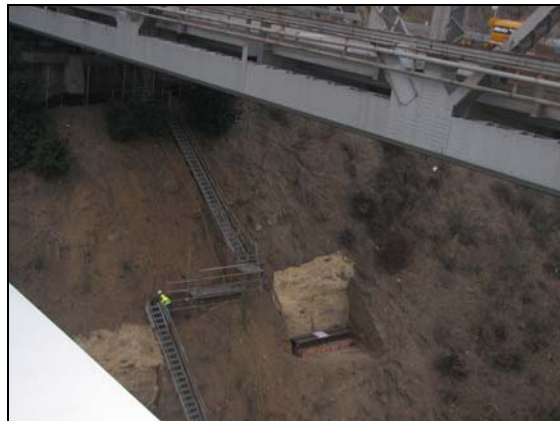

Carquinez Bridge Progress Photo 6



Carquinez Bridge Progress Photo 7



Carquinez Bridge Progress Photo 8

Regional Measure 1 Program

Richmond-San Rafael Bridge (RSRB) Deck Overlay Project

Project Description: Rehabilitate the existing concrete deck on the bridge, damaged due to traffic and exposure to a marine environment.

RSRB Deck Overlay Cost Summary (\$Millions)

Contract	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	b	c	d = b + c	e	f	g = f - d
RSR Deck Overlay						
Capital Outlay Support	8.0	(3.5)	4.5	2.9	4.5	-
Capital Outlay Construction	16.9	3.6	20.5	14.4	20.5	-
Project Reserve	0.1	(0.1)	-	-	-	-
TOTAL	25.0	-	25.0	17.3	25.0	-

Note: Details may not sum to totals due to rounding effects.

RSRB Deck Overlay Schedule Summary

Project	BATA Project Completion Baseline (07/2005)	Approved Changes (Months)	Project Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
Richmond-San Rafael Bridge Deck Overlay Rehabilitation	January 2007	-	January 2007	January 2007	-

Project Status: As of December 1, 2006, all construction work has been accepted.


Project Issues: None

Project Photographs



RSR Concrete Deck Overlay

RICHMOND-SAN RAFAEL BRIDGE
CONTRACT No. 04-041524
(Progress as of 11-2-06)

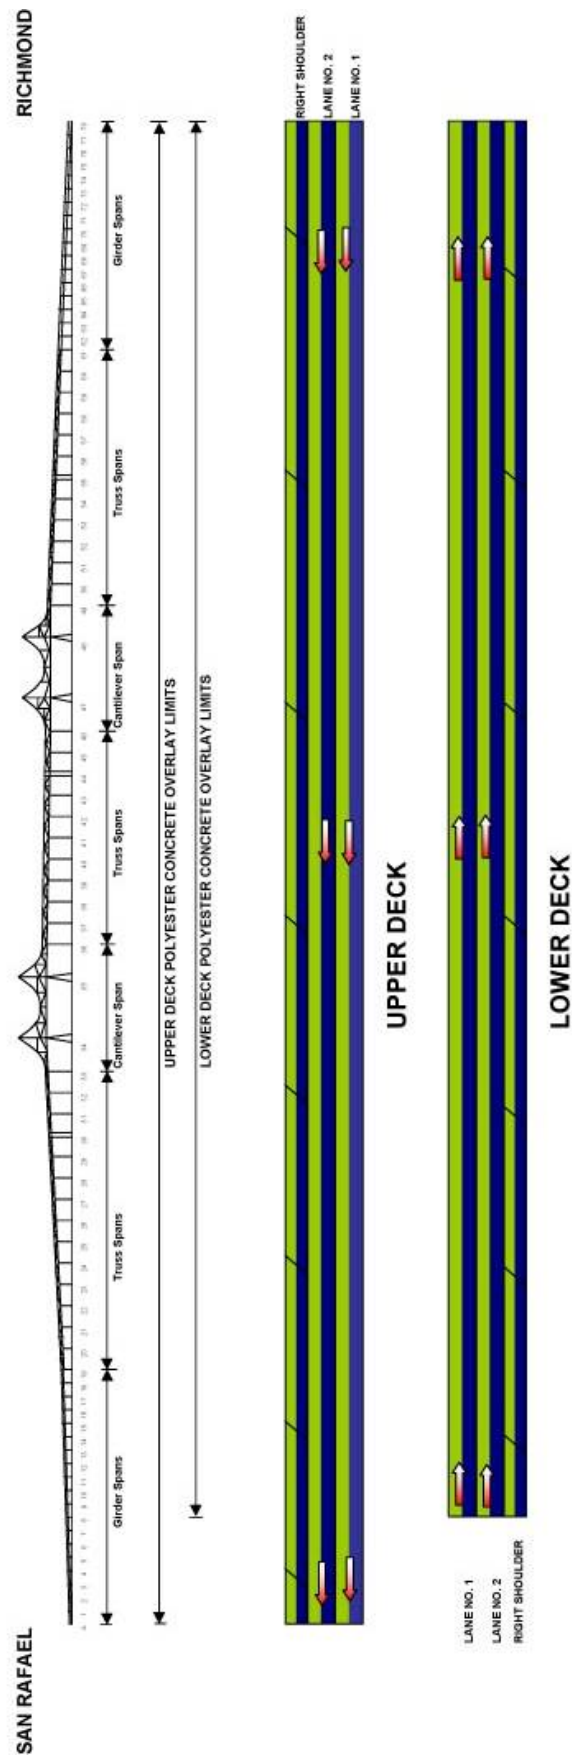

Regional Measure 1 Program

Interstate 880/State Route 92 Interchange Reconstruction Project

Project Description: Modify the existing cloverleaf interchange to increase capacity and improve safety and traffic operations.

Interstate 880/State Route 92 Interchange Cost Summary (\$Millions)

Contract	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	B	c	d = b + c	e	f	g = f - d
I-880/SR-92 Interchange Improvement						
Capital Outlay Support	28.8	-	28.8	30.3	51.7	22.9
Capital Outlay Construction	94.8	-	94.8	-	122.5	27.7
Capital Outlay Right-of-Way	9.9	-	9.9	8.1	12.4	2.5
Project Reserve	0.3	-	0.3	-	9.7	9.4
TOTAL	133.8	-	133.8	38.4	196.3	62.5

Note: Details may not sum to totals due to rounding effects. \$9.6 million in ACTA funds included under Capital Outlay Construction. \$3.7 million included in Capital Outlay Construction for separate landscape contract.

Interstate 880/State Route 92 Interchange Schedule Summary

Project	BATA Project Completion Baseline (07/2005)	Approved Changes (Months)	Project Complete Current Approved Schedule (11/2006)	Contract Complete Schedule Forecast (11/2006)	Schedule Variance (Months)
I-880/SR-92 Interchange Reconstruction	December 2010	-	December 2010	June 2011	7

Project Status: Formal Risk Advertisement was approved by Caltrans. Risk Advertisement is scheduled for January 8, 2007. Bid opening scheduled for April 11, 2007. PS&E was approved by Caltrans at the end October 2006. Formal Risk Advertisement approval by Caltrans is expected to occur in December 2006, pending approval of the construction capital fund allocation plan. It is proposed to allocate the construction funds after the bids are opened. Risk Advertisement target date is early December 2006. Right-of-way acquisition is still in progress. Outstanding parcels include the Union Pacific Railroad parcel, a gas station parcel at Route 92 and Santa Clara St., and the parcels affected by the utility underground along Lindenwood Way. Right of way certification target date is early April 2007. Bids would open shortly afterwards, at which time BATA will take budget update actions as needed. Begin construction target date is June 2007. Construction duration is expected to be four (4) years.

Project Issues:

Issue	Mitigating Action
The forecast schedule included an aggressive schedule for right-of-way acquisition that provided for 18 months to clear numerous parcels in the project area. Additional time will be required to negotiate with parcel owners and the railroad complete property acquisition.	Delays in right-of-way acquisitions are impacting the advertisement and construction of the project. BATA and Caltrans are reviewing methods to accelerate the right-of-way procurement and begin the project. Also, the construction contract will be advertised with an A+B specification, which could reduce the construction duration and partially recover the project schedule.
Bids received on the I-238 Widening contract indicates that the construction estimate may be higher than currently forecasted, from \$196.3 million to \$216.8 million.	Caltrans and BATA will perform a further in-depth review of the estimated costs of major contract items.

Regional Measure 1 Program

Other Completed Regional Measure 1 (RM1) Projects

Summary Description: Other completed Regional Measure 1 projects are the following: (a) Widen the San Mateo-Hayward Bridge along its low-trestle section and its eastern approach, (b) Widen the Bayfront Expressway (SR 84) from the Dumbarton Bridge to the U.S. 101/Marsh Road interchange, (c) Construct an eastern approach (Richmond Parkway) between the Richmond-San Rafael Bridge and Interstate 80 near Pinole, and (d) Modify the U.S. 101/University Avenue interchange, (e) Richmond-San Rafael Bridge Trestle, Fender, and Deck Joint Rehabilitation Project.

Other Completed RM1 Projects Cost Summary (\$Millions)


Contract	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	Variance
a	B	c	d = b + c	e	f	g = f - d
San Mateo-Hayward Bridge Widening Project	217.8	-	217.8	208.6	211.9	(5.9)
Bayfront Expressway Widening Project	36.1	-	36.1	33.2	36.1	-
Richmond Parkway Project	5.9	-	5.9	3.9	5.9	-
U.S. 101/University Interchange	3.8	-	3.8	3.7	3.8	-
RSR Trestle, Fender, and Joint Rehabilitation	102.1	-	102.1	79.9	97.1	(5.0)
TOTAL	365.7	-	365.7	329.3	354.8	(10.9)

Schedule Summary

Project	Actual Project Completion Date
Richmond Parkway Project	May 2001
San Mateo-Hayward Bridge Widening Project	February 2003
Bayfront Expressway Widening Project	January 2004
U.S. 101/University Interchange	April 2004
Richmond-San Rafael Bridge Trestle, Fender, and Deck Joint Rehabilitation	August 2005

Project Status: Construction has been completed on the above listed contracts.

Project Issues: None.

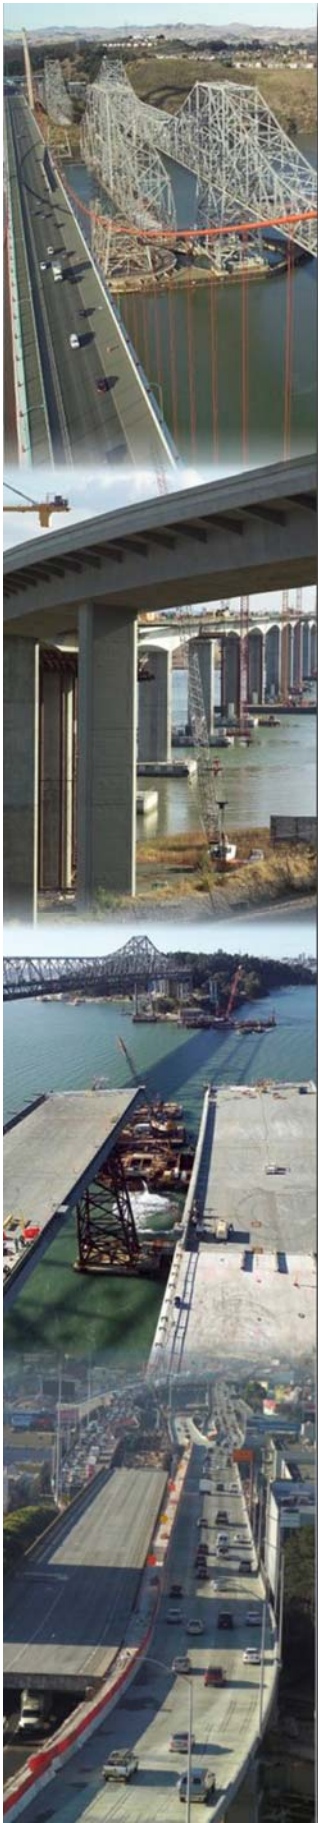

APPENDICES

- A** Toll Bridge Seismic Retrofit Program:
San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project Cost Detail
- B** Toll Bridge Seismic Retrofit Program Cost Detail
- C** Toll Bridge Seismic Retrofit Program Summary Schedule
- D** Regional Measure 1 Program Cost Detail
- E** Regional Measure 1 Program Summary Schedule

** Cost forecasts shown herein are as of June 30, 2006. Forecasts for the Monthly Reports are generally updated on a quarterly basis in conjunction with Risk Analysis assessments for the TBSRP Projects and the TBSRP Quarterly Reports.*

Appendix A: Toll Bridge Seismic Retrofit Program (\$Millions)

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project Cost Detail

Contract	EA Number	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	At-Completion Variance
a	b	c	d	e = c + d	f	g	h = g - e
San Francisco-Oakland Bay Bridge East Span Replacement Project							
East Span - Skyway	01202X						
Capital Outlay Support		197.0	-	197.0	152.1	197.0	-
Capital Outlay Construction		1,293.0	-	1,293.0	1,107.5	1,293.0	-
Total		1,490.0	-	1,490.0	1,259.6	1,490.0	-
East Span - SAS Superstructure	0120FX						
Capital Outlay Support		214.6	-	214.6	26.8	214.6	-
Capital Outlay Construction		1,753.7	-	1,753.7	211.2	1,767.4	13.7
Total		1,968.3	-	1,968.3	238.0	1,982.0	13.7
East Span - SAS E2/T1 Foundations	0120EX						
Capital Outlay Support		52.5	-	52.5	16.3	52.5	-
Capital Outlay Construction		313.5	-	313.5	187.2	313.5	-
Total		366.0	-	366.0	203.5	366.0	-
SAS W2 Foundations	0120CX						
Capital Outlay Support		10.0	-	10.0	9.2	10.0	-
Capital Outlay Construction		26.4	-	26.4	25.2	26.4	-
Total		36.4	-	36.4	34.4	36.4	-
YBI Transition Structures	0120PX						
Capital Outlay Support		78.7	-	78.7	11.5	78.7	-
Capital Outlay Construction		299.3	-	299.3	-	318.5	19.2
Total		378.0	-	378.0	11.5	397.2	19.2
Oakland Touchdown (see notes below)	01204X						
Capital Outlay Support		74.4	-	74.4	22.8	92.1	17.7
Capital Outlay Construction		283.8	-	283.8	-	302.5	18.7
Total		358.2	-	358.2	22.8	394.6	36.4
* OTD Submarine Cable	0120K4						
Capital Outlay Support					0.3	3.0	
Capital Outlay Construction					-	9.6	
Total					0.3	12.6	
* OTD No. 1 (Westbound)	0120L4						
Capital Outlay Support					2.5	49.9	
Capital Outlay Construction					-	226.5	
Total					2.5	276.4	
* OTD No. 2 (Eastbound)	0120M4						
Capital Outlay Support					0.2	15.8	
Capital Outlay Construction					-	62.0	
Total					0.2	77.8	
* OTD Electrical Systems	0120N4						
Capital Outlay Support					-	1.4	
Capital Outlay Construction					-	4.4	
Total					-	5.8	

Notes: Oakland Touchdown Cost-to-Date and Cost Forecast includes prior-to-split Capital Outlay Support Costs.

Note: Details may not sum to totals due to rounding effects.

Appendix A: Toll Bridge Seismic Retrofit Program (\$Millions)

San Francisco-Oakland Bay Bridge (SFOBB) East Span Replacement Project Cost Detail (Cont'd.)

Contract	EA Number	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	At-Completion Variance
a	b	c	d	e = c + d	f	g	h = g - e
YBI South/South Detour	0120RX						
Capital Outlay Support		29.5	-	29.5	17.5	29.5	-
Capital Outlay Construction		131.9	-	131.9	36.6	152.2	20.3
Total		161.4	-	161.4	54.1	181.7	20.3
Existing Bridge Demolition	01209X						
Capital Outlay Support		79.7	-	79.7	0.2	79.7	-
Capital Outlay Construction		239.2	-	239.2	-	222.0	(17.2)
Total		318.9	-	318.9	0.2	301.7	(17.2)
YBI/SAS Archeology	01207X						
Capital Outlay Support		1.1	-	1.1	1.1	1.1	-
Capital Outlay Construction		1.1	-	1.1	1.1	1.1	-
Total		2.2	-	2.2	2.2	2.2	-
YBI - USCG Road Relocation	0120QX						
Capital Outlay Support		3.0	-	3.0	2.7	3.0	-
Capital Outlay Construction		3.0	-	3.0	2.8	3.0	-
Total		6.0	-	6.0	5.5	6.0	-
YBI - Substation and Viaduct	0120GX						
Capital Outlay Support		6.5	-	6.5	6.4	6.5	-
Capital Outlay Construction		11.6	-	11.6	11.3	11.6	-
Total		18.1	-	18.1	17.7	18.1	-
Oakland Geofill	01205X						
Capital Outlay Support		2.5	-	2.5	2.5	2.5	-
Capital Outlay Construction		8.2	-	8.2	8.2	8.2	-
Total		10.7	-	10.7	10.7	10.7	-
Pile Installation Demonstration Project	01208X						
Capital Outlay Support		1.8	-	1.8	1.8	1.8	-
Capital Outlay Construction		9.2	-	9.2	9.2	9.2	-
Total		11.0	-	11.0	11.0	11.0	-
Stormwater Treatment Measures	0120JX						
Capital Outlay Support		6.0	-	6.0	5.7	6.0	-
Capital Outlay Construction		15.0	-	15.0	4.4	15.0	-
Total		21.0	-	21.0	10.1	21.0	-
Right-of-Way and Environmental Mitigation	0120X9						
Capital Outlay Support		-	-	-	-	-	-
Capital Outlay & Right-of-Way		72.4	-	72.4	38.8	72.4	-
Total		72.4	-	72.4	38.8	72.4	-
	04343X & 04300X						
Sunk Cost - Existing East Span Retrofit							
Capital Outlay Support		39.5	-	39.5	39.5	39.5	-
Capital Outlay Construction		30.8	-	30.8	30.8	30.8	-
Total		70.3	-	70.3	70.3	70.3	-
Other Capital Outlay Support							
Environmental Phase		97.7	-	97.7	97.7	97.7	-
Pre-Split Project Expenditures		44.9	-	44.9	44.9	44.9	-
Non-project Specific Costs		20.0	-	20.0	3.2	20.0	-
Total		162.6	-	162.6	145.8	162.6	-
Subtotal Capital Outlay Support		959.4	-	959.4	461.9	977.1	17.7
Subtotal Capital Outlay Construction		4,492.1	-	4,492.1	1,674.3	4,546.8	54.7
Other Budgeted Capital		35.1	-	35.1	0.6	11.0	(24.1)
Total SFOBB East Span Replacement Project		5,486.6	-	5,486.6	2,136.8	5,534.9	48.3


Note: Details may not sum to totals due to rounding effects.

Appendix B: Toll Bridge Seismic Retrofit Program Cost Detail (\$Millions)

Contract	AB 144 / SB 66 Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	At-Completion Variance
a	c	d	e = c + d	f	g	h = g - e
SFOBB East Span Replacement Project						
Capital Outlay Support	959.3	-	959.3	461.9	977.1	17.8
Capital Outlay Construction	4,492.2	-	4,492.2	1,674.3	4,546.8	54.6
Other Budgeted Capital	35.1	-	35.1	0.6	11.0	(24.1)
Total	5,486.6	-	5,486.6	2,136.8	5,534.9	48.3
SFOBB West Approach Replacement						
Capital Outlay Support	120.0	-	120.0	86.0	120.0	-
Capital Outlay Construction	309.0	-	309.0	218.8	309.0	-
Total	429.0	-	429.0	304.8	429.0	-
SFOBB West Span Retrofit						
Capital Outlay Support	75.0	-	75.0	74.8	75.0	-
Capital Outlay Construction	232.9	-	232.9	226.2	232.9	-
Total	307.9	-	307.9	301.0	307.9	-
Richmond-San Rafael Bridge Retrofit						
Capital Outlay Support	134.0	(7.0)	127.0	125.6	127.0	-
Capital Outlay Construction & Right-of-Way	780.0	(82.0)	698.0	665.6	698.0	-
Total	914.0	(89.0)	825.0	791.2	825.0	-
Benicia-Martinez Bridge Retrofit						
Capital Outlay Support	38.1	-	38.1	38.1	38.1	-
Capital Outlay Construction	139.7	-	139.7	139.7	139.7	-
Total	177.8	-	177.8	177.8	177.8	-
Carquinez Bridge Retrofit						
Capital Outlay Support	28.7	-	28.7	28.8	28.7	-
Capital Outlay Construction	85.5	-	85.5	85.4	85.5	-
Total	114.2	-	114.2	114.2	114.2	-
San Mateo-Hayward Bridge Retrofit						
Capital Outlay Support	28.1	-	28.1	28.1	28.1	-
Capital Outlay Construction	135.4	-	135.4	135.3	135.4	-
Total	163.5	-	163.5	163.4	163.5	-
Vincent Thomas Bridge Retrofit (Los Angeles)						
Capital Outlay Support	16.4	-	16.4	16.4	16.4	-
Capital Outlay Construction	42.1	-	42.1	42.0	42.1	-
Total	58.5	-	58.5	58.4	58.5	-
San Diego-Coronado Bridge Retrofit						
Capital Outlay Support	33.5	-	33.5	33.2	33.5	-
Capital Outlay Construction	70.0	-	70.0	69.4	70.0	-
Total	103.5	-	103.5	102.6	103.5	-
Subtotal Capital Outlay Support	1,433.1	(7.0)	1,426.1	892.9	1,443.9	17.8
Subtotal Capital Outlay	6,286.8	(82.0)	6,204.8	3,256.7	6,259.4	54.6
Subtotal Other Budgeted Capital	35.1	-	35.1	0.6	11.0	(24.1)
Miscellaneous Program Costs	30.0	-	30.0	24.5	30.0	-
Subtotal Toll Bridge Seismic Retrofit Program	7,785.0	(89.0)	7,696.0	4,174.7	7,744.3	48.3
Program Contingency	900.0	89.0	989.0	-	940.7	(48.3)
Total Toll Bridge Seismic Retrofit Program	8,685.0	-	8,685.0	4,174.7	8,685.0	-

Note: Details may not sum to totals due to rounding effects.

Appendix C: Toll Bridge Seismic Retrofit Program Summary Schedule

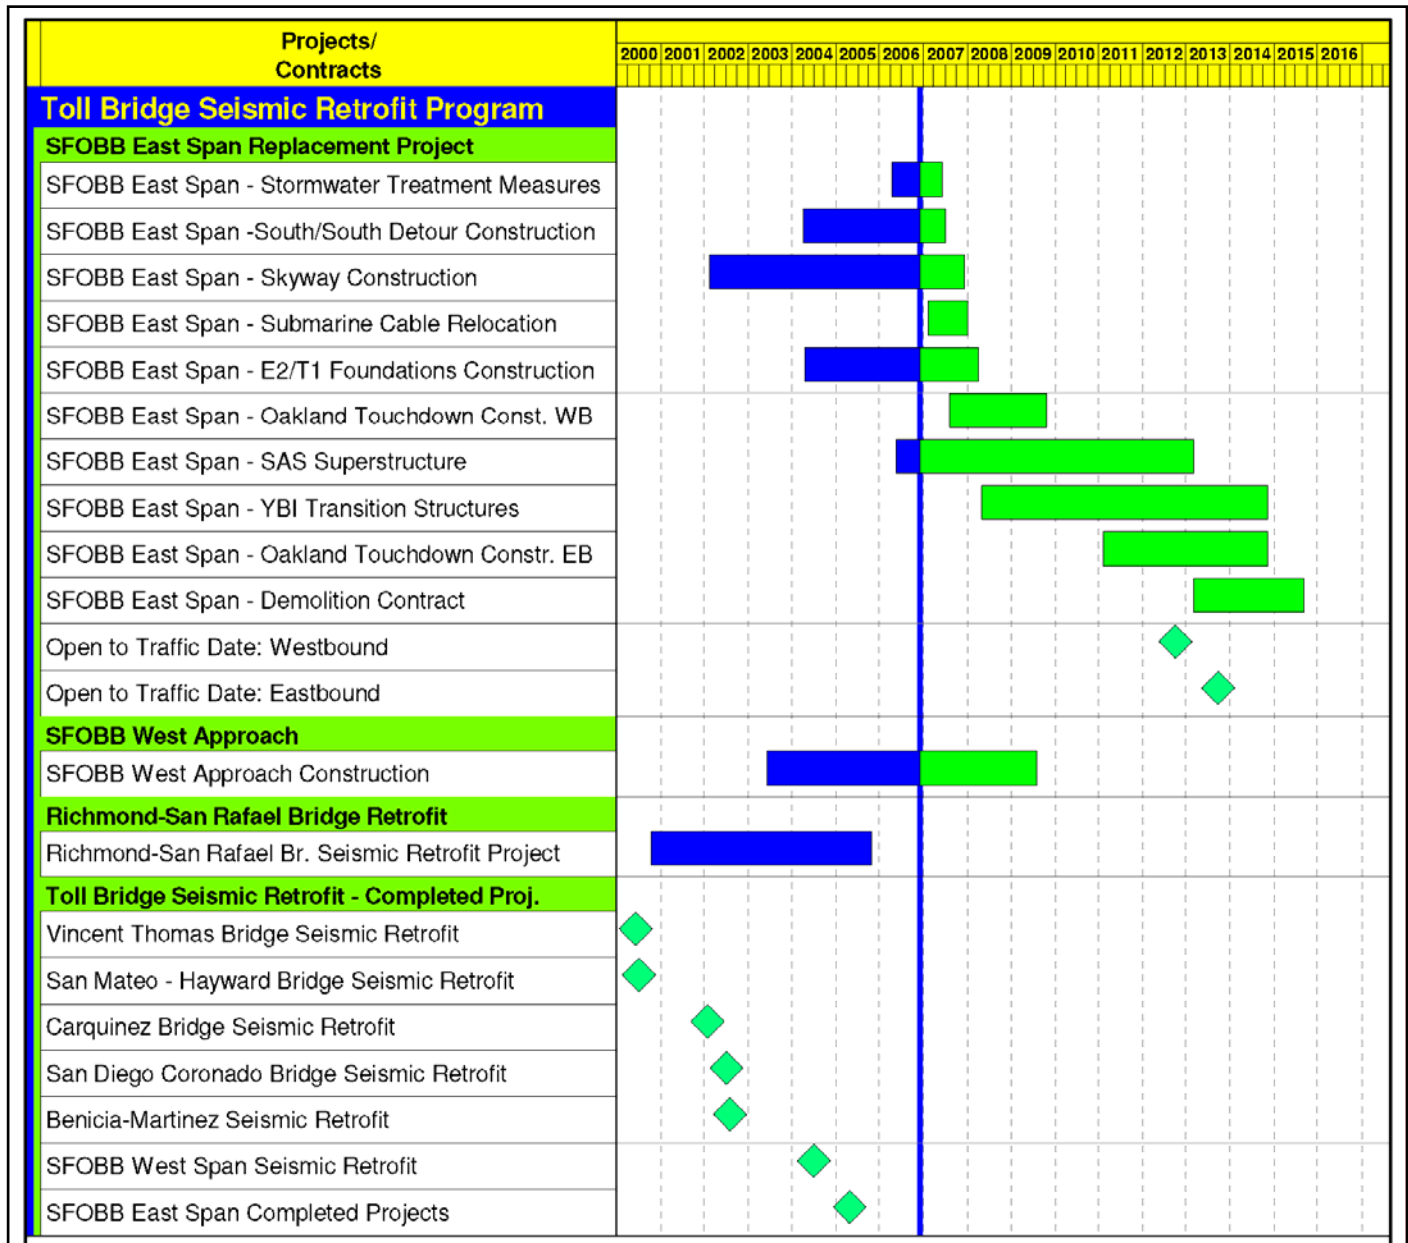

Appendix D: Regional Measure 1 Program Cost Detail (\$Millions)

Project	EA Number	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	At-Completion Variance
a	b	c	d	e = c + d	f	g	h = g - e
New Benicia-Martinez Bridge Project							
New Bridge	00603_						
Capital Outlay Support		84.9	7.7	92.6	81.1	92.6	-
Capital Outlay Construction				-			-
BATA Funding		661.9	107.3	769.2	698.1	769.2	-
Non-BATA Funding		10.1	-	10.1	13.9	10.1	-
Subtotal		672.0	107.3	779.3	712.0	779.3	-
Total		756.9	115.0	871.9	793.1	871.9	-
I-680/I-780 Interchange Reconstruction							
I-680/I-780 Interchange Reconstruction	00606_						
Capital Outlay Support							
BATA Funding		24.9	4.0	28.9	27.9	28.9	-
Non-BATA Funding		1.4	5.1	6.5	5.5	6.5	-
Subtotal		26.3	9.1	35.4	33.4	35.4	-
Capital Outlay Construction							
BATA Funding		54.7	16.1	70.8	67.5	70.8	-
Non-BATA Funding		21.6	-	21.6	15.4	21.6	-
Subtotal		76.3	16.1	92.4	82.9	92.4	-
Total		102.6	25.2	127.8	116.3	127.8	-
I-680/Marina Vista Interchange Reconstruction							
I-680/Marina Vista Interchange Reconstruction	00605_						
Capital Outlay Support		18.3	1.2	19.5	19.6	19.5	-
Capital Outlay Construction		51.5	8.1	59.6	54.7	59.6	-
Total		69.8	9.3	79.1	74.3	79.1	-
New Toll Plaza and Administration Building							
New Toll Plaza and Administration Building	00604_						
Capital Outlay Support		11.9	3.3	15.2	14.8	15.2	-
Capital Outlay Construction		24.3	2.0	26.3	22.6	26.3	-
Total		36.2	5.3	41.5	37.4	41.5	-
Existing Bridge & Interchange Modifications							
Existing Bridge & Interchange Modifications	0060A_						
Capital Outlay Support		4.3	5.7	10.0	5.5	10.0	-
Capital Outlay Construction		17.2	10.9	28.1	-	28.1	-
Total		21.5	16.6	38.1	5.5	38.1	-
Other Contracts							
Other Contracts	See note below						
Capital Outlay Support		11.4	(2.3)	9.1	6.3	9.1	-
Capital Outlay Construction		20.3	(1.3)	19.0	15.2	19.0	-
Capital Outlay Right-of-Way		20.4	(0.1)	20.3	12.3	20.3	-
Total		52.1	(3.7)	48.4	33.8	48.4	-
Subtotal BATA Capital Outlay Support		155.7	19.7	175.3	155.2	175.3	-
Subtotal BATA Capital Outlay Construction		829.9	143.1	973.0	858.1	973.0	-
Subtotal Capital Outlay Right-of-Way		20.4	(0.1)	20.3	12.3	20.3	-
Subtotal Non-BATA Capital Outlay Support		1.4	5.1	6.5	5.5	6.5	-
Subtotal Non-BATA Capital Outlay Construction		31.7	-	31.7	29.3	31.7	-
Project Reserves		20.8	35.3	56.2	-	56.2	-
Total New Benicia-Martinez Bridge Project		1,059.9	203.1	1,263.0	1,060.4	1,263.0	-

Notes:

Includes EA's 00601_, 00608_, 00609_, 0060A_, 0060C_, 0060E_, 0060F_, 0060G_, and 0060H_ and all Project Right-of-Way

Note: Details may not sum to totals due to rounding effects.

Appendix D: Regional Measure 1 Program Cost Detail (\$Millions) (Cont'd.)

Project	EA Number	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	At-Completion Variance
a	b	c	d	e = c + d	f	g	h = g - e
Carquinez Bridge Replacement Project							
New Bridge	01301_						
Capital Outlay Support		60.5	(0.3)	60.2	60.1	60.2	-
Capital Outlay Construction		253.3	4.0	257.3	256.9	257.3	-
Total		313.8	3.7	317.5	317.0	317.5	-
Crockett Interchange Reconstruction	01305_						
Capital Outlay Support		32.0	(0.1)	31.9	31.9	31.9	-
Capital Outlay Construction		73.9	-	73.9	71.9	73.9	-
Total		105.9	(0.1)	105.8	103.8	105.8	-
Existing 1927 Bridge Demolition	01309_						
Capital Outlay Support		16.1	-	16.1	10.9	16.0	(0.1)
Capital Outlay Construction		35.2	-	35.2	21.7	35.2	-
Total		51.3	-	51.3	32.6	51.2	(0.1)
Other Contracts	See note below						
Capital Outlay Support		15.8	(0.7)	15.1	14.7	15.1	-
Capital Outlay Construction		18.8	(0.7)	18.1	15.3	17.9	(0.2)
Capital Outlay Right-of-Way		10.5	-	10.5	9.9	10.5	-
Total		45.1	(1.4)	43.7	39.9	43.5	(0.2)
Subtotal BATA Capital Outlay Support		124.4	(1.1)	123.3	117.6	123.2	(0.1)
Subtotal BATA Capital Outlay Construction		381.2	3.3	384.5	365.8	384.3	(0.2)
Subtotal Capital Outlay Right-of-Way		10.5	-	10.5	9.9	10.5	-
Project Reserves		12.1	(2.2)	9.9	-	10.2	0.3
Total Carquinez Bridge Replacement Project		528.2	-	528.2	493.3	528.2	-

Notes:

Other Contracts includes EA's 01302_, 01303_, 01304_, 01306_, 01307_, 01308_, 0130A_, 0130C_, 0130D_, 0130F_, 0130G_, 0130H_, 0130J_, 00453_, 00493_, 04700_, 00607_, 2A270_, and 29920_ and all Project Right-of-Way


Note: Details may not sum to totals due to rounding effects.

Appendix D: Regional Measure 1 Program Cost Detail (\$Millions) (Cont'd.)

Project	EA Number	BATA Budget (07/2005)	Approved Changes	Current Approved Budget (11/2006)	Cost To Date (11/2006)	Cost Forecast (11/2006)	At-Completion Variance
a	b	c	d	e = c + d	f	g	h = g - e
Richmond-San Rafael Bridge Trestle, Fender, and Deck							
Joint Rehabilitation	See note ¹ below						
Capital Outlay Support							
BATA Funding		2.2	-	2.2	1.4	2.2	-
Non-BATA Funding		8.6	-	8.6	10.4	10.4	1.8
Subtotal		10.8	-	10.8	11.8	12.6	1.8
Capital Outlay Construction							
BATA Funding		40.2	-	40.2	33.4	33.4	(6.8)
Non-BATA Funding		51.1	-	51.1	34.7	51.1	-
Subtotal		91.3	-	91.3	68.1	84.5	(6.8)
Project Reserves		-	-	-	-	-	-
Total		102.1	-	102.1	79.9	97.1	(5.0)
Richmond-San Rafael Bridge Deck Overlay							
Rehabilitation	0415U_						
Capital Outlay Support							
BATA Funding		4.0	0.5	4.5	2.9	4.5	-
Non-BATA Funding		4.0	(4.0)	-	-	-	-
Subtotal		8.0	(3.5)	4.5	2.9	4.5	-
Capital Outlay Construction		16.9	3.6	20.5	14.4	20.5	-
Project Reserves		0.1	(0.1)	-	-	-	-
Total		25.0	-	25.0	17.3	25.0	-
Richmond Parkway Project (RM 1 Share Only)							
Non-Caltrans							
Capital Outlay Support		-	-	-	-	-	-
Capital Outlay Construction		5.9	-	5.9	3.9	5.9	-
Total		5.9	-	5.9	3.9	5.9	-
San Mateo-Hayward Bridge Widening							
See note ² below							
Capital Outlay Support		34.6	(0.2)	34.4	34.1	34.4	-
Capital Outlay Construction		180.2	(1.1)	179.1	174.0	176.2	(2.9)
Capital Outlay Right-of-Way		1.5	-	1.5	0.5	0.6	(0.9)
Project Reserves		1.5	1.3	2.8	-	0.7	(2.1)
Total		217.8	-	217.8	208.6	211.9	(5.9)
I-880/SR-92 Interchange Reconstruction							
EA's 23317_, 01601_, and 01602_							
Capital Outlay Support		28.8	-	28.8	30.3	51.7	22.9
Capital Outlay Construction							
BATA Funding		85.2	-	85.2	-	112.9	27.7
Non-BATA Funding		9.6	-	9.6	-	9.6	-
Subtotal		94.8	-	94.8	-	122.5	27.7
Capital Outlay Right-of-Way		9.9	-	9.9	8.1	12.4	2.5
Project Reserves		0.3	-	0.3	-	9.7	9.4
Total		133.8	-	133.8	38.4	196.3	62.5
Bayfront Expressway Widening							
EA's 00487_, 01511_, and 01512_							
Capital Outlay Support		8.6	(0.3)	8.3	8.1	8.3	-
Capital Outlay Construction		26.5	-	26.5	24.9	26.5	-
Capital Outlay Right-of-Way		0.2	-	0.2	0.2	0.2	-
Project Reserves		0.8	0.3	1.1	-	1.1	-
Total		36.1	-	36.1	33.2	36.1	-
US 101/University Avenue Interchange Modification							
Non-Caltrans							
Capital Outlay Support		-	-	-	-	-	-
Capital Outlay Construction		3.8	-	3.8	3.7	3.8	-
Total		3.8	-	3.8	3.7	3.8	-
Subtotal BATA Capital Outlay Support		358.3	18.6	376.8	349.6	399.6	22.8
Subtotal BATA Capital Outlay Construction		1,569.8	148.9	1,718.7	1,478.2	1,736.5	17.8
Subtotal Capital Outlay Right-of-Way		42.5	(0.1)	42.4	31.0	44.0	1.6
Subtotal Non-BATA Capital Outlay Support		14.0	1.1	15.1	15.9	16.9	1.8
Subtotal Non-BATA Capital Outlay Construction		92.4	-	92.4	64.0	92.4	-
Project Reserves		35.6	34.6	70.3	-	77.9	7.6
Total RM1 Program		2,112.6	203.1	2,315.7	1,938.7	2,367.3	51.6

Note: Details may not sum to totals due to rounding effects.

Appendix E: Regional Measure 1 Program Summary Schedule

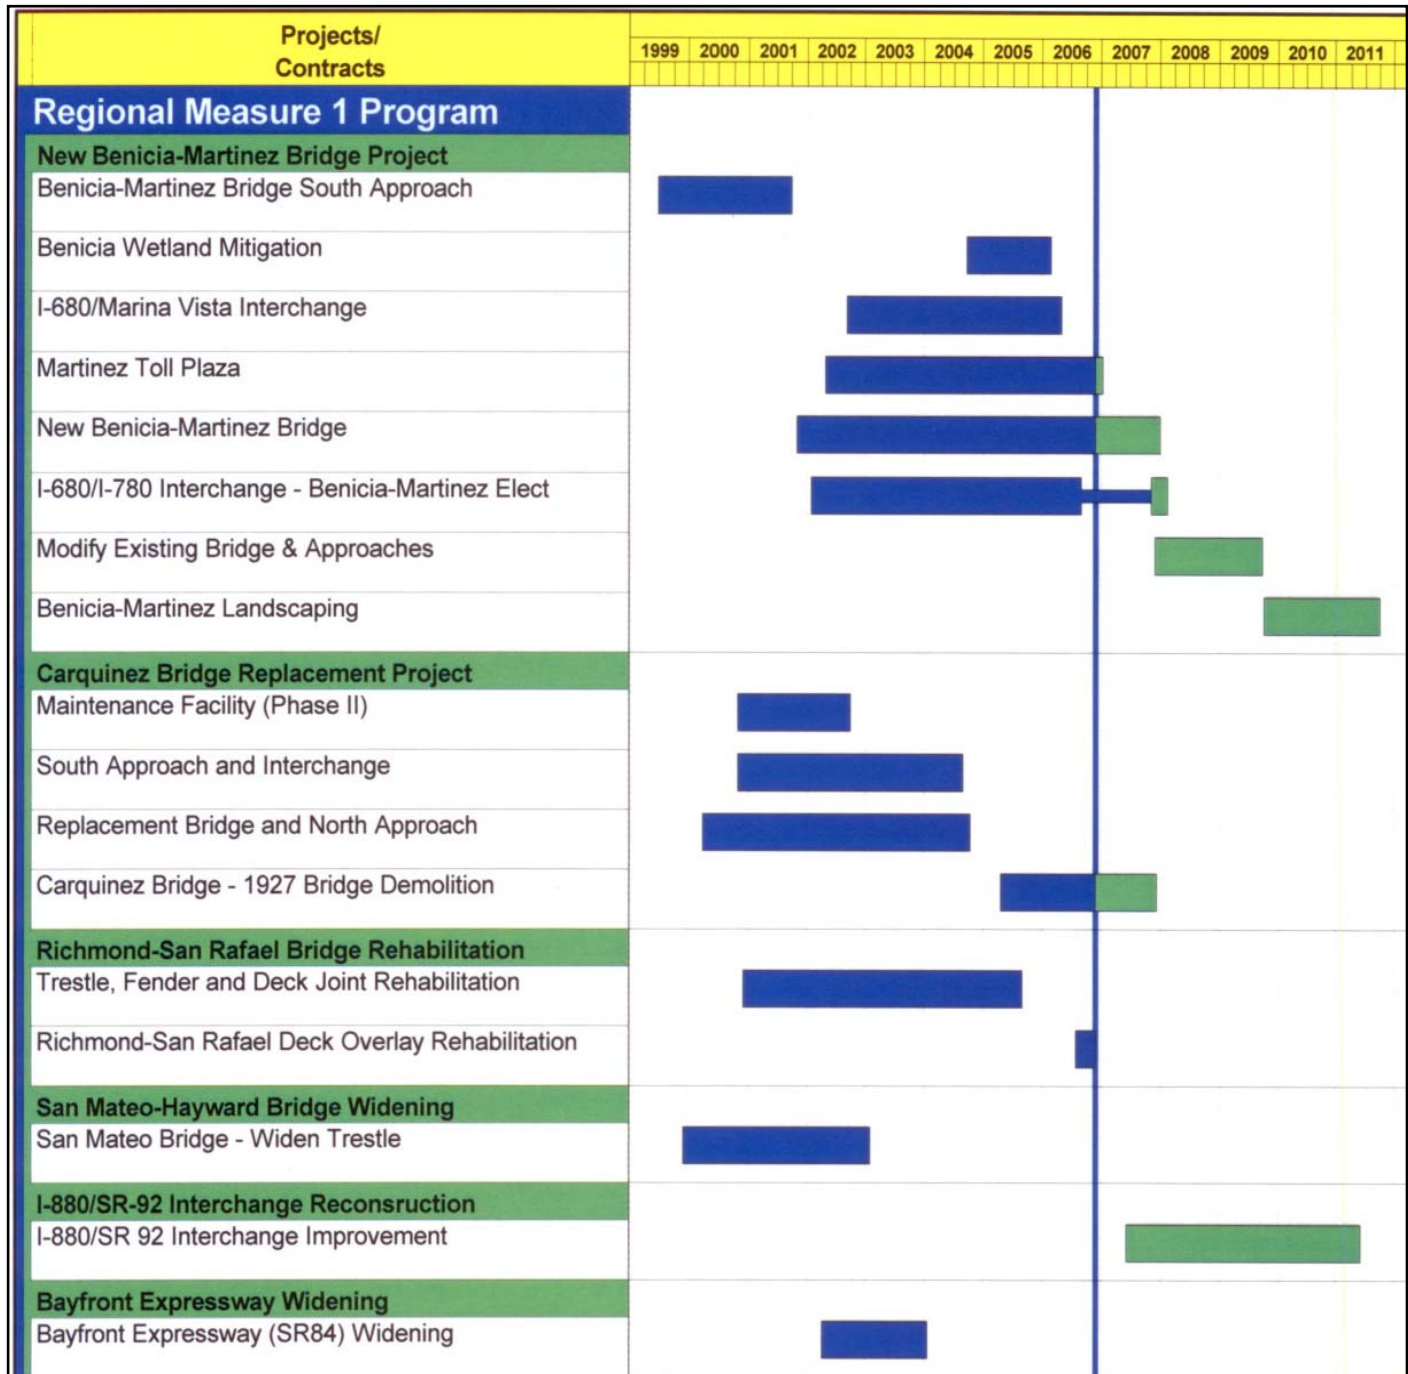

Appendix F: Glossary of Terms

AB144/SB 66 BUDGET: the planned allocation of resources for the Toll Bridge Seismic Retrofit Program, or subordinate projects or contracts, as provided in Assembly Bill 144 and Senate Bill 66, signed into law by Governor Schwarzenegger on July 18, 2005 and September 29, 2005, respectively.

BATA BUDGET: the planned allocation of resources for the Regional Measure 1 Program, or subordinate projects or contracts as authorized by the Bay Area Toll Authority as of June 2005.

APPROVED CHANGES: for cost, changes to the AB144/SB 66 Budget or BATA Budget as approved by the Bay Area Toll Authority Commission. For schedule, changes to the AB 144/SB 66 Project Complete Baseline approved by the Toll Bridge Program Oversight Committee, or changes to the BATA Project Complete Baseline approved by the Bay Area Toll Authority Commission.

CURRENT APPROVED BUDGET: the sum of the AB144/SB66 Budget or BATA Budget and Approved Changes.

COST TO DATE: the actual expenditures incurred by the program, project, or contract as of the month and year shown.

COST FORECAST: the current forecast of all of the costs that are projected to be expended so as to complete the given scope of the program, project, or contract.

AT COMPLETION VARIANCE or VARIANCE (cost): the mathematical difference between the Cost Forecast and the Current Approved Budget.

AB 144/SB 66 PROJECT COMPLETE BASELINE: the planned completion date for the Toll Bridge Seismic Retrofit Program or subordinate projects or contracts.

BATA PROJECT COMPLETE BASELINE: the planned completion date for the Regional Measure 1 Program or subordinate projects or contracts.

PROJECT COMPLETE CURRENT APPROVED SCHEDULE: the sum of the AB144/SB66 Project Complete Baseline or BATA Project Complete Baseline and Approved Changes.

PROJECT COMPLETE SCHEDULE FORECAST: the current projected date for the completion of the program, project, or contract.

SCHEDULE VARIANCE or VARIANCE (schedule): the mathematical difference expressed in months between the Project Complete Schedule Forecast and the Project Complete Current Approved Schedule.

The following information is provided in accordance with California Government code Section 7550:

This document is one of a series of reports prepared for the Bay Area Toll Authority (BATA)/Metropolitan Transportation Commission (MTC) for the Toll Bridge Seismic Retrofit and Regional Measure 1 Programs. The contract value for the monitoring efforts, technical analysis, and field site works that contribute to these reports, as well as the report preparation and production, is \$1,574,873.

**This Page
Intentionally
Left Blank**
