

# BAY AREA TOLL AUTHORITY

Regional Measure 1  
Toll Bridge Projects

## Project Monitoring Program


DECEMBER 2002 PROGRESS REPORT



Metropolitan Transportation  
Commission

Bay Area Toll Authority

Released January 2003



# Bay Area Toll Authority/Metropolitan Transportation Commission

## *Commission Roster*

**Sharon J. Brown**, MTC Chair  
Cities of Contra Costa County

**Steve Kinsey**, MTC Vice Chair  
Marin County and Cities

**Tom Ammiano**  
City and County of San Francisco

**Keith Axtell**  
U.S. Department of Housing and  
Urban Development

**James T. Beall Jr.**  
Santa Clara County

**Mark DeSaulnier**  
Contra Costa County

**Bill Dodd**  
Napa County and Cities

**Dorene M. Giacomini**  
U.S. Department of Transportation

**Scott Haggerty**  
Alameda County

**Barbara Kaufman**  
San Francisco Bay Conservation  
and Development Commission

**Sue Lempert**  
Cities of San Mateo County

**John McLemore**  
Cities of Santa Clara County

**Michael Nevin**  
San Mateo County

**Jon Rubin**  
San Francisco Mayor's Appointee

**Bijan Sarpiti**  
State Business, Transportation  
and Housing Agency

**James P. Spering**  
Solano County and Cities

**Pamela Torliatt**  
Association of Bay Area Governments

**Sharon Wright**  
Sonoma County and Cities

**Shelia Young**  
Cities of Alameda County

## *Management Staff*

*Executive Director*

**Steve Heminger**

*Deputy Director, Operations*

**Ann Flemer**

*Deputy Director, Policy*

**Therese McMillan**

*General Counsel*

**Francis Chin**

*Manager of Finance*

**Brian Mayhew**

*Manager of Bridge  
and Highway Operations*

**Rod McMillan**

**For additional information, please contact:**

*Peter Lee, Program Manager, RM-1*

*(510) 817-3206*

*plee@mtc.ca.gov*

# BAY AREA TOLL AUTHORITY

Regional Measure 1  
Toll Bridge Projects

## Project Monitoring Program

DECEMBER 2002 PROGRESS REPORT



*Prepared for*  
Metropolitan Transportation  
Commission

Bay Area Toll Authority

**Joseph P. Bort MetroCenter**  
101 Eighth Street  
Oakland, California 94607  
Tel: 510-464-7700  
TDD/TTY: 510-464-7769  
Fax: 510-464-7848  
E-mail: [info@mtc.ca.gov](mailto:info@mtc.ca.gov)  
Web: [www.mtc.ca.gov](http://www.mtc.ca.gov)



*Prepared by*  
Bechtel Infrastructure Corporation



*The following information is provided in accordance with California Government code Section 7550:*

*This document is one of a series of reports prepared for the Bay Area Toll Authority (BATA)/Metropolitan Transportation Commission (MTC) for the Regional Measure 1 Toll Bridge Program. The contract value for the monitoring efforts, technical analysis, and field site work which contribute to these reports, as well as the report preparation and production, is \$3,068,993.00.*

**TABLE OF CONTENTS**

Regional Measure 1 Toll Bridge Program .....	<b>1</b>
Executive Summary - Status of Regional Measure 1 Projects, and Key Issues and Developments	
Northern Bridge Group .....	<b>2</b>
Southern Bridge Group .....	<b>4</b>
Cost Status Summary .....	<b>6</b>
Schedule Status Summary .....	<b>7</b>
Northern Bridge Group	
New Benicia-Martinez Bridge .....	<b>8</b>
Carquinez Bridge Replacement .....	<b>10</b>
Richmond-San Rafael Bridge Rehabilitation .....	<b>12</b>
Southern Bridge Group	
San Mateo-Hayward Bridge Widening .....	<b>14</b>
I-880/SR-92 Interchange Improvement .....	<b>16</b>
Dumbarton Bridge West Approach Projects .....	<b>18</b>
Appendices	
Appendix A: Project Budget Adjustments .....	<b>A-1</b>
Appendix B: Current Approved Contract Change Orders (CCOs) .....	<b>B-1</b>
Appendix C: Project Cost Summary Details .....	<b>C-1</b>

REGIONAL MEASURE 1 TOLL BRIDGE PROJECTS





## BAY AREA TOLL AUTHORITY

### REGIONAL MEASURE 1 TOLL BRIDGE PROGRAM

In November 1988, Bay Area voters approved Regional Measure 1 (RM 1) and authorized a standard auto toll of \$1 for all seven state-owned Bay Area toll bridges. The additional revenues generated by the toll increase were identified for use for certain highway and bridge improvements, public transit rail extensions, and other projects that reduce congestion on the bridges.

RM 1 identified nine specific bridge and highway improvement projects as eligible for funding from the toll increase. The projects identified by RM 1 and their status of development are depicted in the map on the facing page and can be itemized as follows:

#### *Northern Bridge Group Projects:*

1. Widening of the existing Benicia-Martinez Bridge (completed; not included in this report)
2. Construction of a new bridge parallel to the existing Benicia-Martinez Bridge
3. Replacement of the existing western span of the Carquinez Bridge
4. Major rehabilitation of the existing Richmond-San Rafael Bridge
  - Trestle and fender rehabilitation
  - Deck rehabilitation
5. Construction of an eastern approach (Richmond Parkway) between the Richmond-San Rafael Bridge and Interstate 80 near Pinole (non-Caltrans project)

#### *Southern Bridge Group Projects:*

1. Construction of the West Grand Avenue connector to the San Francisco-Oakland Bay Bridge (completed; not included in this report)
2. Widening of the existing San Mateo-Hayward Bridge and eastern approach to six lanes
3. Improvement of the Interstate 880/State Route 92 interchange
4. Improvements to the western approaches to the Dumbarton Bridge
  - US 101/University Avenue interchange reconstruction (non-Caltrans project; completed)
  - State Route 84 (Bayfront Expressway) widening.

### MTC, BATA, AND THE CALIFORNIA STATE DEPARTMENT OF TRANSPORTATION (CALTRANS)

As the regional transportation planning agency for the San Francisco Bay Area, MTC is responsible for transportation planning, coordinating, and fund programming in the nine counties surrounding the Bay.

With SB 226, MTC, as the Bay Area Toll Authority (BATA), has also assumed certain duties previously held by the California Transportation Commission, including responsibilities for the programming, administration, and allocation of all toll revenues (excluding the seismic surcharge) from the state-owned toll bridges in the Bay Area.







Caltrans continues to be responsible for the ongoing operation of the state-owned bridges, including the collection of tolls, as well as the maintenance, rehabilitation, and capital improvement of the bridges.




### PROJECT MONITORING PROGRAM

This report focuses on monitoring project cost and schedule performance for the Regional Measure 1 Toll Bridge Improvement Projects, as measured against approved budget and schedule milestones. The report provides comprehensive project status information at three levels of detail:

- Color-coded executive summary of Regional Measure 1 projects status (program level)
- Detailed status of individual bridge projects (project level)
- Supplemental project and contract information, including budget adjustments, approved construction change orders, and project and contract level cost data, in the appendices.

**EXECUTIVE SUMMARY – STATUS OF REGIONAL MEASURE 1 PROJECTS**

NORTHERN BRIDGE GROUP	COST	SCHEDULE
New Benicia-Martinez Bridge		
Carquinez Bridge Replacement		
Richmond-San Rafael Bridge Rehabilitation		

- Legend:**
-  Green = no variance to current budget/schedule
  -  Yellow = variance to current budget/schedule (trend), defined as follows:  
 For Cost: Project (BATA) contingency use may be required  
 For Schedule: Construction contract completion dates delayed by greater than 3 months
  -  Red = variance to current budget/schedule, defined as follows:  
 For Cost: Project budget change may be required  
 For Schedule: "New facility open to traffic" date delayed by greater than 3 months by non-weather-related issues



BAY AREA TOLL AUTHORITY







EXECUTIVE SUMMARY – STATUS OF KEY ISSUES AND DEVELOPMENTS




- On the new bridge contract, erection of falsework for the superstructure continues from the south abutment to Pier 3. Pile drilling/excavation is in progress at Pier 6. Wing walls for Abutment 1 are complete.
- Deep-water pile driving for the new bridge continues to be suspended pending resolution of the fish take issue. The current proposed mitigation strategies will impose significant cost and schedule impacts on construction of the bridge and are under evaluation by Caltrans. The cost and schedule status codes for the project are "red" due to this issue.
- On the I-680/I-780 interchange contract, concrete operations continue on pier foundations and columns for the interchange structures. The retaining wall on eastbound 780 is nearing completion. Construction of the retaining wall at the slide area has progressed down to the third level of tiebacks with shoring, tieback installation and excavation underway. Falsework erection has started for the southbound 680 to northbound 780 structure.
- On the toll plaza contract, concrete operations continue for the tunnel stairways. On the Operations Building, steel framing is in place and installation of metal decking has begun.
- The I-680/Marina Vista interchange contract continues with roadway paving on southbound I-680, the Marina Vista on/off ramp, and Waterfront Road. Work continues to create access across utility lines and the railroad track to work areas.

- On the main span contract, compaction and banding of both the east and west main cables is complete. Tensioning of the cable band bolts and installation of suspenders is in progress. Installation of stairs continues on both towers and the north anchorage.
- On the south approach and interchange contract, falsework erection continues for spans 4 - 6. Falsework has been removed for spans 1 - 4. Concrete operations continue on columns for the interchange structures. Subgrade preparation, underdrain installation, backfilling and paving continue on Westbound I-80.
- The maintenance facility is complete.

- On the west trestle replacement, work continues on the following: demolition along the interior of the existing eastbound and westbound trestles; installation of a temporary work trestle; pile installation. Interior pile installation is at Bent 17 of 37 and pile drill out and concrete placement is at Bent 10 of 37. Exterior trestle work is forecast to commence in January 2003.
- The schedule status code for the project is "yellow" while Caltrans reevaluates the scope and schedule of the deck rehabilitation project.

**EXECUTIVE SUMMARY – STATUS OF REGIONAL MEASURE 1 PROJECTS**

SOUTHERN BRIDGE GROUP	COST	SCHEDULE
San Mateo-Hayward Bridge Widening		
I-880/SR-92 Interchange Improvement		
Dumbarton Bridge West Approach Projects (Bayfront Expressway)		

- Legend:**
-  Green = no variance to current budget/schedule
  -  Yellow = variance to current budget/schedule (trend), defined as follows:  
For Cost: Project (BATA) contingency use may be required  
For Schedule: Construction contract completion dates delayed by greater than 3 months
  -  Red = variance to current budget/schedule, defined as follows:  
For Cost: Project budget change may be required  
For Schedule: “New facility open to traffic” date delayed by greater than 3 months by non-weather-related issues

- On the bridge-widening contract, the new westbound trestle opened to traffic on November 4, 2002. The original two westbound lanes are now closed. Removal of the median barrier on the existing trestle and installation of the metering light structure are in progress. When the barrier removal work is complete, the old trestle will carry three eastbound only traffic lanes with shoulders. This work is forecast to be complete in February 2003.
- The mini-toll plaza is complete.
- The pedestrian overcrossing is complete.

- Caltrans is currently responding to the comments received and preparing the Final Environmental Impact Statement Report (EIS/R) for the project. The report is scheduled for completion in mid 2003.
- Based on a preliminary revised cost estimate for the project, Caltrans is reporting that the project cost will exceed the current contract budget and will require the use of project contingency. As a result, a "yellow" cost status code is indicated in the PMP report.

- 5

## COST STATUS SUMMARY (MILLION DOLLARS)

PROJECT	Baseline Budget (June 2000)	Current Budget (Oct 2002)	Current Forecast (Dec 2002)	Expended To Date (7/98 - 11/02)
<i>Northern Bridge Group</i>				
New Benicia-Martinez Bridge	586.0	652.8	652.8	180.0
Carquinez Bridge Replacement	433.2	479.8	479.8	315.8
Richmond-San Rafael Bridge Rehabilitation				
► West Trestle and Fender Rehabilitation	45.4	35.4	35.4	17.2
► Deck Rehabilitation	53.4	53.4	53.4	0.2
Richmond Parkway ( <i>Non-Caltrans</i> ) <sup>1</sup>	5.9	5.9	5.9	2.4
SUBTOTAL – NBG	<b>1,123.9</b>	<b>1,227.2</b>	<b>1,227.2</b>	<b>515.7</b>
<i>Southern Bridge Group</i>				
San Mateo-Hayward Bridge Widening				
► Widening	203.6	217.5	217.5	186.3
► West Approach Replacement Planting	0.3	0.3	0.3	0.0
I-880/SR-92 Interchange Improvement	124.2	134.2	134.2	11.3
Dumbarton Bridge West Approach Projects				
► US-101/University Avenue Interchange Reconstruction ( <i>Non-Caltrans</i> )	3.8	3.8	3.8	3.7
► Bayfront Expressway (SR-84) Widening	33.8	33.8	33.8	19.9
SUBTOTAL – SBG	<b>365.6</b>	<b>389.5</b>	<b>389.5</b>	<b>221.2</b>
<b>GRAND TOTAL</b>	<b>1,489.5</b>	<b>1,616.8</b>	<b>1,616.8</b>	<b>736.9</b>

<sup>1</sup> For the Richmond Parkway, values shown represent the portion funded by BATA.

BAY AREA TOLL AUTHORITY

SCHEDULE STATUS SUMMARY

PROJECT	New Facility Open to Traffic Baseline (June 2000)	New Facility Open to Traffic Current (Oct 2002)	New Facility Open to Traffic Forecast (Dec 2002)
<i>Northern Bridge Group</i>			
New Benicia-Martinez Bridge	Jan 04	Dec 04	TBD
Carquinez Bridge Replacement	Jan 03	Oct 03	Oct 03
Richmond-San Rafael Bridge Rehabilitation			
▶ West Trestle and Fender Rehabilitation <sup>1</sup>	Dec 04	Sep 04	Sep 04
▶ Deck Rehabilitation <sup>1</sup>	Sep 06	Sep 06	Jul 07
Richmond Parkway ( <i>Non-Caltrans</i> ) <sup>2</sup>	Feb 01	May 01	May 01
<i>Southern Bridge Group</i>			
San Mateo-Hayward Bridge Widening			
▶ Widening	Dec 02	Nov 02	Nov 02
▶ West Approach Replacement Planting <sup>1</sup>	May 08	May 08	May 08
I-880/SR-92 Interchange Improvement	Dec 06	Jun 09	Jun 09
Dumbarton Bridge West Approach Projects			
▶ US-101/University Avenue Interchange Reconstruction ( <i>Non-Caltrans</i> ) <sup>1</sup>	Apr 00	Apr 00	Apr 00
▶ Bayfront Expressway (SR-84) Widening <sup>1</sup>	Mar 03	Apr 04	Oct 03

<sup>1</sup> For the Richmond-San Rafael Bridge Rehab, San Mateo-Hayward Bridge West Approach Planting, and Dumbarton Bridge West Approach projects, the dates shown reflect construction completion; the existing facility remains open to traffic during all phases of construction.

<sup>2</sup> The Canal Boulevard realignment was opened to traffic on May 25, 2001.

## NEW BENICIA-MARTINEZ BRIDGE

The existing Benicia-Martinez Bridge provides Interstate 680 access across the Carquinez Strait between Contra Costa and Solano counties. This project will construct a new parallel Benicia-Martinez Bridge east of the existing span that will include the following features:

- Five northbound lanes on the new bridge (four mixed-flow lanes and one slow-vehicle lane) that will allow conversion of the existing bridge to southbound traffic only
- A new bicycle/pedestrian lane on the existing bridge
- A new toll plaza south of the new bridge in Contra Costa County with 17 toll booths, including two high-occupancy-vehicle (HOV) bypass lanes
- Reconstruction of the Interstate 680/Marina Vista Road and Interstate 680/Interstate 780 interchanges

### Project Photos



*I-680 Southbound at I-780*



*Toll Plaza Tunnel Construction*



*New Bridge South Abutment*

### Current Activities:

- On the main span contract, multiple foundation pile and concrete operations continue. Concrete operations are in progress at wing walls on the south abutment. Falsework erection for the superstructure is underway between the south abutment and Pier 3. Pile drilling/excavation continue at Pier 6. Deepwater pile casing cleanout and concrete operations are in progress at Pier 8. On the north temporary trestle, sheet piles are installed at Pier 17 for pile driving and pile cap excavation. SWPPP measures are in place for the rain season.
- Deep-water pile installation for the new bridge is suspended pending resolution of the fish take issue. The proposed mitigation strategies will impose significant construction cost and schedule impacts and are being evaluated by Caltrans.
- On the I-680/I-780 interchange contract, multiple operations are underway along both roadways. On I-780, concrete operations are complete at Retaining Wall 3. Foundation pier drilling, concrete operations and falsework erection continue for the new interchange structures at Park Road and West Arsenal. Construction of Retaining Wall 1 at the slide area continues with the installation of the third level of shoring and tiebacks. Falsework erection has reached from Abutment 15 to Span 13 on the EN line from southbound I-780 to northbound I-680. SWPPP measures are in place for the rain season.
- On the toll plaza contract, structural steel framing is being bolted and welded. Metal decking installation is in progress. Tunnel concrete is complete. Concrete operations continue for the stairs to the tollbooths.
- On the I-680/Marina Vista interchange contract, the baseline construction schedule has been returned by Caltrans for resubmittal by the contractor. Excavation, drain installation and paving are in progress to widen southbound I-680, and to gain access to the work area within the Marina Vista on/off ramp and Waterfront Road. Base rock is being placed over utilities and railroad tracks for the access road. Traffic has been diverted on Waterfront Road to allow for widening. A new cloverleaf loop has been completed from Waterfront Road to northbound I-680.

BAY AREA TOLL AUTHORITY

NEW BENICIA-MARTINEZ BRIDGE

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (Oct 2002)	Current Forecast (Dec 2002)	Variance	Expended to Date (7/98 - 11/02)	Notes
Capital Outlay Construction						
South Approach	6.0	7.0	7.0	0.0	6.4	
New Bridge	247.3	307.5	307.5	0.0	70.4	A
Toll Plaza and Administration Building	22.8	21.4	21.4	0.0	4.4	
I-680/Marina Vista Interchange	43.2	45.1	45.1	0.0	1.4	
I-680/I-780 Interchange	80.8	54.7	54.7	0.0	20.8	
Other Budgeted Capital	28.1	30.0	30.0	0.0	1.7	
Capital Outlay Support	78.2	99.1	99.1	0.0	60.6	
Capital ROW	21.1	14.4	14.4	0.0	11.3	
Non-BATA Funding	0.0	31.0	31.0	0.0	3.1	
Project (BATA) Contingency	58.4	42.5	42.5			
<b>Project Total (a)</b>	<b>586.0</b>	<b>652.8</b>	<b>652.8</b>	<b>0.0</b>	<b>180.0</b>	
(a) Totals may be rounded						

SCHEDULE STATUS	Baseline (June 2000)	Current (Oct 2002)	Forecast (Dec 2002)	Variance	Notes
<b>Construction Contract Completion</b>					
New Bridge	Jan 04	Sep 04	TBD	n.a.	A
Toll Plaza and Administration Building	Feb 03	Sep 04	Sep 04	0	
I-680/Marina Vista Interchange	Dec 03	Nov 04	Dec 04	+1	
I-680/I-780 Interchange	Dec 03	Dec 04	Jan 05	+1	
South Approach	Mar 01	Oct 01	Oct 01	0	
Modify Existing Bridge	Jul 05	Dec 06	Dec 06	0	
<b>Project</b>					
<b>New Facility Open to Traffic</b>	<b>Jan 04</b>	<b>Dec 04</b>	<b>TBD</b>	<b>n.a.</b>	<b>A</b>

NOTES

ACTION

A. The current proposed strategies to mitigate the inadvertent fish takes during pile driving operations will impose significant cost and schedule impacts on construction of the bridge. Construction completion is expected to be delayed 12 to 18 months beyond the current contract completion scheduled for September 2004.

Caltrans is evaluating the strategies and the associated cost and schedule impacts.



## CARQUINEZ BRIDGE REPLACEMENT

The existing Carquinez Bridge carries Interstate 80 traffic between the cities of Vallejo and Crockett on two separate bridges: the 1927 bridge for westbound traffic and the 1958 bridge for eastbound traffic. While the 1958 bridge is being strengthened under Caltrans' seismic retrofit program, the 1927 bridge has been identified as being seismically deficient and will be replaced under the RM 1 program. The Carquinez Bridge replacement project will construct a new suspension bridge west of the existing bridges. The existing 1927 bridge will be demolished after the completion of this project. The project will incorporate the following features:

- Four westbound lanes on the new bridge (three mixed-flow lanes and one HOV lane)
- A new bicycle/pedestrian lane on the new bridge

### Project Photos



*Installation of Suspenders on the Main Cables*



*Westbound I-80*



*South Approach Falsework*

### Current Activities:

- On the replacement bridge and north approach contract, dismantling of spinning equipment and compaction and banding of the cables is complete. Suspenders are being installed. This will be followed by hanging of the deck panels (due for delivery in early 2003). Stairs and landings are being installed in Towers 2 and 3 and the north anchorage. The architectural wall on the north approach is receiving the final finishes.
- On the south approach and interchange contract, falsework is removed for spans 1 - 4 on the Crockett Viaduct; falsework erection continues for spans 4 - 6. Subgrade preparation, underdrains installation, base course and concrete work continue for the D3 line (Westbound I-80). Concrete operations continue on the columns for the westbound and eastbound on/off ramps.
- The maintenance facility is complete.

BAY AREA TOLL AUTHORITY

CARQUINEZ BRIDGE REPLACEMENT

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (Oct 2002)	Current Forecast (Dec 2002)	Variance	Expended to Date (7/98 - 11/02)	Notes
Capital Outlay Construction						
Replacement Bridge and North Approach	213.7	239.2	239.2	0.0	174.4	
South Approach and Interchange	116.0	73.9	73.9	0.0	41.6	
Maintenance Facility (Phases I & II)	7.0	8.1	8.1	0.0	7.7	
1927 Bridge Demolition	16.0	16.0	16.0	0.0	0.0	
Other Budgeted Capital	10.6	11.5	11.5	0.0	6.3	
Capital Outlay Support	43.7	102.9	102.9	0.0	76.6	
Capital ROW	9.6	11.1	11.1	0.0	9.3	
Project (BATA) Contingency	16.5	17.1	17.1	0.0		
<b>Project Total (a)</b>	<b>433.2</b>	<b>479.8</b>	<b>479.8</b>	<b>0.0</b>	<b>315.8</b>	

(a) Totals may be rounded

SCHEDULE STATUS	Baseline (June 2000)	Current (Oct 2002)	Forecast (Dec 2002)	Variance	Notes
<b>Construction Contract Completion</b>					
Replacement Bridge & North Approach	Dec 03	May 04	May 04	0	
South Approach and Interchange (Phase 1)	Oct 04	Jul 03	Aug 03	+1	
Maintenance Facility	Mar 02	Sep 02	Sep 02	0	
1927 Bridge Demolition	Mar 06	Mar 06	Mar 06	0	
<b>Project</b>					
New Facility Open to Traffic	Jan 03	Oct 03	Oct 03	0	

NOTES

ACTION


## RICHMOND-SAN RAFAEL BRIDGE REHABILITATION

Completed in 1956, the Richmond-San Rafael Bridge provides access - via Interstate 580 - across San Francisco Bay between Marin and Contra Costa counties. Major rehabilitation of the bridge was specified in RM 1 to be eligible for toll funding.

Currently, there are two major rehabilitation projects planned for the bridge:

- The first project is to replace the western trestle (low-rise) section of the bridge near San Rafael and rehabilitate the ship collision protection fender system at various bridge piers. This rehabilitation work is being combined with a seismic retrofit project.
- The second project is to rehabilitate the existing concrete deck on the bridge. The cast-in-place concrete riding surface (deck) has been worn over

time due to traffic and exposure to the marine environment. This project will follow the completion of the trestle and fender rehabilitation project to avoid possible construction conflicts.

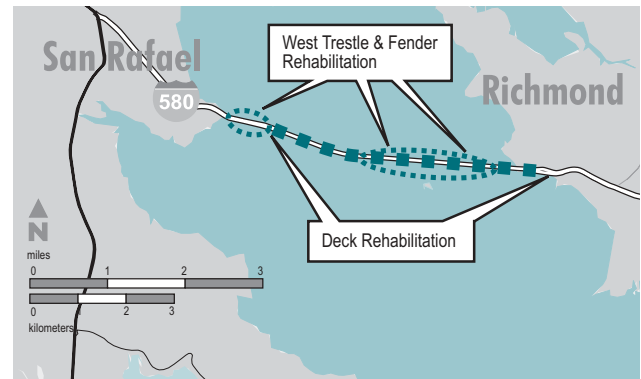

### Project Photos



*Existing Trestle Interiors (looking east)*



*Interior Foundation Piles*

### Current Activities:

- The west trestle replacement consists of rebuilding the eastbound and westbound trestles near San Quentin. The trestles are parallel for most of their length and diverge to carry traffic onto the upper and lower decks of the main bridge. The westbound trestle, serving the upper deck, is 2,844 feet (867 meters), between Bents 1 and 29; the eastbound trestle, serving the lower deck, is 3,635 feet (1,108 meters), between Bents 1 and 37. The trestle replacement procedure consists of reducing lane width, demolishing an 8 feet (2 meters) linear section of interior bridge deck and installing interior sixty-six inch (1,680 mm) cast-in-drilled-hole (CIDH) piles at the mid-span of every other existing 50 foot (15 meter) deck section. Pile installation includes pile driving and drill out, reinforcing steel installation and concrete infill. When installation of the interior piles is complete, the operation is repeated on the exterior, where 8 feet (2 meters) of exterior bridge deck is removed and exterior piles are installed. After installation of the piles, pile/bent caps will be cast in place below the existing superstructure, atop the opposing interior and exterior piles. Following pile-bent construction, one trestle at a time will be closed at night for superstructure replacement. Each night, two of the existing 50-foot (15 meter) sections will be removed and replaced with one 100-foot (30 meter) precast section.
- Construction continues from west to east on the interior sections of the existing eastbound and westbound trestles. Interior pile installation is currently at Bent 17 of 37 with drilling out and concrete placing in the pile shells at Bent 10 of 37.
- Interior trestle work is not on the critical path and actual work has slowed from earlier forecasts. The schedule for the trestle work is currently under revision; exterior trestle work is forecast to begin in January 2003.

BAY AREA TOLL AUTHORITY

**RICHMOND-SAN RAFAEL BRIDGE REHABILITATION**

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (Oct 2002)	Current Forecast (Dec 2002)	Variance	Expended to Date (7/98 - 11/02)	Notes
<b>West Trestle and Fender Rehabilitation</b>						
Capital Outlay Construction	33.9	0.0	0.0	0.0	0.0	
Capital Outlay Support	5.4	0.7	0.7	0.0	0.7	
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Non-BATA Funding	0.0	34.6	34.6	0.0	16.5	
Project (BATA) Contingency	6.1	0.0	0.0	0.0		
<b>Subtotal</b>	<b>45.4</b>	<b>35.4</b>	<b>35.4</b>	<b>0.0</b>	<b>17.2</b>	
<b>Deck Rehabilitation</b>						
Capital Outlay Construction	33.0	33.0	33.0	0.0	0.0	
Capital Outlay Support	9.0	5.0	5.0	0.0	0.2	
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Non-BATA Funding	0.0	4.0	4.0	0.0	0.0	
Project (BATA) Contingency	11.4	11.4	11.4	0.0		
<b>Subtotal</b>	<b>53.4</b>	<b>53.4</b>	<b>53.4</b>	<b>0.0</b>	<b>0.2</b>	
<b>Project Total (a)</b>	<b>98.9</b>	<b>88.8</b>	<b>88.8</b>	<b>0.0</b>	<b>17.4</b>	
(a) Totals may be rounded						

SCHEDULE STATUS	Baseline (June 2000)	Current (Oct 2002)	Forecast (Dec 2002)	Variance	Notes
<b>Construction Contract Completion</b>					
West Trestle and Fender Rehabilitation	Dec 04	Sep 04	Sep 04	0	
Deck Rehabilitation	Sep 06	Sep 06	Jul 07	+10	A
<b>Project</b>					
<b>New Facility Open to Traffic</b>					B

NOTES	ACTION
A. Caltrans is reporting a forecast completion in mid-2005 for the retrofit project with the deck rehabilitation to follow.	Caltrans is reviewing the forecast completion date of the deck rehabilitation contract.
B. The existing facility remains open to traffic during all phases of construction.	None.



## SAN MATEO-HAYWARD BRIDGE WIDENING

In 1996, the western approach to the San Mateo-Hayward Bridge from U.S. Route 101 was widened from four to six lanes to match the configuration of the high-rise section of the bridge. The current project will complete the widening work in this corridor along the low-trestle section of the bridge and its eastern approach to Interstate 880. The project includes the following features:

- Widening of the low-rise trestle and eastern approach from I-880 from four to six lanes with shoulders
- Extension of the existing west-bound HOV lane one mile west along the eastern approach from Interstate 880
- Construction of a new pedestrian/bicycle overcrossing of State Route 92
- Expansion of the existing toll plaza
- Improvements to the Hayward Shoreline Interpretive Center



*Mini Toll Plaza*

### Project Construction Progress and Photos



*Eastbound Trestle Reconstruction*



*Pedestrian Overcrossing*

### Current Activities:

- On the bridge widening contract, the westbound trestle opened to traffic on November 4, 2002, with three traffic lanes and shoulders. The original two westbound lanes are closed for nighttime removal of the median barrier and reconstruction on the existing trestle. Upon completion of the barrier removal, the old trestle will carry three eastbound only traffic lanes with shoulders. Installation of the metering light structure west of the toll plaza is in progress.
- The mini toll plaza opened for operation on October 25, 2002. Construction on the contract is complete as of November 30, 2002.
- The pedestrian overcrossing is complete and open to pedestrian traffic.

BAY AREA TOLL AUTHORITY


SAN MATEO-HAYWARD BRIDGE WIDENING

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (Oct 2002)	Current Forecast (Dec 2002)	Variance	Expended to Date (7/98 - 11/02)	Notes
<b>Widening</b>						
Capital Outlay Construction						
Widen Trestle	124.8	128.9	128.9	0.0	122.2	
Widen Roadway	29.2	26.1	26.1	0.0	25.4	
Construct Mini Toll Plaza	4.4	6.3	6.3	0.0	5.9	
Other Budgeted Capital	8.9	8.6	8.6	0.0	2.9	
Capital Outlay Support	15.5	39.8	39.8	0.0	29.4	
Capital ROW	1.5	1.5	1.5	0.0	0.5	
Project (BATA) Contingency	19.3	6.3	6.3	0.0		
<b>Subtotal</b>	<b>203.6</b>	<b>217.5</b>	<b>217.5</b>	<b>0.0</b>	<b>186.3</b>	
<b>West Approach Planting</b>						
Capital Outlay Construction	0.2	0.2	0.2	0.0	0.0	
Capital Outlay Support	0.1	0.1	0.1	0.0	0.0	
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Project (BATA) Contingency	0.1	0.1	0.1	0.0		
<b>Subtotal</b>	<b>0.3</b>	<b>0.3</b>	<b>0.3</b>	<b>0.0</b>	<b>0.0</b>	
<b>Project Total (a)</b>	<b>203.9</b>	<b>217.8</b>	<b>217.8</b>	<b>0.0</b>	<b>186.3</b>	
(a) Totals may be rounded						

SCHEDULE STATUS	Baseline (June 2000)	Current (Oct 2002)	Forecast (Dec 2002)	Variance	Notes
<b><u>Construction Contract Completion</u></b>					
<b>Widening</b>					
Widen Trestle	Dec 02	Feb 03	Feb 03	0	
Construct Mini Toll Plaza	Nov 02	Nov 02	Nov 02	0	
Widen Eastern Approach	Nov 02	Sep 01	Sep 01	0	
Pedestrian Overcrossing	Sep 02	Sep 02	Sep 02	0	
<b>West Approach Planting</b>					
West Approach Replacement Planting	May 08	May 08	May 08	0	
<b><u>Project</u></b>					
New Facility Open to Traffic	Dec 02	Nov 02	Nov 02		
<b>NOTES</b>			<b>ACTION</b>		

## I-880/SR-92 INTERCHANGE IMPROVEMENT

As part of an effort to improve traffic flow and to relieve congestion on the San Mateo-Hayward Bridge and its approaches, RM 1 identified the need to improve and reconstruct the Interstate 880/State Route 92 interchange. While still in the environmental clearance phase, the project proposes to modify the existing cloverleaf interchange to increase capacity and improve safety and traffic operations. Various alternatives are under consideration and are being assessed as part of the environmental process.

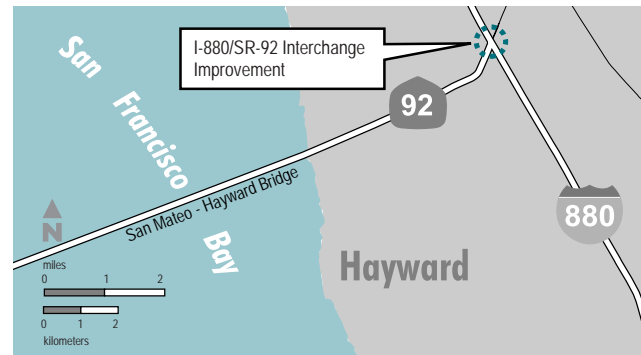

### Project Photos



*Existing Interchange; looking west*



*Alternative H Interchange; looking west*

### Current Activities:

- In December 2001 Caltrans and other stakeholders selected Alternate "H" for the project. Caltrans is currently preparing the Final Environmental Impact Statement/Report (FEIS/R) for submittal to the Federal Highway Administration (FHWA) in early 2003.



BAY AREA TOLL AUTHORITY

I-880/SR 92 INTERCHANGE IMPROVEMENT

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (Oct 2002)	Current Forecast (Dec 2002)	Variance	Expended to Date (7/98 - 11/02)	Notes
<b>I-880/SR-92 Interchange Improvement</b>						
Capital Outlay Construction	70.3	94.6	94.6	0.0	0.0	A
Capital Outlay Support	20.8	24.1	24.1	0.0	11.3	A
Capital ROW	8.0	0.1	0.1	0.0	0.0	A
Non-BATA Funding	0.0	10.0	10.0	0.0		
Project (BATA) Contingency	25.1	5.5	5.5	0.0	0.0	
<b>Project Total (a)</b>	<b>124.2</b>	<b>134.2</b>	<b>134.2</b>	<b>0.0</b>	<b>11.3</b>	
(a) Totals may be rounded						

SCHEDULE STATUS	Baseline (June 2000)	Current (Oct 2002)	Forecast (Dec 2002)	Variance	Notes
<b><u>Construction Contract Completion</u></b>					
I-880/SR-92 Interchange Improvement	Dec 06	Jun 09	Jun 09	0	
<b><u>Project</u></b>					
New Facility Open to Traffic	Dec 06	Jun 09	Jun 09	0	

NOTES	ACTION
A. A preliminary revised Caltrans estimate for the project is higher than the current budget.	BATA is reviewing.

## DUMBARTON BRIDGE WEST APPROACH PROJECTS

RM 1 identified the need for improvements to the western approaches to the Dumbarton Bridge. Through coordination with the City/County Association of Governments of San Mateo County, two projects were identified for toll bridge funding:

- The first project, sponsored by the City of East Palo Alto, modifies the U.S. Route 101/University Avenue interchange. This project is designed to help alleviate traffic congestion and improve overall traffic flow to University Avenue and the Dumbarton Bridge.
- The second project, sponsored by Caltrans, widens the Bayfront Expressway (State Route 84) from the Dumbarton Bridge to the U.S. 101/Marsh Road interchange. The existing six-lane expressway section from the bridge to University Avenue will be reconstructed with upgraded shoulders and lane widths. The existing expressway section from University Avenue to Marsh Road will be widened from four to six lanes.



### Project Photos



*Northbound Excavation*



*Retaining Wall Construction*

### Current Activities:

- On the Bayfront Expressway (SR-84) widening contract, excavation, drain installation and placing of lightweight fill are complete on the eastbound shoulder between University Ave. and the Dumbarton Bridge. Traffic has been diverted to the newly paved section to allow excavation on the north side of SR-84. Paving is complete on the eastbound side between University Ave. and Willow Road.
- Retaining wall construction, electrical installation for street lights and tunnel work are in progress along the west side of the expressway between Willow and Marsh Roads and traffic is diverted to the outside lanes to allow for construction work in the median.
- The Ravenswood Triangle between Willow Road and University Ave. continues to be restored as a wetland with the creation of mounds and ponds.

BAY AREA TOLL AUTHORITY

DUMBARTON BRIDGE WEST APPROACH PROJECTS

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (Oct 2002)	Current Forecast (Dec 2002)	Variance	Expended to Date (7/98 - 11/02)	Notes
<b>US101/University Avenue Interchange Reconstruction (Non-Caltrans)</b>						
Capital Outlay Construction	3.8	3.8	3.8	0.0	3.7	
Capital Outlay Support	0.0	0.0	0.0	0.0	0.0	
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Project (BATA) Contingency	0.0	0.0	0.0	0.0		
<b>Subtotal</b>	<b>3.8</b>	<b>3.8</b>	<b>3.8</b>	<b>0.0</b>	<b>3.7</b>	
<b>Bayfront Expressway (SR84) Widening</b>						
Capital Outlay Construction	24.8	26.6	26.6	0.0	14.2	
Capital Outlay Support	4.4	6.5	6.5	0.0	5.6	A
Capital ROW	1.3	0.2	0.2	0.0	0.2	
Project (BATA) Contingency	3.3	0.5	0.5	0.0		
<b>Subtotal</b>	<b>33.8</b>	<b>33.8</b>	<b>33.8</b>	<b>0.0</b>	<b>19.9</b>	
<b>Project Total (a)</b>	<b>37.6</b>	<b>37.6</b>	<b>37.6</b>	<b>0.0</b>	<b>23.6</b>	
(a) Totals may be rounded						

SCHEDULE STATUS	Baseline (June 2000)	Current (Oct 2002)	Forecast (Dec 2002)	Variance	Notes
<b><u>Construction Contract Completion</u></b>					
US 101/University Avenue Interchange Reconstruction (Non-Caltrans)	Apr 00	Apr 00	Apr 00	0	
Bayfront Expressway (SR84) Widening	Mar 03	Apr 04	Oct 03	-6	
<b><u>Project</u></b>					
New Facility Open to Traffic	Mar 03	Apr 04	Oct 03	-6	
<b>NOTES</b>			<b>ACTION</b>		

A Caltrans has requested additional funds for capital outlay support.

## APPENDICES

**Appendix A: Project Budget Adjustments**

**Appendix B: Current Approved Contract Change Orders**

**Appendix C: Project Cost Summary Details**



BAY AREA TOLL AUTHORITY

**APPENDIX A – LIST OF PROJECT BUDGET ADJUSTMENTS**

DEFINITIONS:

**Baseline Budget (June 2000):** Baseline budgets as established by BATA in June 2000 for each project within the overall program.

**Current Budget:** Budget currently serving as the baseline for monitoring purposes. The current budget is equal to the established June 2000 budget, plus or minus any adjustment as listed below.

**Project Baseline Adjustments**

Date	Description of Adjustment
10/2000	Current Budgets for allocated capital outlay adjusted by BATA to reflect current Caltrans construction contract allotments.
11/2000	Current Budgets for the Benicia-Martinez and Richmond-San Rafael Bridge projects revised to reflect new funding from Non-BATA sources per agreements with Caltrans and a Prop. 192 refund from Caltrans related to the Carquinez Bridge project.
01/2001	Current Budget for the Benicia-Martinez bridge revised to reflect allocations by BATA.
03/2001	Current Budget for the Carquinez Bridge revised by BATA.
10/2001	Current Budget for the Benicia-Martinez Bridge revised by BATA.
12/2001	Current Budgets for the Benicia-Martinez and San Mateo-Hayward Bridges revised by BATA.

BAY AREA TOLL AUTHORITY

**APPENDIX B – APPROVED CONTRACT CHANGE ORDERS (CCO)  
FOR DECEMBER 2002  
BENICIA-MARTINEZ BRIDGE**

Bridge/ Contract	CCO Number <sup>1</sup>	CCO Description	Funding Source <sup>2</sup>	Impacts	
				Cost (\$1000's)	Schedule
<b>New Bridge 04-006034</b>		No Approved Change Orders for December			
<b>Subtotal</b>					
<b>Toll Plaza 04-006044</b>	5	Security Badges	C	31.7	
	8	Apprenticeship Training	C	14.4	
	9	SWPPP Maintenance	C	50.0	
	10	Provide Additional SWPPP Measures	C	50.0	
<b>Subtotal</b>				<b>146.1</b>	
<b>Marina Vista Interchange 04-006054</b>		No Approved Change Orders for December 2002			
<b>Subtotal</b>					
<b>I-680/I-780 Interchange 04-006064</b>	1	Flagging and Traffic Control	C	150.0	
	5	Buried Man-Made Objects	C	20.0	
	6	Compensation Adjustment for AC Price Index Fluctuations	C	14.9	
	7	Revise NDT Requirement for 24" Pipe Pile	C	(8.0)	
	8	QC/QA – Revise Section 39-5.02 & 395-03	C	0.0	
	9	QC/QA – Revise Section 39-2.03 (Price Method)	C	0.0	
<b>Subtotal</b>				<b>176.9</b>	
<b>South Approach 04-006094</b>		Contract is complete.			
<b>Totals for December 2002<sup>3</sup></b>				<b>323.0</b>	

<sup>1</sup> Only approved CCOs for the month are listed in Appendix B.

<sup>2</sup> Funding Source(s)  
S = Supplemental work  
C = Construction contingency

<sup>3</sup> Approved CCO cost total is within the approved current contract budget.

BAY AREA TOLL AUTHORITY

**APPENDIX B – APPROVED CONTRACT CHANGE ORDERS (CCO)  
FOR DECEMBER 2002  
CARQUINEZ BRIDGE**

Bridge/ Contract	CCO Number <sup>1</sup>	CCO Description	Funding Source <sup>2</sup>	Impacts	
				Cost (\$1000's)	Schedule
<b>Carquinez Bridge Replacement 04-013014</b>		No Approved Change Orders for December 2002			
<b>Subtotal</b>					
<b>South Approach and Crockett Interchange 04-013054</b>	43	Removal/Lower Drainage System 5	C	8.6	
<b>Subtotal</b>				8.6	
<b>Maintenance Facility 04-013084</b>		Contract is complete.			
<b>Subtotal</b>					
<b>Totals for December 2002<sup>3</sup></b>				8.6	

<sup>1</sup> Only approved CCOs for the month are listed in Appendix B.

<sup>2</sup> Funding Source(s)  
S = Supplemental work  
C = Construction contingency

<sup>3</sup> Approved CCO cost total is within the approved current contract budget.



BAY AREA TOLL AUTHORITY

**APPENDIX B – APPROVED CONTRACT CHANGE ORDERS (CCO)  
FOR DECEMBER 2002  
SAN MATEO-HAYWARD BRIDGE**

Bridge/ Contract	CCO Number <sup>1</sup>	CCO Description	Funding Source <sup>2</sup>	Impacts	
				Cost (\$1000's)	Schedule
<b>Widen Trestle 04-045014</b>	12	Construct Approach Slab	C	10.0	17
	14-S2	Adjustment of Contract Time	C	600.0	
	39	Settlement of Non-CCO 14 Time Related Issues	C	0.0	
	45	Revise Transportation to Engineer	C	0.0	
<b>Subtotal</b>				<b>600.0</b>	
<b>Mini-Toll Plaza 04-045024</b>		No Approved Change Orders for December 2002			
<b>Subtotal</b>					
<b>Pedestrian Overcrossing 04-045044</b>		Contract is complete.			
<b>Subtotal</b>					
<b>Widen Roadway 04-045034</b>		Contract is complete.			
<b>Totals for December 2002<sup>3</sup></b>				<b>600.0</b>	

<sup>1</sup> Only approved CCOs for the month are listed in Appendix B.

<sup>2</sup> Funding Source(s)  
S = Supplemental work  
C = Construction contingency

<sup>3</sup> Approved CCO cost total is within the approved current contract budget.

## BAY AREA TOLL AUTHORITY

## APPENDIX C – PROJECT COST SUMMARY DETAILS

The following sheets provide detailed cost information for each of the bridge projects. Capital Outlay Support (Engineering), Capital Right-of-Way and Capital Outlay are shown for each of the projects. The Project (BATA) Contingency, as well as the bridge projects totals, is shown at the end of each bridge summary.

**Definitions:**

1. Capital Outlay Support includes both Caltrans and Architectural/Engineering (A/E) consultant support.
2. Capital Right of Way includes acquisition, loss of goodwill, demolition, utilities relocations, relocation assistance, title costs, and sale of excess lands.
3. Capital Outlay includes construction bid terms, external third party agreements, state-furnished materials, supplemental construction work, and construction contingencies.

Project Cost Summaries  
(\$ Millions)

	EA Number	Baseline Budget Jun-00	Current Budget Oct-02	Current Forecast Dec-02	Net Change	Expended <sup>1</sup> to Date (7/98 – 11/02)	Note
<b>Northern Bridge Group</b>							
<i>Project 2003 – New Benicia-Martinez Bridge</i>							
<b>South Approach</b>							
Capital Outlay Support	00609x	3.5	4.0	4.0	0.0	3.6	
Capital Right of Way	006099	7.0	7.7	7.7	0.0	7.2	
Capital Outlay	006094	6.0	7.0	7.0	0.0	6.4	
<b>Total South Approach</b>		<b>16.5</b>	<b>18.8</b>	<b>18.8</b>	<b>0.0</b>	<b>17.2</b>	
<b>New Bridge</b>							
Capital Outlay Support	00603x	31.9	36.0	36.0	0.0	23.7	
Capital Right of Way	006039	4.1	2.5	2.5	0.0	0.8	
Capital Outlay	006034	247.3	307.5	307.5	0.0	70.4	
Non-BATA Funding		0.0	10.1	10.1	0.0	1.7	
<b>Total New Bridge</b>		<b>283.3</b>	<b>356.1</b>	<b>356.1</b>	<b>0.0</b>	<b>96.5</b>	
<b>Toll Plaza &amp; Administration Building</b>							
Capital Outlay Support	00604x	6.2	10.3	10.3	0.0	6.7	
Capital Right of Way	006049	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	006044	22.8	21.4	21.4	0.0	4.4	
<b>Total Toll Plaza &amp; Admin.</b>		<b>29.1</b>	<b>31.7</b>	<b>31.7</b>	<b>0.0</b>	<b>11.1</b>	
<b>I-680/Marina Vista Interchange</b>							
Capital Outlay Support	00605x	10.7	15.7	15.7	0.0	9.7	
Capital Right of Way	006059	7.4	2.5	2.5	0.0	1.9	
Capital Outlay	006054	43.2	45.1	45.1	0.0	1.4	
<b>Total I-680/MV I/C</b>		<b>61.4</b>	<b>63.3</b>	<b>63.3</b>	<b>0.0</b>	<b>13.0</b>	
<b>I-680/I-780 Interchange</b>							
Capital Outlay Support	00606x	18.7	25.7	25.7	0.0	14.8	
Capital Right of Way	006069	1.7	1.7	1.7	0.0	1.4	
Capital Outlay	006064	80.8	54.7	54.7	0.0	20.8	
Non-BATA Funding		0.0	20.9	20.9	0.0	1.4	
<b>Total I-680/I-780 I/C</b>		<b>101.2</b>	<b>103.0</b>	<b>103.0</b>	<b>0.0</b>	<b>38.4</b>	

<sup>1</sup> Unaudited

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Oct-02	Current Forecast Dec-02	Net Change	Expended to Date (7/98 – 11/02)	Note
<b>Project 2003 – New Benicia-Martinez Bridge (cont'd)</b>							
<b>Other Budgeted Capital</b>							(a)
Capital Outlay Support		7.1	7.4	7.4	0.0	2.2	
Capital Right of Way		0.9	0.0	0.0	0.0	0.0	
Capital Outlay		28.1	30.0	30.0	0.0	1.7	
<b>Total Other Budgeted Capital</b>		<b>36.1</b>	<b>37.4</b>	<b>37.4</b>	<b>0.0</b>	<b>3.9</b>	
Total Capital Outlay Support		78.2	99.1	99.1	0.0	60.6	
Total Capital Right of Way		21.1	14.4	14.4	0.0	11.3	
Total Capital Outlay		428.2	465.8	465.8	0.0	105.0	
Non-BATA Funding		0.0	31.0	31.0	0.0	3.1	
Project Contingency (BATA)		58.4	42.5	42.5	0.0		
<b>Total New Benicia-Martinez Bridge</b>		<b>586.0</b>	<b>652.8</b>	<b>652.8</b>	<b>0.0</b>	<b>180.0</b>	
<b>Project 3002 – Carquinez Bridge Replacement</b>							
<b>Replacement Bridge &amp; North Approach</b>							(b)
Capital Outlay Support	01301x	17.7	58.4	58.4	0.0	47.2	
Capital Right of Way	013019	3.0	3.0	3.0	0.0	3.3	
Capital Outlay	013014	213.7	239.2	239.2	0.0	174.4	
<b>Total Replacement Bridge &amp; N. Approach</b>		<b>234.4</b>	<b>300.6</b>	<b>300.6</b>	<b>0.0</b>	<b>224.9</b>	
<b>South Approach &amp; Interchange</b>							(c)
Capital Outlay Support	01305x	22.7	32.4	32.4	0.0	22.7	
Capital Right of Way	013059	5.0	5.0	5.0	0.0	4.6	
Capital Outlay	013054	116.0	73.9	73.9	0.0	41.6	
<b>Total South Approach &amp; I/C</b>		<b>143.7</b>	<b>111.3</b>	<b>111.3</b>	<b>0.0</b>	<b>68.8</b>	
<b>Maintenance Facility Phase I &amp; II</b>							(d)
Capital Outlay Support		0.7	4.8	4.8	0.0	4.3	
Capital Right of Way		1.6	1.6	1.6	0.0	1.4	
Capital Outlay		7.0	8.1	8.1	0.0	7.7	
<b>Total Maint. Facility Ph I &amp; II</b>		<b>9.3</b>	<b>14.6</b>	<b>14.6</b>	<b>0.0</b>	<b>13.4</b>	
<b>Demolition – 1927 Bridge</b>							
Capital Outlay Support	01309x	2.0	4.1	4.1	0.0	1.2	
Capital Right of Way	013099	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	013094	16.0	16.0	16.0	0.0	0.0	
<b>Total Demo – 1927 Bridge</b>		<b>18.0</b>	<b>20.1</b>	<b>20.1</b>	<b>0.0</b>	<b>1.2</b>	

Notes

- (a) Includes EA 00601\*, 00608\*, 0060A\*, 0060C\*, 0060F\*, 0060G\*, 0060H\*
- (b) Includes EA 00453\*, 01301\*, 01303\*, 01304\*
- (c) Includes EA 01302\*, 01305\*, 04700\*
- (d) Includes EA 00607\*, 01308\*

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Oct-02	Current Forecast Dec-02	Net Change	Expended to Date (7/98 – 11/02)	Note
<b>Project 3002 - Carquinez Bridge Replacement (cont'd)</b>							
<b>Other Budgeted Capital</b>							(e)
Capital Outlay Support		0.6	3.1	3.1	0.0	1.2	
Capital Right of Way		0.0	1.5	1.5	0.0	0.0	
Capital Outlay		10.6	11.5	11.5	0.0	6.3	
<b>Total Other Budgeted Capital</b>		<b>11.2</b>	<b>16.1</b>	<b>16.1</b>	<b>0.0</b>	<b>7.5</b>	
Total Capital Outlay Support		43.7	102.9	102.9	0.0	76.6	
Total Capital Right of Way		9.6	11.1	11.1	0.0	9.3	
Total Capital Outlay		363.3	348.7	348.7	0.0	230.0	
Project (BATA) Contingency		16.5	17.1	17.1	0.0		
<b>Total Carquinez Bridge</b>		<b>433.2</b>	<b>479.8</b>	<b>479.8</b>	<b>0.0</b>	<b>315.8</b>	
<b>Project 4003 – Richmond-San Rafael Bridge – West Trestle and Fender Rehabilitation</b>							
Capital Outlay Support	0438Ux	5.4	0.7	0.7	0.0	0.7	(f)
Capital Right of Way	0438U9	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	0438U4	33.9	0.0	0.0	0.0	0.0	
Non-BATA Funding		0.0	34.6	34.6	0.0	16.5	
Project (BATA) Contingency		6.1	0.0	0.0	0.0		
<b>Total R-SR Bridge – W. Trestle &amp; Fender Rehabilitation</b>		<b>45.4</b>	<b>35.4</b>	<b>35.4</b>	<b>0.0</b>	<b>17.2</b>	
<b>Project 4002 – Richmond-San Rafael Bridge – Deck Rehabilitation</b>							
Capital Outlay Support	04152x	9.0	5.0	5.0	0.0	0.2	
Capital Right of Way	041529	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	041524	33.0	33.0	33.0	0.0	0.0	
Non-BATA Funding		0.0	4.0	4.0	0.0	0.0	
Project (BATA) Contingency		11.4	11.4	11.4	0.0		
<b>Total R-SR Bridge – Deck Rehab</b>		<b>53.4</b>	<b>53.4</b>	<b>53.4</b>	<b>0.0</b>	<b>0.2</b>	
<b>Richmond Parkway (Non-Caltrans)</b>							
Capital Outlay Support	non-Caltrans	0.0	0.0	0.0	0.0	0.0	
Capital Right of Way	non-Caltrans	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	non-Caltrans	5.9	5.9	5.9	0.0	2.4	(g)
<b>Total Richmond Parkway</b>		<b>5.9</b>	<b>5.9</b>	<b>5.9</b>	<b>0.0</b>	<b>2.4</b>	
<b>Total Northern Bridge Group</b>		<b>1123.9</b>	<b>1227.2</b>	<b>1227.2</b>	<b>0.0</b>	<b>515.7</b>	

Notes

(e) Includes EA 01306\*, 01307\*, 0130A\*, 0130C\*, 0130D\*, 0130F\*, 0130G\*, 0130H\*, 0130J\*, 0130X\*

(f) Includes EA 04382\*, 04383\*, 0438U\*

(g) Total reimbursements made to the City of Richmond for current allocation.

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Oct-02	Current Forecast Dec-02	Net Change	Expended to Date (7/98 – 11/02)	Note
<b>Southern Bridge Group</b>							
<b>Project 6004 – San Mateo-Hayward Bridge Widening</b>							
<b>Widen Trestle</b>							
Capital Outlay Support	04501x	7.9	22.8	22.8	0.0	17.7	(h)
Capital Right of Way	045019	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	045014	124.8	128.9	128.9	0.0	122.2	
<b>Total Widen Trestle</b>		<b>132.7</b>	<b>151.7</b>	<b>151.7</b>	<b>0.0</b>	<b>140.0</b>	
<b>Widen Roadway</b>							
Capital Outlay Support	04503x	4.3	6.0	6.0	0.0	6.0	
Capital Right of Way	045039	1.0	0.0	0.0	0.0	0.0	
Capital Outlay	045034	29.2	26.1	26.1	0.0	25.4	
<b>Total Widen Roadway</b>		<b>34.5</b>	<b>32.1</b>	<b>32.1</b>	<b>0.0</b>	<b>31.4</b>	
<b>Construct Mini Toll Plaza</b>							
Capital Outlay Support	04502x	1.7	3.8	3.8	0.0	2.2	
Capital Right of Way	045029	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	045024	4.4	6.3	6.3	0.0	5.9	
<b>Total Mini Toll Plaza</b>		<b>6.1</b>	<b>10.1</b>	<b>10.1</b>	<b>0.0</b>	<b>8.1</b>	
<b>Other Budgeted Capital</b>							
Capital Outlay Support		1.6	7.2	7.2	0.0	3.4	(i)
Capital Right of Way		0.5	1.5	1.5	0.0	0.5	
Capital Outlay		8.9	8.6	8.6	0.0	2.9	
<b>Total Other Budgeted Capital</b>		<b>11.0</b>	<b>17.3</b>	<b>17.3</b>	<b>0.0</b>	<b>6.8</b>	
Total Capital Outlay Support		15.5	39.8	39.8	0.0	28.7	
Total Capital Right of Way		1.5	1.5	1.5	0.0	0.5	
Total Capital Outlay		167.3	169.9	169.9	0.0	152.8	
Project (BATA) Contingency		19.3	6.3	6.3	0.0		
<b>Total San Mateo-Hayward Bridge Widening</b>		<b>203.6</b>	<b>217.5</b>	<b>217.5</b>	<b>0.0</b>	<b>182.0</b>	
<b>San Mateo-Hayward Bridge – West Approach Replacement Planting</b>							
Capital Outlay Support	04860x	0.1	0.1	0.1	0.0	0.0	
Capital Right of Way	048609	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	048604	0.2	0.2	0.2	0.0	0.0	
Project (BATA) Contingency		0.1	0.1	0.1	0.0		
<b>Total SM-H Bridge W. Approach Replacement Planting</b>		<b>0.4</b>	<b>0.4</b>	<b>0.4</b>	<b>0.0</b>	<b>0.0</b>	

Notes:

(h) Includes EA 04501\*

(i) Includes EA 00305\*, 04504\*, 04505\*, 04506\*, 04507\*, 04508\*, 04509\*

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Oct-02	Current Forecast Dec-02	Net Change	Expended to Date (7/98 – 11/02)	Note
<b>I-880/SR-92 Interchange Improvement</b>							(j)
Capital Outlay Support	23317x	20.8	24.1	24.1	0.0	11.3	
Capital Right of Way	233179	8.0	0.1	0.1	0.0	0.0	
Capital Outlay	233174	70.3	94.6	94.6	0.0	0.0	
Non-BATA Funding		0.0	10.0	10.0	0.0		
Project (BATA) Contingency		25.1	5.5	5.5	0.0		
<b>Total I-880/SR-92 I/C Improve.</b>		<b>124.2</b>	<b>134.2</b>	<b>134.2</b>	<b>0.0</b>	<b>11.3</b>	
<b>Dumbarton Bridge West Approach Projects</b>							
<b>US101/University Avenue Interchange Reconstruction (non-Caltrans)</b>							
Capital Outlay Support		0.0	0.0	0.0	0.0	0.0	
Capital Right of Way		0.0	0.0	0.0	0.0	0.0	
Capital Outlay		3.8	3.8	3.8	0.0	3.7	(k)
<b>Total US-101/University Ave.</b>		<b>3.8</b>	<b>3.8</b>	<b>3.8</b>	<b>0.0</b>	<b>3.7</b>	
<b>Bayfront Expressway (SR-84) Widening</b>							(l)
Capital Outlay Support	00487x	4.4	6.5	6.5	0.0	5.4	
Capital Right of Way	004879	1.3	0.2	0.2	0.0	0.2	
Capital Outlay	004874	24.8	26.6	26.6	0.0	14.2	
Project (BATA) Contingency		3.3	0.5	0.5	0.0		
<b>Total Bayfront Expressway (SR-84)</b>		<b>33.8</b>	<b>33.8</b>	<b>33.8</b>	<b>0.0</b>	<b>19.9</b>	
<b>Total Dumbarton Bridge W. Approach</b>		<b>37.6</b>	<b>37.6</b>	<b>37.6</b>	<b>0.0</b>	<b>23.6</b>	
<b>Total Southern Bridge Group</b>		<b>365.7</b>	<b>389.6</b>	<b>389.6</b>	<b>0.0</b>	<b>221.3</b>	

Notes:

(j) Includes EA 01601\* and 01602\*

(k) Total reimbursements made to the City of East Palo Alto for current allocation.

(l) Includes EA 01511\* and 01512\*

General Notes:

1. Capital outlay support includes both Caltrans and Architectural/Engineering (A/E) consultant support.
2. Capital right of way includes acquisition, loss of goodwill, demolition, utilities relocations, relocation assistance, title costs, and sale of excess lands.
3. Capital outlay includes construction bid items, supplemental construction work, state furnished materials, construction contingencies, and external third party agreements.
