

BAY AREA TOLL AUTHORITY

Regional Measure 1
Toll Bridge Projects

Project Monitoring Program


JULY 2004 PROGRESS REPORT



Metropolitan Transportation
Commission

Bay Area Toll Authority

Released August 2004

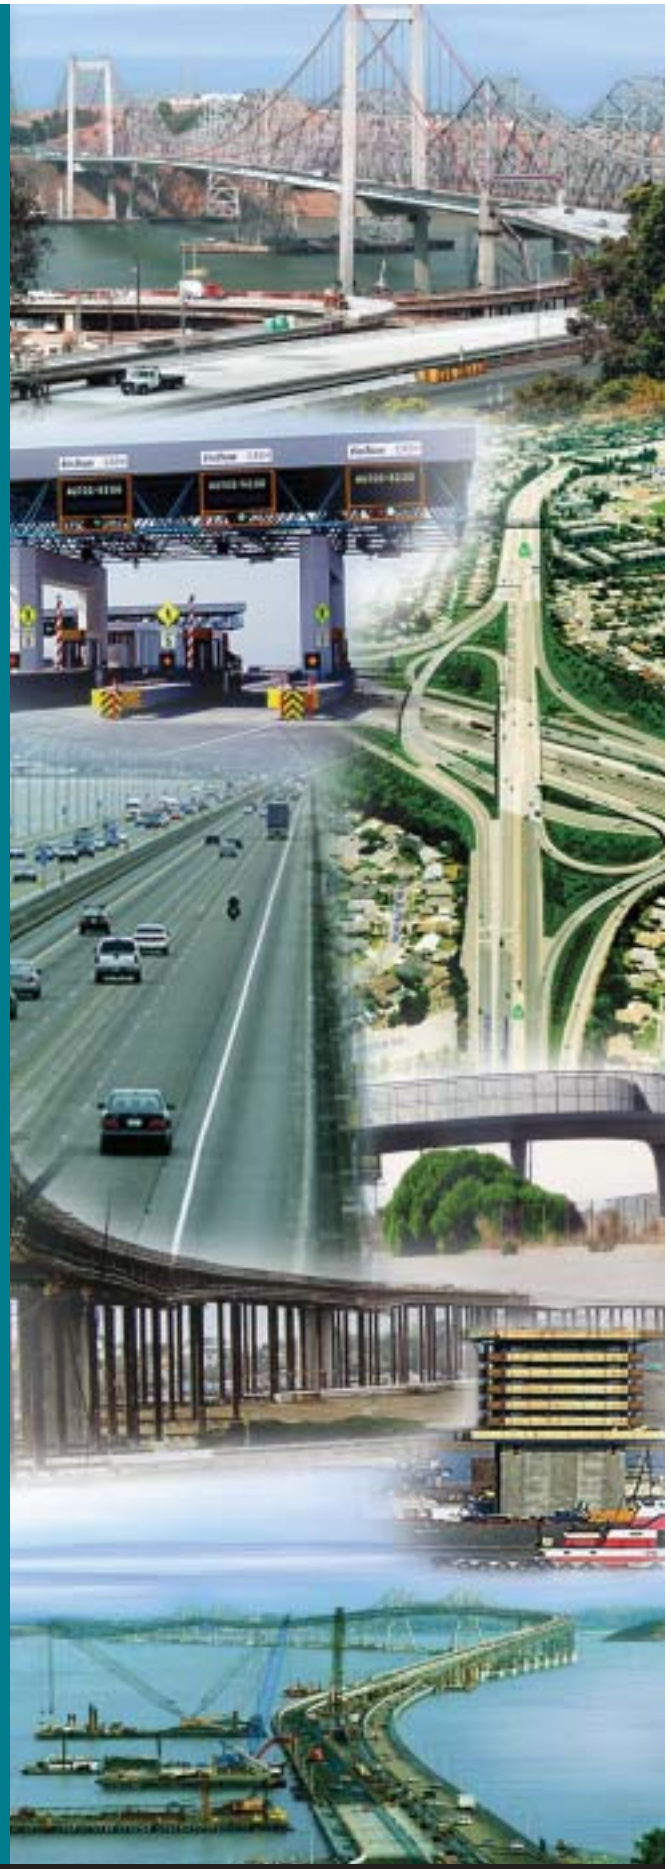

Bay Area Toll Authority/Metropolitan Transportation Commission

Commission Roster

Steve Kinsey, MTC Chair
Marin County and Cities

Jon Rubin, MTC Vice Chair
San Francisco Mayor's Appointee

Tom Ammiano
City and County of San Francisco

Irma L. Anderson
Cities of Contra Costa County

Tom Azumbrado
U.S. Department of Housing and
Urban Development

James T. Beall Jr.
Santa Clara County

Mark DeSaulnier
Contra Costa County

Bill Dodd
Napa County and Cities

Dorene M. Giacomini
U.S. Department of Transportation

Scott Haggerty
Alameda County

Barbara Kaufman
San Francisco Bay Conservation
and Development Commission

Sue Lempert
Cities of San Mateo County

John McLemore
Cities of Santa Clara County

Michael Nevin
San Mateo County

Bijan Sartipi
State Business, Transportation
and Housing Agency

James P. Spering
Solano County and Cities

Pamela Torliatt
Association of Bay Area Governments

Sharon Wright
Sonoma County and Cities

Shelia Young
Cities of Alameda County

Management Staff

Executive Director
Steve Heminger

Deputy Director, Operations
Ann Flemer

Deputy Director, Policy
Therese McMillan

General Counsel
Francis Chin

Manager of Finance
Brian Mayhew

*Manager of Bridge
and Highway Operations*
Rod McMillan

For additional information, please contact:

Peter Lee, Program Manager, RM-1
(510) 817-3206
plee@mtc.ca.gov

BAY AREA TOLL AUTHORITY

Regional Measure 1
Toll Bridge Projects

Project Monitoring Program

JULY 2004 PROGRESS REPORT




Prepared for
Metropolitan Transportation
Commission

Bay Area Toll Authority

Joseph P. Bort MetroCenter
101 Eighth Street
Oakland, California 94607
Tel: 510-464-7700
TDD/TTY: 510-464-7769
Fax: 510-464-7848
E-mail: info@mtc.ca.gov
Web: www.mtc.ca.gov



Prepared by
Bechtel Infrastructure Corporation




The following information is provided in accordance with California Government code Section 7550:

This document is one of a series of reports prepared for the Bay Area Toll Authority (BATA)/Metropolitan Transportation Commission (MTC) for the Regional Measure 1 Toll Bridge Program. The contract value for the monitoring efforts, technical analysis, and field site work which contribute to these reports, as well as the report preparation and production, is \$3,068,993.00.

TABLE OF CONTENTS

Regional Measure 1 Toll Bridge Program	1
Executive Summary - Status of Regional Measure 1 Projects, and Key Issues and Developments	
Northern Bridge Group	2
Southern Bridge Group	4
Cost Status Summary	6
Schedule Status Summary	7
Northern Bridge Group	
New Benicia-Martinez Bridge	8
Carquinez Bridge Replacement	10
Richmond-San Rafael Bridge Rehabilitation	12
Southern Bridge Group	
San Mateo-Hayward Bridge Widening	14
I-880/SR-92 Interchange Improvement	16
Dumbarton Bridge West Approach Projects	18
Appendices	
Appendix A: Project Budget Adjustments.	A-1
Appendix B: Current Approved Contract Change Orders (CCOs)	B-1
Appendix C: Project Cost Summary Details	C-1

REGIONAL MEASURE 1 TOLL BRIDGE PROJECTS

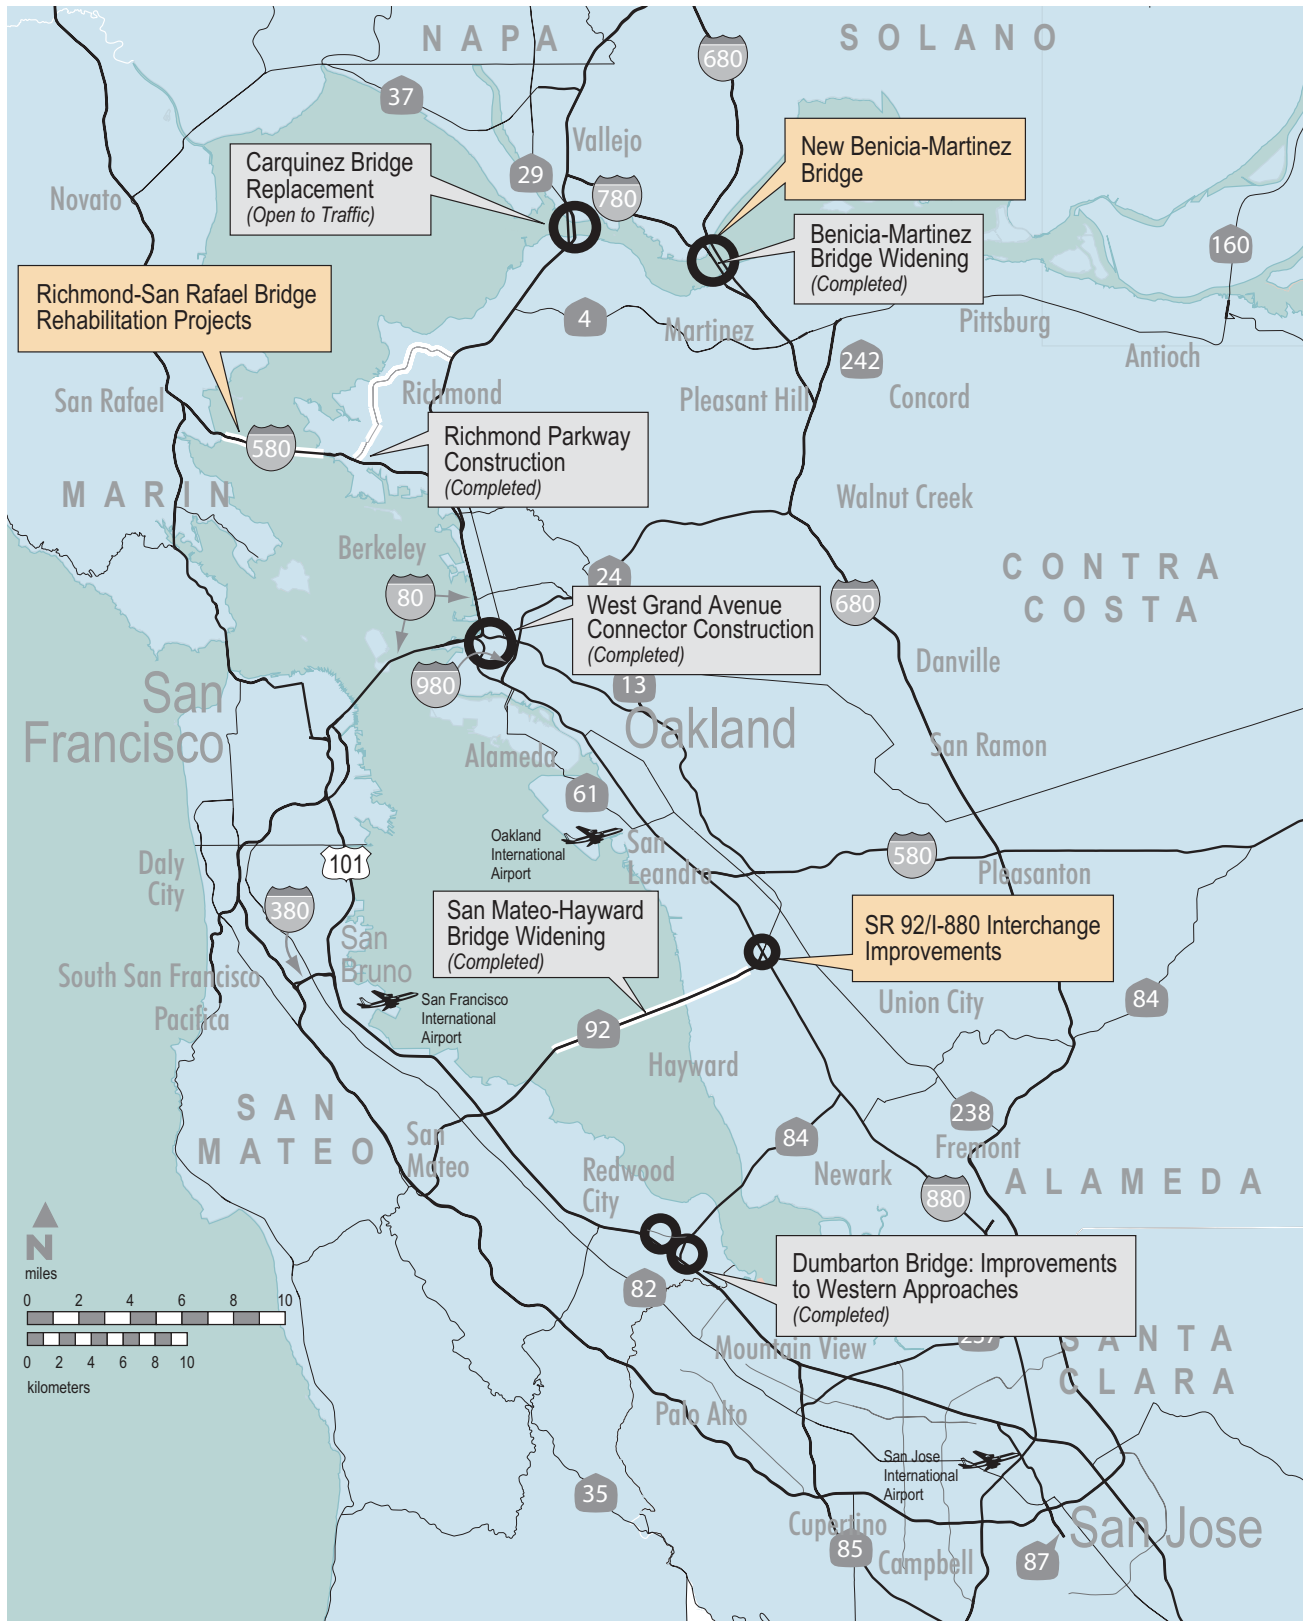

BAY AREA TOLL AUTHORITY

REGIONAL MEASURE 1 TOLL BRIDGE PROGRAM

In November 1988, Bay Area voters approved Regional Measure 1 (RM 1) and authorized a standard auto toll of \$1 for all seven state-owned Bay Area toll bridges. The additional revenues generated by the toll increase were identified for use for certain highway and bridge improvements, public transit rail extensions, and other projects that reduce congestion on the bridges.

RM 1 identified nine specific bridge and highway improvement projects as eligible for funding from the toll increase. The projects identified by RM 1 and their status of development are depicted in the map on the facing page and can be itemized as follows:

Northern Bridge Group Projects:

1. Widening of the existing Benicia-Martinez Bridge (completed; not included in this report)
2. Construction of a new bridge parallel to the existing Benicia-Martinez Bridge
3. Replacement of the existing western span of the Carquinez Bridge (open to traffic)
4. Major rehabilitation of the existing Richmond-San Rafael Bridge
 - Trestle and fender rehabilitation
 - Deck rehabilitation
5. Construction of an eastern approach (Richmond Parkway) between the Richmond-San Rafael Bridge and Interstate 80 near Pinole (non-Caltrans project; completed)

Southern Bridge Group Projects:

1. Construction of the West Grand Avenue connector to the San Francisco-Oakland Bay Bridge (completed; not included in this report)
2. Widening of the existing San Mateo-Hayward Bridge and eastern approach to six lanes (completed)
3. Improvement of the Interstate 880/State Route 92 interchange
4. Improvements to the western approaches to the Dumbarton Bridge
 - US 101/University Avenue interchange reconstruction (non-Caltrans project; completed)
 - State Route 84 (Bayfront Expressway) widening (completed).

MTC, BATA, AND THE CALIFORNIA STATE DEPARTMENT OF TRANSPORTATION (CALTRANS)

As the regional transportation planning agency for the San Francisco Bay Area, MTC is responsible for transportation planning, coordinating, and fund programming in the nine counties surrounding the Bay.

With SB 226, MTC, as the Bay Area Toll Authority (BATA), has also assumed certain duties previously held by the California Transportation Commission, including responsibilities for the programming, administration, and allocation of all toll revenues (excluding the seismic surcharge) from the state-owned toll bridges in the Bay Area.







Caltrans continues to be responsible for the ongoing operation of the state-owned bridges, including the collection of tolls, as well as the maintenance, rehabilitation, and capital improvement of the bridges.




PROJECT MONITORING PROGRAM

This report focuses on monitoring project cost and schedule performance for the Regional Measure 1 Toll Bridge Improvement Projects, as measured against approved budget and schedule milestones. The report provides comprehensive project status information at three levels of detail:

- Color-coded executive summary of Regional Measure 1 projects status (program level)
- Detailed status of individual bridge projects (project level)
- Supplemental project and contract information, including budget adjustments, approved construction change orders, and project and contract level cost data, in the appendices.

EXECUTIVE SUMMARY – STATUS OF REGIONAL MEASURE 1 PROJECTS

NORTHERN BRIDGE GROUP	COST	SCHEDULE
New Benicia-Martinez Bridge		
Carquinez Bridge Replacement		
Richmond-San Rafael Bridge Rehabilitation		







- Legend:**
-  Green = no variance to current budget/schedule
 -  Yellow = variance to current budget/schedule (trend), defined as follows:
For Cost: Project (BATA) contingency use may be required
For Schedule: Construction contract completion dates delayed by greater than 3 months
 -  Red = variance to current budget/schedule, defined as follows:
For Cost: Project budget change may be required
For Schedule: "New facility open to traffic" date delayed by greater than 3 months by non-weather-related issues




BAY AREA TOLL AUTHORITY

EXECUTIVE SUMMARY – STATUS OF KEY ISSUES AND DEVELOPMENTS

- On the new bridge contract, superstructure construction is in progress on the Martinez side and foundation work continues in the strait. Superstructure deck concrete is in place from the south abutment to Pier 4. Rock sockets are now installed for eight of twelve piers in the strait (four in deep water, four in shallow water). Rock socket installation is in progress at deep-water piers 12 and 14. At pier 8, the second stage of the footing is nearing completion and preparations are underway to start the first lift of the concrete column. Soffits were poured at pier tables 5 and 9; diaphragm formwork is in progress. The pier 7 footing is being precast at Mare Island.
 - In May, BATA approved a \$405 million budget adjustment for prior reported construction difficulties. Use of project contingency for future cost increases related to superstructure construction and support is still possible. Bechtel and BATA will continue to review cost issues.
 - On the I-680/I-780 interchange contract, column concrete is complete for bents 18 and 19 on the north shore. Soldier pile installation is in progress along Bayshore Road for construction at bent 20. Superstructure deck concrete is complete on the I-780 to I-680 connector overpass. The connector is forecast to open in September 2004. The southbound I-680 to westbound I-780 connector from Bayshore Road to the Park Road Overcrossing opened to traffic on June 26, 2004.
 - On the toll plaza contract, two of four slab-on-grade pours are complete. Formwork continues for tollbooths 8 to 17 on the completed slab. Formwork, and electrical conduit and rebar placement are in progress on the remaining two slabs. Structural steel canopy trusses are being erected between bents 2 and 3.
 - On the I-680/Marina Vista interchange contract, the northbound off-ramp at Marina Vista was opened on July 19, 2004. Earthmoving is now underway for the new main line to abutment 1. The approach slab for abutment 9 was placed on July 12, 2004.
-
- The replacement bridge opened to traffic on November 11, 2003. Call box installation is complete on the bridge. Punchlist work continues. Pedestrian railing is complete on the north bike path and at the Vista Point. The pedestrian/bike path opened to the public on May 15, 2004.
 - Construction completion of this contract is forecast for September 2004.
 - On the south approach and interchange contract, the I-80 Crockett Viaduct opened to traffic on November 11, 2003. The on-ramp from Crockett to westbound I-80 opened on December 9, 2003. The westbound off-ramp from the new bridge into Crockett opened on April 22, 2004. The eastbound off-ramp from I-80 into Crockett opened on May 24, 2004.
 - Construction completion of this contract is forecast for August 2004.
 - The Advertise date for the 1927 Bridge Demolition contract is forecast for August 2004.
 - The cost status code for the project is "yellow" due to construction claims, increasing cost of the demolition contract and increasing support costs. Caltrans is reviewing these costs to determine funding impacts.
-
- On the replacement westbound trestle, all piling and pile caps have been installed. All twenty-eight pre-cast deck sections have been installed eastward and exterior barrier rail installation is complete. On the replacement eastbound trestle, demolition and exterior pile installation continue eastward to bent 26 of 37. Sixteen precast pile caps have been placed and four deck sections have been installed.
 - In July, BATA approved a \$48.5 million request from Caltrans to accelerate repairs to various deck joints on the bridge via contract change order on the seismic retrofit project. By performing the work under a change order, the work will be completed 3 years earlier than originally planned. To fund this work, BATA is utilizing funds already budgeted for the work as part of the RM-1 Richmond-San Rafael Deck Rehabilitation Project and from the Toll Bridge Rehabilitation Program.

EXECUTIVE SUMMARY – STATUS OF REGIONAL MEASURE 1 PROJECTS

SOUTHERN BRIDGE GROUP	COST	SCHEDULE
San Mateo-Hayward Bridge Widening		
I-880/SR-92 Interchange Improvement		
Dumbarton Bridge West Approach Projects (Bayfront Expressway)		

- Legend:**
-  Green = no variance to current budget/schedule
 -  Yellow = variance to current budget/schedule (trend), defined as follows:
For Cost: Project (BATA) contingency use may be required
For Schedule: Construction contract completion dates delayed by greater than 3 months
 -  Red = variance to current budget/schedule, defined as follows:
For Cost: Project budget change may be required
For Schedule: “New facility open to traffic” date delayed by greater than 3 months by non-weather-related issues

BAY AREA TOLL AUTHORITY

EXECUTIVE SUMMARY – STATUS OF KEY ISSUES AND DEVELOPMENTS

- On the bridge-widening contract, both the new westbound and the reconstructed eastbound trestles are complete and fully operational. Caltrans has accepted the contract and is in the process of resolving claims and closing the contract.
 - Caltrans has concluded negotiations with the contractor to settle final claims on the trestle-widening contract and has requested a supplemental allocation of funds from BATA. In July, BATA approved a supplemental allocation of \$9.2 million to the contract from existing project savings and contingencies.
-
- The Federal Highway Administration (FHWA) approved the Final Environmental Impact Statement Report (FEIS/R) for the project on December 29, 2003. A Record of Decision (ROD) by FHWA was completed in July 2004.
 - The Caltrans Project Report was completed on December 31, 2003. Caltrans is currently preparing the plans, specifications, and estimates (PS&E) for the project. Sixty-five percent PS&E has been achieved. One hundred percent PS&E is forecast for January 2005.
 - Advance right of way acquisition (ROW) has started.
 - The status code for the project cost is "yellow," based on forecasted cost increases due to escalation and support. As the engineering design progresses, Bechtel will further review the cost estimates. The status code for the project schedule is "red", based on the currently forecasted 14 month delay to the completion date due to the delay of the environmental approval. BATA and Bechtel will review the forecasted schedule for options to expedite completion of the project.
-
- On the Bayfront Expressway widening contract, the widened expressway officially opened to traffic on July 29, 2003. Caltrans accepted the contract on January 15, 2004.
 - A follow-on contract has been awarded for environmental mitigation at the Ravenswood Triangle area. The work involves wetland reconstruction and habitat restoration for the salt-water harvest mouse.

COST STATUS SUMMARY (MILLION DOLLARS)

PROJECT	Baseline Budget (June 2000)	Current Budget (July 2004)	Current Forecast (July 2004)	Expended To Date (7/98 - 06/04)
Northern Bridge Group				
New Benicia-Martinez Bridge	586.0	1,057.8	1,057.8	571.8
Carquinez Bridge Replacement	433.2	486.3	511.9	438.6
Richmond-San Rafael Bridge Rehabilitation				
➤ West Trestle and Fender Rehabilitation	45.4	94.1	94.1	34.2
➤ Deck Rehabilitation	53.4	25.0	25.0	0.4
Richmond Parkway (Non-Caltrans) ¹	5.9	5.9	5.9	3.9
SUBTOTAL - NBG	1,123.9	1,669.1	1,694.7	1043.4
Southern Bridge Group				
San Mateo-Hayward Bridge Widening				
➤ Widening	203.6	217.5	210.5	196.0
➤ West Approach Replacement Planting	0.4	0.4	0.4	0.0
I-880/SR-92 Interchange Improvement	124.2	133.8	149.3	18.8
Dumbarton Bridge West Approach Projects				
➤ US-101/University Avenue Interchange Reconstruction (Non-Caltrans)	3.8	3.8	3.8	3.7
➤ Bayfront Expressway (SR-84) Widening	33.8	36.0	36.0	32.6
SUBTOTAL - SBG	365.7	391.4	399.9	251.1
GRAND TOTAL	1,489.6	2,060.5	2,094.6	1,299.9

BAY AREA TOLL AUTHORITY

SCHEDULE STATUS SUMMARY

PROJECT	New Facility Open to Traffic Baseline (June 2000)	New Facility Open to Traffic Current (July 2004)	New Facility Open to Traffic Forecast (July 2004)
<i>Northern Bridge Group</i>			
New Benicia-Martinez Bridge	Jan 04	Dec 06	Dec 06
Carquinez Bridge Replacement	Jan 03	Nov 03	Nov 03
Richmond-San Rafael Bridge Rehabilitation			
➤ West Trestle and Fender Rehabilitation ¹	Dec 04	Feb 05	May 05
➤ Deck Rehabilitation ¹	Sep 06	Jul 07	Dec 08
Richmond Parkway (<i>Non-Caltrans</i>)	Feb 01	May 01	May 01
<i>Southern Bridge Group</i>			
San Mateo-Hayward Bridge Widening			
➤ Widening	Dec 02	Nov 02	Nov 02
➤ West Approach Replacement Planting ¹	May 08	May 08	May 08
I-880/SR-92 Interchange Improvement	Dec 06	Jun 09	Aug 10
Dumbarton Bridge West Approach Projects			
➤ US-101/University Avenue Interchange Reconstruction (<i>Non-Caltrans</i>) ¹	Apr 00	Apr 00	Apr 00
➤ Bayfront Expressway (SR-84) Widening ¹	Mar 03	Jul 03	Jul 03

¹ For the Richmond-San Rafael Bridge Rehab, San Mateo-Hayward Bridge West Approach Planting, and Dumbarton Bridge West Approach projects, the dates shown reflect construction completion; the existing facility remains open to traffic during all phases of construction.

NEW BENICIA-MARTINEZ BRIDGE

The existing Benicia-Martinez Bridge provides Interstate 680 access across the Carquinez Strait between Contra Costa and Solano counties. This project will construct a new parallel Benicia-Martinez Bridge east of the existing span that will include the following features:

- Five northbound lanes on the new bridge (four mixed-flow lanes and one slow-vehicle lane) that will allow conversion of the existing bridge to southbound traffic only
- A new bicycle/pedestrian lane on the existing bridge
- A new toll plaza south of the new bridge in Contra Costa County with 17 toll booths, including two high-occupancy-vehicle (HOV) bypass lanes
- Reconstruction of the Interstate 680/Marina Vista Road and Interstate 680/Interstate 780 interchanges

Project Photos



New Bridge – Piers 8 and 9



New Bridge – Piers 14 to 19



New Bridge – Pier Table 5

Current Activities:

- On the new bridge contract, superstructure deck concrete is in place from the south abutment to pier 4. Rock socket installation is in progress at pier 12 with five of eight rock sockets complete and at pier 14 with three of eight rock sockets complete. Pier table 5 soffit pours occurred on July 1 and July 23, respectively. The soffit for pier table 9 was poured on July 30, 2004. Pier table diaphragm construction is in progress on piers 5 and 9. The second stage footing for pier 8 was poured on July 21, 2004 and rebar placement for the column is in progress. A precast footing for pier 7 is underway at Mare Island. Placement of pier 13 footing is forecast for late August 2004.
- On the I-680/I-780 interchange contract, superstructure deck concrete is in place on the I-780/I-680 connector overpass from the east abutment to the west abutment. Barrier rail installation and jacking of hinge 5 are in progress. Opening of the connector overpass is forecast for September 2004. On the Benicia shoreline, the concrete columns on westbound bents 18 and 19 are complete. Soldier piles are being driven along Bayshore Road for bent 20 construction. Embankment fill is being placed for I-780 westbound.
- On the toll plaza contract, the second of four concrete slabs-on-grade was poured on July 8, 2004. The concrete skirts for tollbooths 13 to 17 are complete. Formwork for tollbooths 8 to 12 is underway. Bottom mat rebar and in-slab conduit installation is underway on the two remaining slab quadrants. Structural steel canopy trusses are being erected between bents 2 and 3. On the Operations Building, electrical wiring is underway for the roof mounted HVAC units. The HVAC units for the toll plaza were set in the courtyard on July 27, 2004.
- On the I-680/Marina Vista interchange contract, paving is complete on the new Marina Vista off-ramp; the off-ramp opened to traffic on July 19, 2004. Mass earthwork for the main line is underway. Superstructure falsework is being erected between bents 4 and 6 over Waterfront Road and the railroad. The approach slab at abutment 9 was poured on July 12, 2004. Retaining wall 4 footings are being formed and poured.
- Bids for the Mitigation Site were opened on July 27, 2004.

BAY AREA TOLL AUTHORITY

NEW BENICIA-MARTINEZ BRIDGE

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (July 2004)	Current Forecast (July 2004)	Variance	Expended to Date (7/98 - 06/04)	Notes
Capital Outlay Construction						
South Approach	6.0	7.0	7.0	0.0	6.6	
New Bridge	247.3	644.9	644.9	0.0	339.2	A
Toll Plaza and Administration Building	22.8	24.3	24.3	0.0	15.0	
I-680/Marina Vista Interchange	43.2	51.5	51.5	0.0	33.9	
I-680/I-780 Interchange	80.8	54.7	57.0	2.3	39.3	B
Other Budgeted Capital	28.1	30.5	30.5	0.0	2.2	
Capital Outlay Support	78.2	155.6	155.6	0.0	103.9	A
Capital ROW	21.1	20.4	20.4	0.0	11.6	
Non-BATA Funding	0.0	31.0	31.0	0.0	20.1	
Project (BATA) Contingency	58.4	37.8	35.6	-2.3		B
Project Total (a)	586.0	1,057.8	1,057.8	0.0	571.8	A
(a) Totals may be rounded						


SCHEDULE STATUS	Baseline (June 2000)	Current (July 2004)	Forecast (July 2004)	Variance	Notes
Construction Contract Completion					
New Bridge	Jan 04	Dec 06	Apr 07	+4	
Toll Plaza and Administration Building	Feb 03	Jan 05	Apr 05	+4	
Toll Plaza Planting		Jul 05	Nov 05	+4	
I-680/Marina Vista Interchange	Dec 03	Jan 05	Nov 05	+10	C
I-680/I-780 Interchange	Dec 03	May 05	Jun 05	+1	
I-680/I-780 I/C Electrical Completion		May 05	Sep 05	+4	
South Approach	Mar 01	Oct 01	Oct 01	0	Complete
Modify Existing Bridge	Jul 05	Jul 08	July 08	0	
Project					
New Facility Open to Traffic	Jan 04	Dec 06	Dec 06	0	

NOTES	ACTION
A. BATA approved a \$405 million budget adjustment in May 2004 for prior reported construction difficulties associated with foundation piles and associated rock sockets, as well as for superstructure design adjustments and additional support.	The use of project contingency may be required for future cost increases related to superstructure construction and support. BATA will continue to review the issues.
B. Caltrans has reported potential change orders due to foundations and differing site conditions.	BATA and Bechtel are reviewing the potential cost increase.
C. Removal of contaminated soil delayed progress on the Marina Vista Interchange.	All contaminated soil has been removed successfully. Work continues to progress.

CARQUINEZ BRIDGE REPLACEMENT

The Carquinez Bridge has carried Interstate 80 traffic between the cities of Vallejo and Crockett on two separate bridges: the 1927 bridge for westbound traffic and the 1958 bridge for eastbound traffic. The 1958 bridge has been strengthened under Caltrans' seismic retrofit program; the 1927 bridge was identified as being seismically deficient and is being replaced under the RM 1 program. The Carquinez Bridge replacement project is a new suspension bridge west of the existing bridges. The existing 1927 bridge will be demolished after the completion of the replacement bridge and approaches. The project incorporates the following features:

- Four westbound lanes on the new bridge (three mixed-flow lanes and one HOV lane)
- A bicycle/pedestrian lane on the new bridge

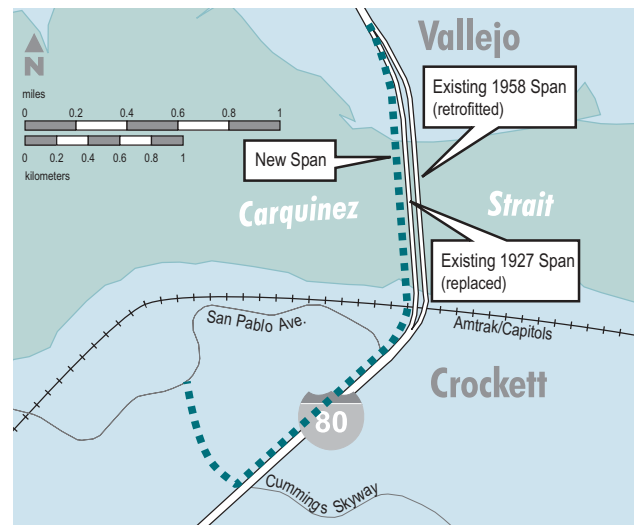

Project Photos



Carquinez South Interchange



Carquinez Bridges

Current Activities:

- On the replacement bridge and north approach contract, traffic was directed onto the new bridge on November 11, 2003. The pedestrian and bicycle path opened on May 15, 2004. Installation of pedestrian railing at the Vista Point is complete. Installation of call boxes is complete on the new bridge. Soil nailing/hillside stabilization under the north approach is complete. Miscellaneous punchlist, electrical and change order work continue for the contract. Construction completion of the contract is forecast for September 2004.
- On the south approach and interchange contract, the on-ramp to westbound I-80 opened on December 9, 2003. Kendall and Rio Del Vista streets re-opened to traffic in early January 2004. The westbound on-ramp opened on April 22, 2004. The eastbound off-ramp opened on May 24, 2004. Bridge deck grinding on the south viaduct to reduce the noise level was completed on July 16, 2004. Transition roadwork, signage, and asphalt paving are nearing completion for the temporary approach from the north end of the 1927 Bridge to the toll plaza, in preparation for the deck rehabilitation of the 1958 Bridge. Construction completion of the contract is forecast for August 2004.
- The Advertise date for the 1927 Bridge Demolition contract is forecast for August 2004.

BAY AREA TOLL AUTHORITY

CARQUINEZ BRIDGE REPLACEMENT

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (July 2004)	Current Forecast (July 2004)	Variance	Expended to Date (7/98 - 06/04)	Notes
Capital Outlay Construction						
Replacement Bridge and North Approach	213.7	251.7	251.7	0.0	242.6	A
South Approach and Interchange	116.0	73.9	73.9	0.0	65.8	A
Maintenance Facility (Phases I & II)	7.0	8.1	8.1	0.0	7.9	
1927 Bridge Demolition	16.0	16.0	33.4	17.4	0.0	A, B
Other Budgeted Capital	10.6	10.8	8.8	-2.0	6.4	
Capital Outlay Support	43.7	114.2	121.1	6.9	106.3	A
Capital ROW	9.6	9.6	11.5	1.9	9.6	A
Project (BATA) Contingency	16.5	1.9	3.5	1.6		A
Project Total (a)	433.2	486.3	511.9	25.6	438.6	A

(a) Totals may be rounded

SCHEDULE STATUS	Baseline (June 2000)	Current (July 2004)	Forecast (July 2004)	Variance	Notes
Construction Contract Completion					
Replacement Bridge and North Approach	Dec 03	Aug 04	Sep 04	+1	
South Approach and Interchange (Phase 1)	Feb 03	Nov 03	Nov 03	0	Complete
South Approach and Interchange (Phase 2)		Oct 04	Aug 04	-2	
Maintenance Facility	Mar 02	Sep 02	Sep 02	0	Complete
1927 Bridge Demolition	Mar 06	Mar 06	Mar 06	0	
Project					
New Facility Open to Traffic	Jan 03	Nov 03	Nov 03	0	

NOTES	ACTION
A. Based on current information, potential claims and additional support services costs may increase the total project cost by an additional \$25 million for a total project cost of \$512 million. Bechtel will assist in the review of potential claims and support cost increases on the project. The results of this review will be included in a future PMP report.	Caltrans is working with the contractors to properly evaluate these potential construction cost increases, and is in the process of submitting an update of the support budget, which may require additional funds.
B. A recent check estimate for demolition of the 1927 Bridge indicates a potential cost increase which will require funds in excess of the current project contingency. BATA plans to adopt a revised budget after bids are opened in October.	Bechtel is updating its check estimate with current information provided by Caltrans, and will advise BATA of its findings.


RICHMOND-SAN RAFAEL BRIDGE REHABILITATION

Completed in 1956, the Richmond-San Rafael Bridge provides access - via Interstate 580 - across San Francisco Bay between Marin and Contra Costa counties. Major rehabilitation of the bridge was specified in RM 1 to be eligible for toll funding.

Currently, there are two major rehabilitation projects planned for the bridge:

- The first project is to replace the western trestle (low-rise) section of the bridge near San Rafael and rehabilitate the ship collision protection fender system at various bridge piers. This rehabilitation work is being combined with a seismic retrofit project.
- The second project is to rehabilitate the existing concrete deck on the bridge. The cast-in-place concrete riding surface (deck) has been worn over


time due to traffic and exposure to the marine environment. This project will follow the completion of the trestle and fender rehabilitation project to avoid possible construction conflicts.

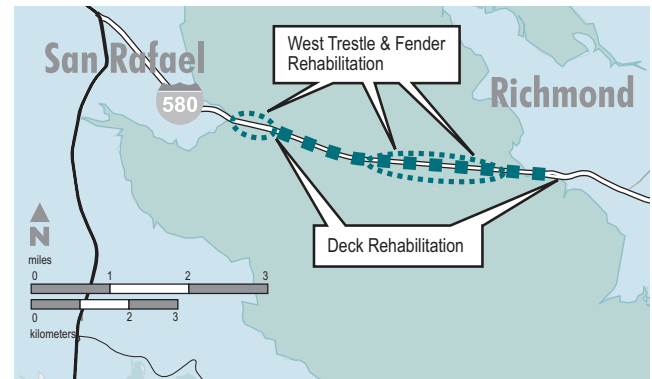

Project Photos



Trestle Replacement Looking East

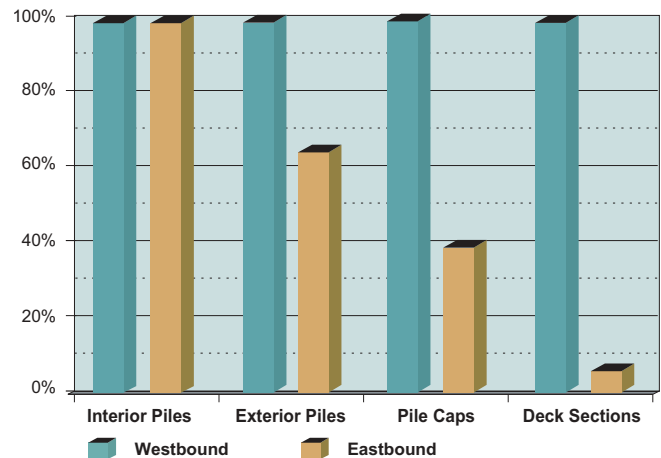

Trestle Progress

Current Activities:

- The west trestle replacement consists of rebuilding the eastbound and westbound trestles near San Quentin. The trestles are parallel for most of their length and diverge to carry traffic onto or from the upper or lower deck of the main bridge. The westbound trestle, serving the upper deck, is 2,844 feet between Bents 1 and 29; the eastbound trestle, serving the lower deck, is 3,635 feet between Bents 1 and 37. The trestle replacement procedure consists of demolishing linear section of interior bridge deck, installing a temporary interior work trestle, and installing interior sixty-six inch cast-in-drilled-hole (CIDH) piles at the mid-span of every other existing 50-foot deck section. When installation of the interior piles is advanced, a similar operation is repeated on the exterior, where a section of exterior bridge deck is removed and exterior piles are installed. Pile caps are cast in place below the existing superstructure, on the new piles. One trestle at a time is closed at night for superstructure replacement. During closure, two of the existing 50-foot sections are removed and replaced with one new 100-foot precast section.
- On the trestle replacement, interior pile installation is complete and the interior work trestle is removed. On the eastbound trestle, demolition and exterior pile installation continue eastward to bent 26. Working west to east, sixteen pile caps are placed and four 100' deck panels are placed. On the westbound trestle, all pre-cast deck sections are placed and exterior barrier rail is complete.
- In July, BATA approved a \$48.5 million request from Caltrans to accelerate repairs to various deck joints on the bridge via contract change order on the seismic retrofit project. By performing the work under a change order, the work will be completed 3 years earlier than originally planned.

BAY AREA TOLL AUTHORITY

RICHMOND-SAN RAFAEL BRIDGE REHABILITATION

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (July 2004)	Current Forecast (July 2004)	Variance	Expended to Date (7/98 - 06/04)	Notes
West Trestle and Fender Rehabilitation						
Capital Outlay Construction	33.9	57.2	57.2	0.0	3.9	A
Capital Outlay Support	5.4	2.3	2.3	0.0	1.0	A
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Non-BATA Funding	0.0	34.6	34.6	0.0	29.3	
Project (BATA) Contingency	6.1	0.0	0.0	0.0		
Subtotal	45.4	94.1	94.1	0.0	34.5	
Deck Rehabilitation						
Capital Outlay Construction	33.0	16.9	16.9	0.0	0.0	A
Capital Outlay Support	9.0	4.0	4.0	0.0	0.4	A
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Non-BATA Funding	0.0	4.0	4.0	0.0	0.0	
Project (BATA) Contingency	11.4	0.1	0.1	0.0		
Subtotal	53.4	25.0	25.0	0.0	0.4	
Project Total (a)	98.9	119.2	119.2	0.0	34.5	
(a) Totals may be rounded						


SCHEDULE STATUS	Baseline (June 2000)	Current (July 2004)	Forecast (July 2004)	Variance	Notes
Construction Contract Completion					
West Trestle and Fender Rehabilitation	Dec 04	Feb 05	May 05	+3	A
Deck Rehabilitation	Sep 06	Jul 07	Jan 07	-7	A
Project					
New Facility Open to Traffic					B

NOTES	ACTION
A. Scope of work and funds for the RM-1 and Rehab Programs have been consolidated between the seismic retrofit/trestle/fender/interim deck repairs/deck joint work and the deck overlay rehabilitation project.	None.
B. The existing facility remains open to traffic during all phases of construction.	None.

SAN MATEO-HAYWARD BRIDGE WIDENING

In 1996, the western approach to the San Mateo-Hayward Bridge from U.S. Route 101 was widened from four to six lanes to match the configuration of the high-rise section of the bridge. The current project completed the widening work in this corridor along the low-trestle section of the bridge and its eastern approach to Interstate 880. The project includes the following features:

- Widening of the low-rise trestle and eastern approach from I-880 from four to six lanes with shoulders
- Extension of the existing west-bound HOV lane one mile west along the eastern approach from Interstate 880
- Construction of a new pedestrian/bicycle overcrossing of State Route 92
- Expansion of the existing toll plaza
- Improvements to the Hayward Shoreline Interpretive Center

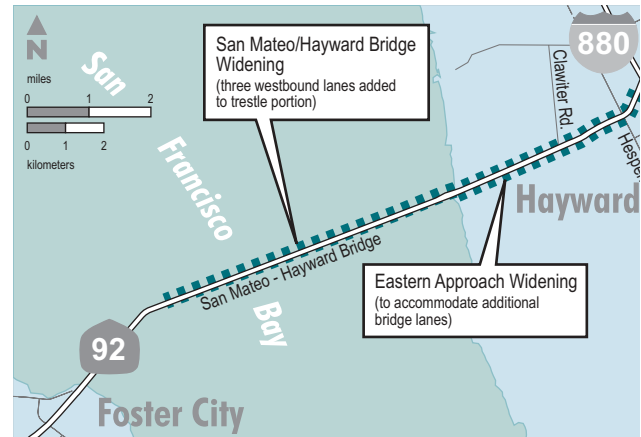

Project Construction Progress and Photos



Trestle Looking West



Mini Toll Plaza

Current Activities:

- On the bridge-widening contract, construction is complete and both trestles are open to traffic. Caltrans accepted the contract on March 6, 2003 and is in the process of closing the contract and resolving claims on the project.
- Caltrans has concluded negotiations with the contractor to settle final claims on the trestle-widening contract and has requested a supplemental allocation of funds from BATA. In July, BATA approved a supplemental allocation of \$9.2 million to the contract from existing project savings and contingencies.

BAY AREA TOLL AUTHORITY

SAN MATEO-HAYWARD BRIDGE WIDENING

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (July 2004)	Current Forecast (July 2004)	Variance	Expended to Date (7/98 - 06/04)	Notes
Widening						
Capital Outlay Construction						
Widen Trestle	124.8	138.1	138.1	0.0	126.9	A
Widen Roadway	29.2	26.1	25.5	-0.6	25.5	
Construct Mini Toll Plaza	4.4	6.3	6.0	-0.3	6.0	
Other Budgeted Capital	8.9	8.6	5.5	-3.1	3.5	
Capital Outlay Support	15.5	34.4	34.3	-0.1	33.6	
Capital ROW	1.5	1.5	0.5	-1.0	0.5	
Project (BATA) Contingency	19.3	2.5	0.6	-2.0		A
Subtotal	203.6	217.5	210.5	-7.0	196.0	B
West Approach Planting						
Capital Outlay Construction	0.2	0.2	0.2	0.0	0.0	
Capital Outlay Support	0.1	0.1	0.1	0.0	0.0	
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Project (BATA) Contingency	0.1	0.1	0.1	0.0		
Subtotal	0.4	0.4	0.4	0.0	0.0	
Project Total (a)	204.0	217.9	210.9	-7.0	196.0	
(a) Totals may be rounded						

SCHEDULE STATUS	Baseline (June 2000)	Current (July 2004)	Forecast (July 2004)	Variance	Notes
Construction Contract Completion					
Widening					
Widen Trestle	Dec 02	Feb 03	Feb 03	0	Complete
Construct Mini Toll Plaza	Nov 02	Nov 02	Nov 02	0	Complete
Widen Eastern Approach	Nov 02	Sep 01	Sep 01	0	Complete
Pedestrian Overcrossing	Sep 02	Sep 02	Sep 02	0	Complete
West Approach Planting					
West Approach Replacement Planting	May 08	May 08	May 08	0	
Project					
New Facility Open to Traffic	Dec 02	Nov 02	Nov 02		Complete

NOTES	ACTION
-------	--------

A. Final settlement of outstanding claims required utilization of project contingency.


Caltrans has concluded negotiations with the contractor to resolve outstanding claims

B. BATA will be closing out completed contracts and moving any

BATA is reviewing project budgets and

I-880/SR-92 INTERCHANGE IMPROVEMENT


As part of an effort to improve traffic flow and to relieve congestion on the San Mateo-Hayward Bridge and its approaches, RM 1 identified the need to improve and reconstruct the Interstate 880/State Route 92 interchange. The project proposes to modify the existing cloverleaf interchange to increase capacity and improve safety and traffic operations. Various alternatives has been considered and assessed as part of the environmental process.

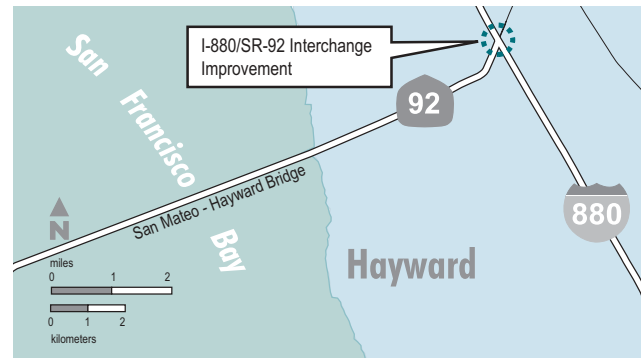

Project Photos



Existing Interchange; looking west

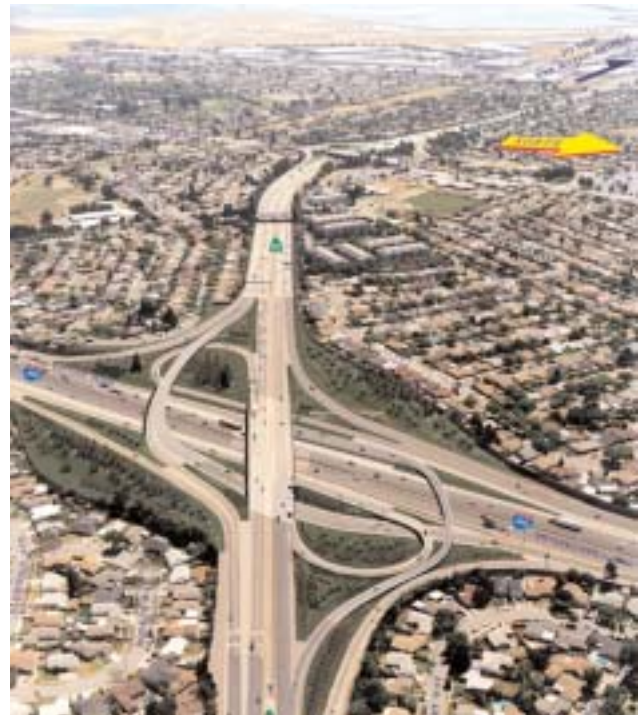

Alternative H Interchange; looking west

Current Activities:

- The Federal Highway Administration (FHWA) approved the Final Environmental Impact Statement Report (FEIS/R) for the project on December 29, 2003. A Record of Decision (ROD) was prepared by FHWA and completed in July 2004.
- The Caltrans Project Report was completed on December 31, 2003. Caltrans is currently preparing the plans, specifications, and estimates (PS&E) for the project. Sixty-five percent PS&E was achieved in April 2004. One hundred percent PS&E is forecast for January 2005.
- Advance right of way acquisition (ROW) has started.
- Based on forecasted cost increases due to escalation and support, the status code for the project cost is "yellow." As the engineering design progresses, Bechtel will further review the cost estimates.

BAY AREA TOLL AUTHORITY

I-880/SR 92 INTERCHANGE IMPROVEMENT

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (July 2004)	Current Forecast (July 2004)	Variance	Expended to Date (7/98 – 06/04)	Notes
I-880/SR-92 Interchange Improvement						
Capital Outlay Construction	70.3	85.2	84.7	-0.5	0.0	A
Capital Outlay Support	20.8	23.9	35.1	11.2	18.8	A
Capital ROW	8.0	9.9	9.9	0.0	0.0	
Non-BATA Funding	0.0	9.6	9.6	0.0		
Project (BATA) Contingency	25.1	5.3	10.1	4.8		A
Project Total (a)	124.2	133.8	149.3	15.5	18.8	A

(a) Totals may be rounded

SCHEDULE STATUS	Baseline (June 2000)	Current (July 2004)	Forecast (July 2004)	Variance	Notes
Construction Contract Completion					
I-880/SR-92 Interchange Improvement	Dec 06	Jun 09	Aug 10	+14	A
Project					
New Facility Open to Traffic	Dec 06	Jun 09	Aug 10	+14	A

NOTES	ACTION
A. Later than anticipated approval of the final environmental clearance documents has significantly delayed project delivery by 14 months. The delay has also increased project cost due to lengthened support involvement and escalation. The forecasted schedule is still has an aggressive right-of-way clearance schedule of 18 months to clear numerous parcels in the project area.	Bechtel will be preparing a check estimate based on a Caltrans 65% engineering design and will be reviewing the project schedule to investigate options to expedite completion and Caltrans' revised support budget for the project.

DUMBARTON BRIDGE WEST APPROACH PROJECTS

RM 1 identified the need for improvements to the western approaches to the Dumbarton Bridge. Through coordination with the City/County Association of Governments of San Mateo County, two projects were identified for toll bridge funding:

- The first project, sponsored by the City of East Palo Alto, modified the U.S. Route 101/University Avenue interchange. This project was designed to alleviate traffic congestion and improve overall traffic flow to University Avenue and the Dumbarton Bridge.
- The second project, sponsored by Caltrans, widened the Bayfront Expressway (State Route 84) from the Dumbarton Bridge to the U.S. 101/Marsh Road interchange. The six-lane expressway section from the bridge to University Avenue is reconstructed with upgraded shoulders and lane widths. The existing expressway section from University Avenue to Marsh Road is widened from four to six lanes.



Project Photos



Bayfront at Willow Westbound



Bayfront at University Eastbound

Current Activities:

- The Bayfront Expressway (SR-84) widening contract was officially opened to traffic on July 29, 2003. Caltrans accepted the contract on January 15, 2004.
- A follow-on contract has been awarded at the Ravenswood Triangle for wetland reconstruction and habitat restoration for the salt-water harvest mouse.

BAY AREA TOLL AUTHORITY

DUMBARTON BRIDGE WEST APPROACH PROJECTS

COST STATUS (\$ Million)	Baseline Budget (June 2000)	Current Budget (July 2004)	Current Forecast (July 2004)	Variance	Expended to Date (7/98 – 06/04)	Notes
US101/University Avenue Interchange Reconstruction (Non-Caltrans)						
Capital Outlay Construction	3.8	3.8	3.8	0.0	3.7	
Capital Outlay Support	0.0	0.0	0.0	0.0	0.0	
Capital ROW	0.0	0.0	0.0	0.0	0.0	
Subtotal	3.8	3.8	3.8	0.0	3.7	
Bayfront Expressway (SR84) Widening						
Capital Outlay Construction	24.8	26.5	26.5	0.0	24.6	
Capital Outlay Support	4.4	8.6	8.6	0.0	7.8	
Capital ROW	1.3	0.2	0.2	0.0	0.2	
Project Contingency (BATA)	3.3	0.8	0.8	0.0		
Subtotal	33.8	36.0	36.0	0.0	32.6	
Project Total (a)	37.6	39.8	39.8	0.0	36.3	
(a) Totals may be rounded						


SCHEDULE STATUS	Baseline (June 2000)	Current (July 2004)	Forecast (July 2004)	Variance	Notes
Construction Contract Completion					
US 101/University Avenue Interchange Reconstruction (Non-Caltrans)	Apr 00	Apr 00	Apr 00	0	Complete
Bayfront Expressway (SR84) Widening	Mar 03	Jan 04	Jan 04	0	Complete
Project					
New Facility Open to Traffic	Mar 03	Jul 03	Jul 03	0	Complete
NOTES			ACTION		

APPENDICES

Appendix A: Project Budget Adjustments

Appendix B: Current Approved Contract Change Orders

Appendix C: Project Cost Summary Details



BAY AREA TOLL AUTHORITY

APPENDIX A – LIST OF PROJECT BUDGET ADJUSTMENTS

DEFINITIONS:

Baseline Budget (June 2000): Baseline budgets as established by BATA in June 2000 for each project within the overall program.

Current Budget: Budget currently serving as the baseline for monitoring purposes. The current budget is equal to the established June 2000 budget, plus or minus any adjustment as listed below.

Project Baseline Adjustments

Date	Description of Adjustment
10/2000	Current Budgets for allocated capital outlay adjusted by BATA to reflect current Caltrans construction contract allotments.
11/2000	Current Budgets for the Benicia-Martinez and Richmond-San Rafael Bridge projects revised to reflect new funding from Non-BATA sources per agreements with Caltrans and a Prop. 192 refund from Caltrans related to the Carquinez Bridge project.
01/2001	Current Budget for the Benicia-Martinez Bridge revised to reflect allocations by BATA.
03/2001	Current Budget for the Carquinez Bridge revised by BATA.
10/2001	Current Budget for the Benicia-Martinez Bridge revised by BATA.
12/2001	Current Budgets for the Benicia-Martinez and San Mateo-Hayward Bridges revised by BATA.
06/2003	Current Budget for the Bayfront Widening project revised by BATA.
05/2004	Current Budget for the Benicia-Martinez Bridge project revised by BATA.
07/2004	Current Budget for for Richmond-San Rafael Bridge project revised by BATA to reflect transfer of scope and funds from Rehab Program.

BAY AREA TOLL AUTHORITY

**APPENDIX B – APPROVED CONTRACT CHANGE ORDERS (CCO)
FOR JULY 2004
BENICIA-MARTINEZ BRIDGE**

Bridge/ Contract	CCO Number ¹	CCO Description	Funding Source ²	Impacts	
				Cost (\$1000's)	Schedule (Days)
New Bridge 04-006034	109.0	Pile Remediation (Anomaly Repair & Stuck Casing)	C	2,000.0	
	110.0	Construction Joint Repair	C	13,000.0	
	111.0	Marine Transportation	C	1,500.0	
	113.0	Cage Centralization	C	100.0	
Subtotal				16,600.0	
Toll Plaza 04-006044	45.1	Reinforcement Modification for Bents 1, 2, 3	C	215.8	112
	76.0	(Time Adjust)	C	10.0	
	79.0	Treadle Revision	C	4.1	
		Miscellaneous OB Revisions			
Subtotal				229.9	
MV/680 Interchange 04-006054	24.2	Tesoro Pipeline Support (Time Adjustment)	C	48.0	8
	25.3	Contaminated Materials (Time Adjustment)	C	198.0	33
	26.3	"WR" Cut-off Wall Revision/Pipe Piling (Time Adjustment)	C	96.0	16
	31.5	Additional Water Treatment	C	500.0	
	34.1	Stand-by Time 12/1/03-3/4/04	C	50.0	
	41.0	Drainage System "6"	C	3.4	
	46.0	Insulfoam EPS Blocks	C	58.0	
Subtotal				953.4	
680/780 Interchange 04-006064	1.2	Flagging and Traffic Control		50.0	
	8.1	Photo Identification Badges		20.5	
	22.2	W. Arsenal Type R Slab and "A" Seal		5.5	
	40.1	Bent 18/9 Rebar Tube Revisions		7.3	
	78.1	Rebar Substitution – Use of Grade A615		0.0	
Subtotal				83.3	
South Approach 04-006094		Contract is Complete			
Totals for July 2004				17,866.6	

¹ Only approved CCOs for the month are listed in Appendix B.

² Funding Source(s) S = Supplemental work C = Construction contingency

BAY AREA TOLL AUTHORITY

**APPENDIX B – APPROVED CONTRACT CHANGE ORDERS (CCO)
FOR JULY 2004
CARQUINEZ BRIDGE**

Bridge/ Contract	CCO Number ¹	CCO Description	Funding Source ²	Impacts	
				Cost (\$1000's)	Schedule
Carquinez Bridge Replacement 04-013014	37	Superstructure Adjustment for I/C Project	C	48.9	
	98.1	Maintenance Traveler Redesign and Delay Costs	C	1,225.8	
	106.0	North End Asphalt Concrete Overlay	C	136.0	
	113.0	Revisions to Security Systems	C	11.5	
	155.0	Deck Lifting/Steel Work Equipment Delay Costs	C	191.1	
Subtotal				1,613.3	
Crockett Interchange 04-013054	32	Retaining Wall Stay Plates	C	89.7	
	63.2	Consolidate Construction and PI Trailer	C	5.0	
	85.1	EB Gore Area Grade Differential	C	14.0	
	99.4	Additional AC Pavement Repairs	C	80.0	
	164	Striping & Sign Changes at VDR/KA	C	4.9	
	167	Architectural and Landscape Changes	C	50.0	
Subtotal				243.6	
Maintenance Facility 04-013084		Contract is complete			
Subtotal					
Totals for July 2004				1,856.8	

¹ Only approved CCOs for the month are listed in Appendix B.

² Funding Source(s)
S = Supplemental work
C = Construction contingency

BAY AREA TOLL AUTHORITY

APPENDIX C – PROJECT COST SUMMARY DETAILS

The following sheets provide detailed cost information for each of the bridge projects. Capital Outlay Support (Engineering), Capital Right-of-Way and Capital Outlay are shown for each of the projects. The Project (BATA) Contingency, as well as the bridge projects totals, is shown at the end of each bridge summary.

Definitions:

1. Capital Outlay Support includes both Caltrans and Architectural/Engineering (A/E) consultant support.
2. Capital Right of Way includes acquisition, loss of goodwill, demolition, utilities relocations, relocation assistance, title costs, and sale of excess lands.
3. Capital Outlay includes construction bid terms, external third party agreements, state-furnished materials, supplemental construction work, and construction contingencies.

Project Cost Summaries (\$ Millions)						
EA Number	Baseline Budget Jun-00	Current Budget Jul-04	Current Forecast Jul-04	Net Change	Expended ¹ to Date (7/98 – 06/04)	Note
Northern Bridge Group						
<i>Project 2003 – New Benicia-Martinez Bridge</i>						
South Approach						
Capital Outlay Support	00609x	3.5	3.6	3.6	0.0	3.6
Capital Right of Way	006099	7.0	7.7	7.7	0.0	7.2
Capital Outlay	006094	6.0	7.0	7.0	0.0	6.6
Total South Approach		16.5	18.4	18.4	0.0	17.5
New Bridge						
Capital Outlay Support	00603x	31.9	84.9	84.9	0.0	48.3
Capital Right of Way	006039	4.1	8.4	8.4	0.0	0.9
Capital Outlay	006034	247.3	644.9	644.9	0.0	339.2
Non-BATA Funding		0.0	10.1	10.1	0.0	7.6
Total New Bridge		283.3	748.4	748.4	0.0	396.1
Toll Plaza & Administration Building						
Capital Outlay Support	00604x	6.2	11.9	11.9	0.0	11.0
Capital Right of Way	006049	0.0	0.0	0.0	0.0	0.0
Capital Outlay	006044	22.8	24.3	24.3	0.0	15.0
Total Toll Plaza & Admin.		29.1	36.2	36.2	0.0	26.0
I-680/Marina Vista Interchange						
Capital Outlay Support	00605x	10.7	18.2	18.2	0.0	15.7
Capital Right of Way	006059	7.4	2.0	2.0	0.0	2.0
Capital Outlay	006054	43.2	51.5	51.5	0.0	33.9
Total I-680/MV I/C		61.4	71.7	71.7	0.0	51.6
I-680/I-780 Interchange						
Capital Outlay Support	00606x	18.7	24.8	24.8	0.0	21.1
Capital Right of Way	006069	1.7	1.7	1.7	0.0	1.4
Capital Outlay	006064	80.8	54.7	57.0	2.3	39.3
Non-BATA Funding		0.0	20.9	20.9	0.0	12.5
Total I-680/I-780 I/C		101.2	102.2	104.4	2.3	74.3

¹ Unaudited

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Jul-04	Current Forecast Jul-04	Net Change	Expended to Date (7/98 – 06/04)	Note
Project 2003 – New Benicia-Martinez Bridge (cont'd)							
Other Budgeted Capital							(a)
Capital Outlay Support		7.1	12.1	12.1	0.0	4.1	
Capital Right of Way		0.9	0.5	0.5	0.0	0.0	
Capital Outlay		28.1	30.5	30.5	0.0	2.2	
Total Other Budgeted Capital		36.1	43.1	43.1	0.0	6.3	
Total Capital Outlay Support		78.2	155.6	155.6	0.0	103.9	
Total Capital Right of Way		21.1	20.4	20.4	0.0	11.6	
Total Capital Outlay		428.2	813.0	815.2	2.3	436.2	
Non-BATA Funding		0.0	31.0	31.0	0.0	20.1	
Project Contingency (BATA)		58.4	37.8	35.6	-2.3		
Total New Benicia-Martinez Bridge		586.0	1,057.8	1,057.8	0.0	571.8	
Project 3002 – Carquinez Bridge Replacement							
Replacement Bridge and North Approach							(b)
Capital Outlay Support	01301x	17.7	66.8	66.8	0.0	65.9	
Capital Right of Way	013019	3.0	3.0	3.4	0.4	3.3	
Capital Outlay	013014	213.7	251.7	251.7	0.0	242.6	
Total Replacement Bridge and North Approach		234.4	321.5	321.9	0.4	311.8	
South Approach and Interchange							(c)
Capital Outlay Support	01305x	22.7	31.5	31.5	0.0	30.8	
Capital Right of Way	013059	5.0	5.0	5.1	0.1	4.9	
Capital Outlay	013054	116.0	73.9	73.9	0.0	65.8	
Total South Approach & I/C		143.7	110.3	110.4	0.1	101.5	
Maintenance Facility Phase I & II							(d)
Capital Outlay Support		0.7	5.1	4.5	-0.6	4.4	
Capital Right of Way		1.6	1.6	1.6	0.0	1.4	
Capital Outlay		7.0	8.1	8.1	0.0	7.9	
Total Maintenance Facility Ph I & II		9.3	14.8	14.2	-0.6	13.7	
Demolition – 1927 Bridge							
Capital Outlay Support	01309x	2.0	9.0	16.0	7.0	4.0	
Capital Right of Way	013099	0.0	0.0	0.3	0.3	0.0	
Capital Outlay	013094	16.0	16.0	33.4	17.4	0.0	
Total Demo – 1927 Bridge		18.0	25.0	49.7	24.7	4.0	

Notes

- (a) Includes EA 00601*, 00608*, 0060A*, 0060C*, 0060E*, 0060F*, 0060G*, 0060H*
- (b) Includes EA 00453*, 01301*, 01303*, 01304*
- (c) Includes EA 01302*, 01305*, 04700*
- (d) Includes EA 00607*, 01308*

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Jul-04	Current Forecast Jul-04	Net Change	Expended to Date (7/98 – 06/04)	Note
Project 3002 - Carquinez Bridge Replacement (cont'd)							
Other Budgeted Capital							(e)
Capital Outlay Support		0.6	1.8	2.2	0.4	1.3	
Capital Right of Way		0.0	0.0	1.1	1.1	0.0	
Capital Outlay		10.6	10.8	8.8	-2.0	6.4	
Total Other Budgeted Capital		11.2	12.7	12.1	-0.6	7.6	
Total Capital Outlay Support		43.7	114.2	121.1	6.9	106.3	
Total Capital Right of Way		9.6	9.6	11.5	1.9	9.6	
Total Capital Outlay		363.3	360.5	375.8	15.3	322.6	
Project (BATA) Contingency		16.5	1.9	3.5	1.6		
Total Carquinez Bridge		433.2	486.3	511.9	25.6	438.6	
Project 4003 - Richmond-San Rafael Bridge – West Trestle and Fender Rehabilitation							
Capital Outlay Support	0438Ux	5.4	2.3	2.3	0.0	1.0	(f)
Capital Right of Way	0438U9	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	0438U4	33.9	57.2	57.2	0.0	3.9	
Non-BATA Funding		0.0	34.6	34.6	0.0	29.3	
Project (BATA) Contingency		6.1	0.0	0.0	0.0		
Total R-SR Bridge – West Trestle and Fender Rehabilitation		45.4	94.1	94.1	0.0	34.2	
Project 4002 - Richmond-San Rafael Bridge – Deck Rehabilitation							
Capital Outlay Support	04152x	9.0	4.0	4.0	0.0	0.4	
Capital Right of Way	041529	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	041524	33.0	16.9	16.9	0.0	0.0	
Non-BATA Funding		0.0	4.0	4.0	0.0	0.0	
Project (BATA) Contingency		0.1	0.1	0.1	0.0		
Total R-SR Bridge – Deck Rehab		25.0	25.0	25.0	0.0	0.4	
Richmond Parkway (Non-Caltrans)							
Capital Outlay Support	non-Caltrans	0.0	0.0	0.0	0.0	0.0	
Capital Right of Way	non-Caltrans	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	non-Caltrans	5.9	5.9	5.9	0.0	3.9	(g)
Total Richmond Parkway		5.9	5.9	5.9	0.0	3.9	
Total Northern Bridge Group		1,123.9	1,669.1	1,682.6	13.5	1,048.7	

Notes

(e) Includes EA 01306*, 01307*, 0130A*, 0130C*, 0130D*, 0130F*, 0130G*, 0130H*, 0130J*, 0130X*

(f) Includes EA 04382*, 04383*, 0438U*

(g) Total reimbursements made to the City of Richmond for current allocation.

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Jul-04	Current Forecast Jul-04	Net Change	Expended to Date (7/98 – 06/04)	Note
Southern Bridge Group							
Project 6004 – San Mateo-Hayward Bridge Widening							
Widen Trestle							
Capital Outlay Support	04501x	7.9	21.3	21.3	0.0	21.2	(h)
Capital Right of Way	045019	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	045014	124.8	138.1	138.1	0.0	126.9	
Total Widen Trestle		132.7	159.4	159.4	0.0	148.1	
Widen Roadway							
Capital Outlay Support	04503x	4.3	6.0	6.0	0.0	6.0	
Capital Right of Way	045039	1.0	0.0	0.0	0.0	0.0	
Capital Outlay	045034	29.2	26.1	25.5	-0.6	25.5	
Total Widen Roadway		34.5	32.0	31.4	-0.6	31.4	
Construct Mini Toll Plaza							
Capital Outlay Support	04502x	1.7	2.4	2.4	0.0	2.4	
Capital Right of Way	045029	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	045024	4.4	6.3	6.0	-0.3	6.0	
Total Mini Toll Plaza		6.1	8.6	8.4	-0.3	8.4	
Other Budgeted Capital							
Capital Outlay Support		1.6	4.7	4.7	0.0	4.1	(i)
Capital Right of Way		0.5	1.5	0.5	-1.0	0.5	
Capital Outlay		8.9	8.6	6.6	-3.1	3.5	
Total Other Budgeted Capital		11.0	14.8	10.7	-4.1	8.1	
Total Capital Outlay Support		15.5	34.4	34.4	0.0	33.6	
Total Capital Right of Way		1.5	1.5	0.5	-1.0	0.5	
Total Capital Outlay		167.3	179.1	175.0	-4.0	161.9	
Project (BATA) Contingency		19.3	2.5	0.6	-2.0		
Total San Mateo-Hayward Bridge Widening		203.6	217.5	210.5	-7.0	196.0	
San Mateo-Hayward Bridge – West Approach Replacement Planting							
Capital Outlay Support	04860x	0.1	0.1	0.1	0.0	0.0	
Capital Right of Way	048609	0.0	0.0	0.0	0.0	0.0	
Capital Outlay	048604	0.2	0.2	0.2	0.0	0.0	
Project (BATA) Contingency		0.1	0.1	0.1	0.0		
Total SM-H Bridge West Approach Replacement Planting		0.4	0.4	0.4	0.0	0.0	

Notes:

(h) Includes EA 04501*

(i) Includes EA 00305*, 04504*, 04505*, 04506*, 04507*, 04508*, 04509*

BAY AREA TOLL AUTHORITY

Appendix C – Project Cost Summary Details (cont'd)

	EA Number	Baseline Budget Jun-00	Current Budget Jul-04	Current Forecast Jul-04	Net Change	Expended to Date (7/98 – 06/04)	Note
I-880/SR-92 Interchange Improvement							(j)
Capital Outlay Support	23317x	20.8	23.9	35.1	11.2	18.8	
Capital Right of Way	233179	8.0	9.9	9.9	0.0	0.0	
Capital Outlay	233174	70.3	85.2	84.7	-0.5	0.0	
Non-BATA Funding		0.0	9.6	9.6	0.0		
Project (BATA) Contingency		25.1	5.3	10.1	4.8		
Total I-880/SR-92 I/C Improvement		124.2	133.8	149.3	15.5	18.8	
Dumbarton Bridge West Approach Projects							
US101/University Avenue Interchange Reconstruction (non-Caltrans)							
Capital Outlay Support		0.0	0.0	0.0	0.0	0.0	
Capital Right of Way		0.0	0.0	0.0	0.0	0.0	
Capital Outlay		3.8	3.8	3.8	0.0	3.7	(k)
Total US-101/University Avenue		3.8	3.8	3.8	0.0	3.7	
Bayfront Expressway (SR-84) Widening							(l)
Capital Outlay Support	00487x	4.4	8.6	8.6	0.0	7.8	
Capital Right of Way	004879	1.3	0.2	0.2	0.0	0.2	
Capital Outlay	004874	24.8	26.5	26.5	0.0	24.6	
Project (BATA) Contingency		3.3	0.8	0.8	0.0		
Total Bayfront Expressway (SR-84)		33.8	36.0	36.0	0.0	32.6	
Total Southern Bridge Group		365.7	391.4	406.9	15.5	251.1	

Notes:

(j) Includes EA 01601* and 01602*

(k) Total reimbursements made to the City of East Palo Alto for current allocation.

(l) Includes EA 01511* and 01512*

General Notes:

1. Capital outlay support includes both Caltrans and Architectural/Engineering (A/E) consultant support.
2. Capital right of way includes acquisition, loss of goodwill, demolition, utilities relocations, relocation assistance, title costs, and sale of excess lands.
3. Capital outlay includes construction bid items, supplemental construction work, state furnished materials, construction contingencies, and external third party agreements.

PHOTOS



Marina Vista – On-ramp



Marina Vista – Mainline Earthwork



I-680 / I-780 – Soldier Piles on Bayshore Road



Benicia-Martinez Toll Plaza – Canopy Truss Erection



Richmond-San Rafael – Eastbound Sections



Richmond-San Rafael – Westbound Shoulder
